DeKalb County School District | Operations

Project Update Report

Report Date	October 10, 2026
Project Name/Number	Security Vestibule Project – Group I
Facility Name	Area 1, 2, and 3
Area Superintendent	Dr. Beth Kyle, Terri Brown, Ateshia Lester
Principal	Various
School Contact	Various
Project Manager	Laura Flagg
Architect	LS3P
Contractor	LEFKO Group

Scope of Work:

- Update security vestibules for 25 schools within the DCSD.

Subgroup 1: Canby Lane ES, Columbia HS, Lithonia HS, Panola Way ES
Subgroup 2: Browns Mill ES, Cedar Grove HS, Flat Shoals ES, Salem MS
Subgroup 3: Brockett ES, Jolly ES, Stone Mountain MS, Tucker MS
Subgroup 4: Coralwood Education Center, Margaret Harris Comprehensive, McLendon ES, Woodward ES
Subgroup 5: Avondale ES, Dekalb School of Arts, Dunaire ES, Robert Shaw Theme School
Subgroup 6: Chamblee MS, Chamblee HS, Dunwoody HS, Hightower ES, Kingsley ES

Project Construction Budget: $ 18,457,627

Project Schedule Milestones:

- Design Completion – September 2025
- General Contractor Procurement - Ongoing
- Construction Start - June 2026
- Construction End – November 2027

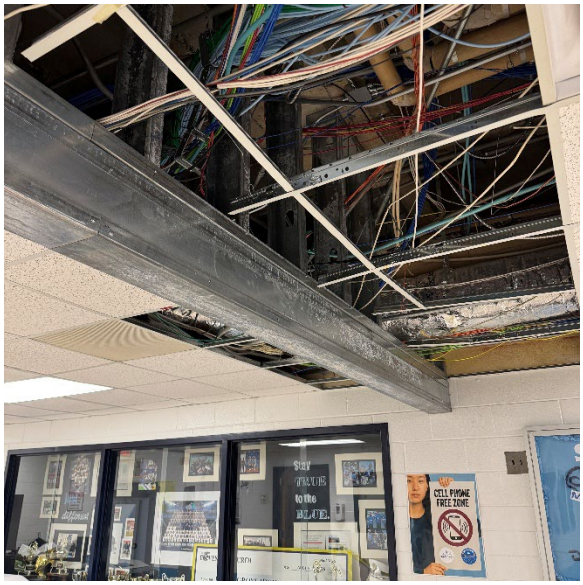
Current Project Status:

- Contractor has completed most of the glazing and film installations for Subgroup 2. Remaining work is awaiting glazing arrival.
- Contractor continues with submittal process and procurement for all subgroups.
- Headers for subgroup 2 was started during Fall Break.
- Headers have been installed and inspected.
- Storefront and door hardware ordered for subgroup 2.

4-Week Look Ahead

- Completion of Phase I for subgroup 2, and schools ready to reopen on 10/13/26.
- Contractor preparing for Subgroup 3.
- Continue with submittal process and procurement for all subgroups.

- **Project Photographs**

	
Flat Shoals ES – Preparation for Header	Cedar Grove HS – Header Installation
	
Browns Mill ES – Header Installation	Salem MS – Header Installation
