
Monthly Progress Report

October 2026

Hempstead Union Free School District (ABGS MS)

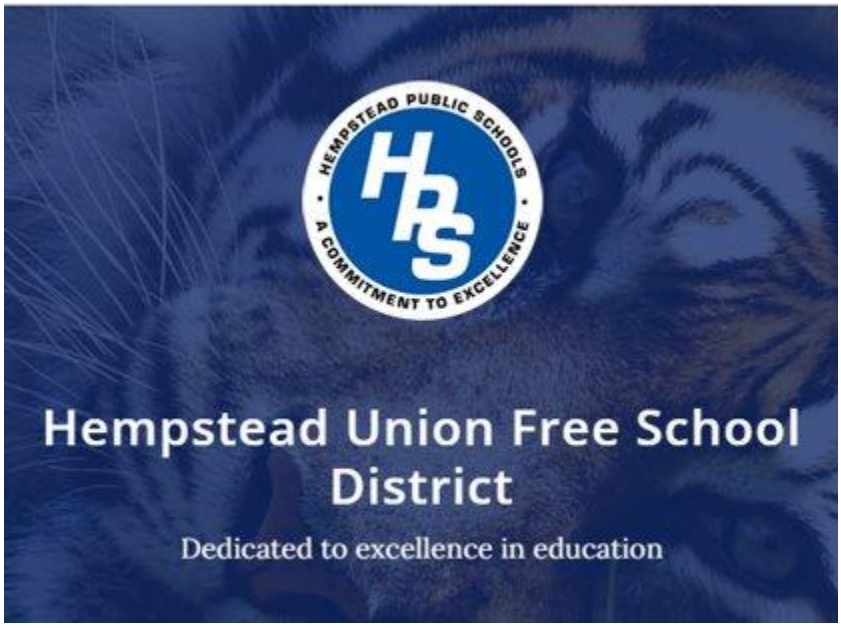

Report prepared by Idris Mashriqi

PARK EAST CONSTRUCTION CORP.

Table of Contents

Section I – Program Summary

Section II – Work Progress October 2026

Section III – Work Projected for November 2026

Section IV – Progress Photos

Section V – Monthly Workforce Summary

Section I – Program Summary
October 2026

- **Hempstead UFSD – ABGS MS**
  - New addition to the existing building.
  - Abatement work throughout the existing building.
  - Classroom upgrades in the existing building.
  - New boilers installation in the existing building.
  - MEP upgrades throughout the existing building.

Section II - Work Progress
October 2026

Hempstead UFSD – ABGS MS

- **VRD:**
  - Started laying out curtain walls.
  - Received window delivery.
  - Started preparing window openings for new windows.
  - Installed densglass on the exterior as needed.
  - Continued framing soffits throughout extension.
  - Installed pencil rod throughout for new ceiling grid.
  - Completed blocking for roof curbs and blocking for roof edge.
  - Started installing 1st layer of roof board and water protectant layer.
  - South wall opening in the Gym, closed.
  - Installed block in north stairwell.
  - Started grading and compacting gym floor to prepare for concrete pour.
- **Relle:**
  - Continued roughing power and lighting wiring in new addition.
- **Hirsch:**
  - Continued installation for water and waste lines.
- **RMS**
  - Continued installing new HW piping and refrigerant on first and second floors ceilings.
  - Continued duct installation throughout new addition.
  - Delivered sound insulation boards for all curbs. Started installing boards.

Section III - Work Planned
November 2026

Hempstead UFSD – ABGS MS

- **VRD:**
  - Continue installing soffits.
  - Continue metal stud framing as needed in new addition.
  - Complete remaining concrete pours in new addition.
  - Complete installation of roofing.
  - Start installation of windows.
- **Relle:**
  - Continue roughing as needed for new addition.
  - Continue pulling wire to all locations.
- **Hirsch:**
  - Continue roughing as needed for new addition.
  - Start sprinkler piping.
- **RMS:**
  - Continue installing piping in boiler room.
  - Continue refrigerant piping and HW piping installation in new addition.
  - Continue with duct work installation in new addition.
  - Rig new roof top units.
  - Deliver and install fan coil units.
  - Start roughing for controls.

Section IV – Progress Photos





Hempstead ABGS MS

Section IV – Progress Photos






Hempstead ABGS MS


Section IV – Progress Photos




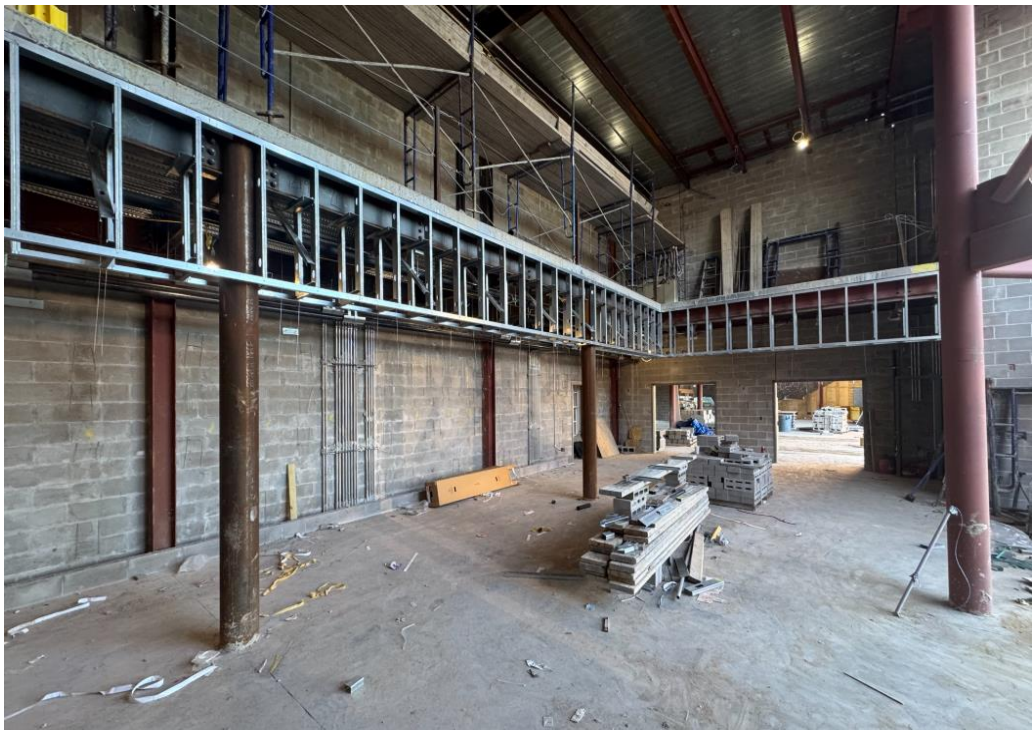

Hempstead ABGS MS

Section IV – Progress Photos

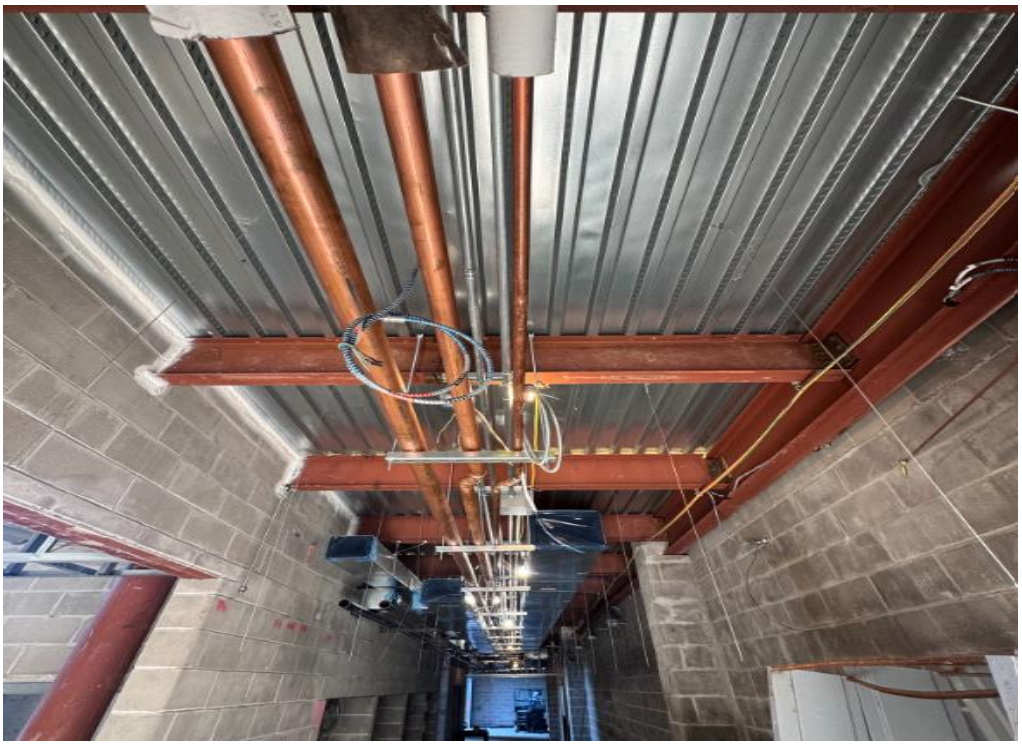


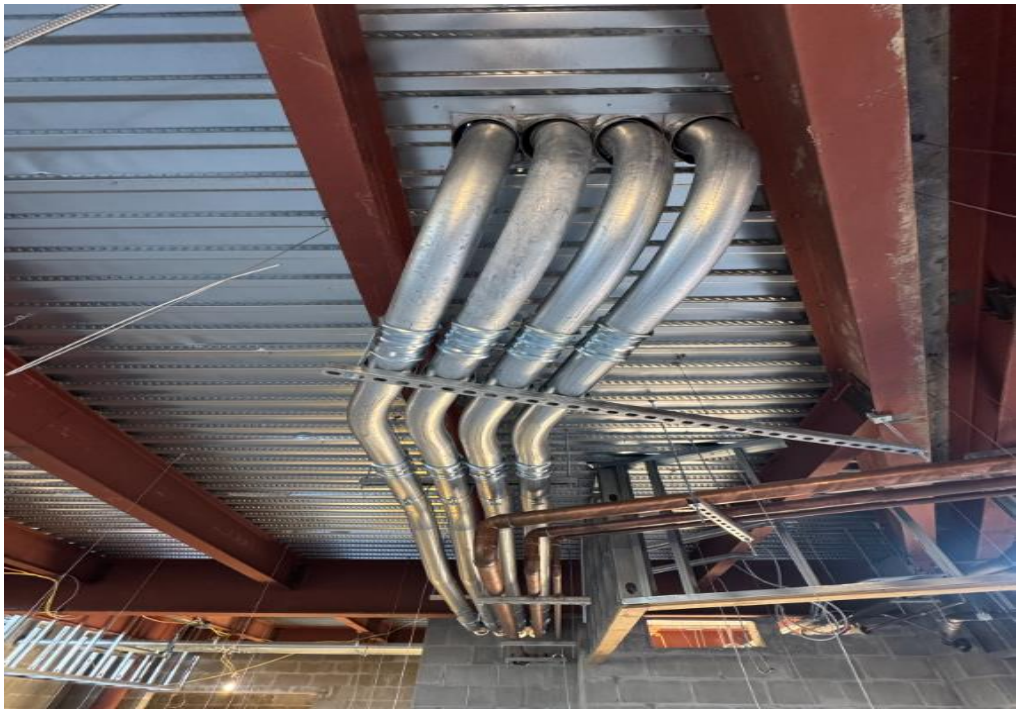

Hempstead ABGS MS


Section IV – Progress Photos




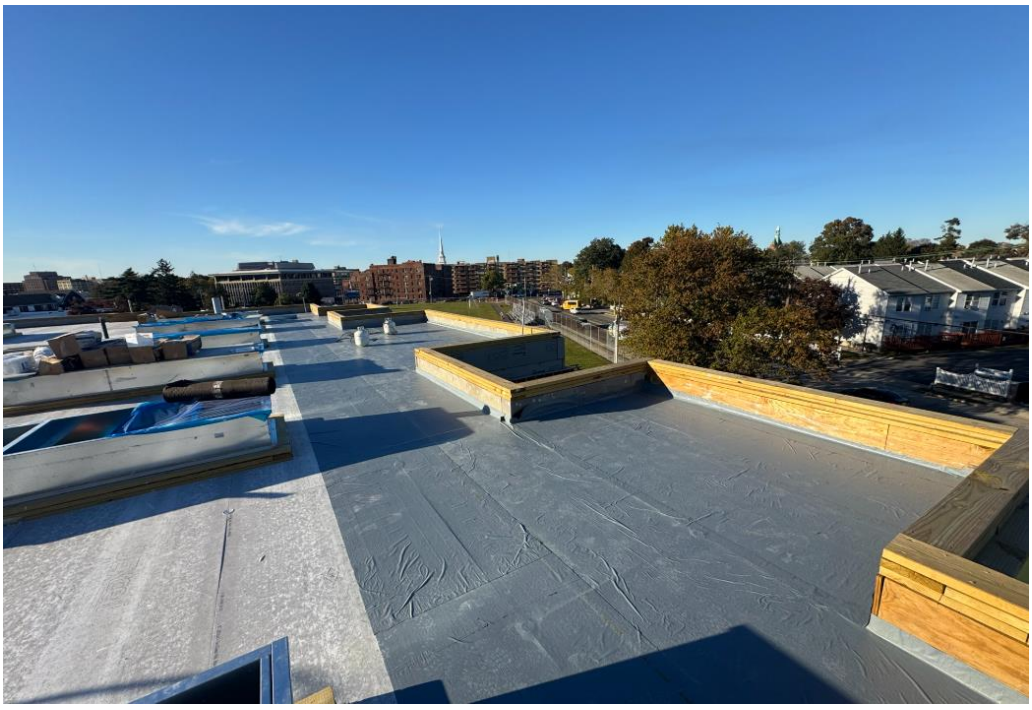

Hempstead ABGS MS

Section IV – Progress Photos

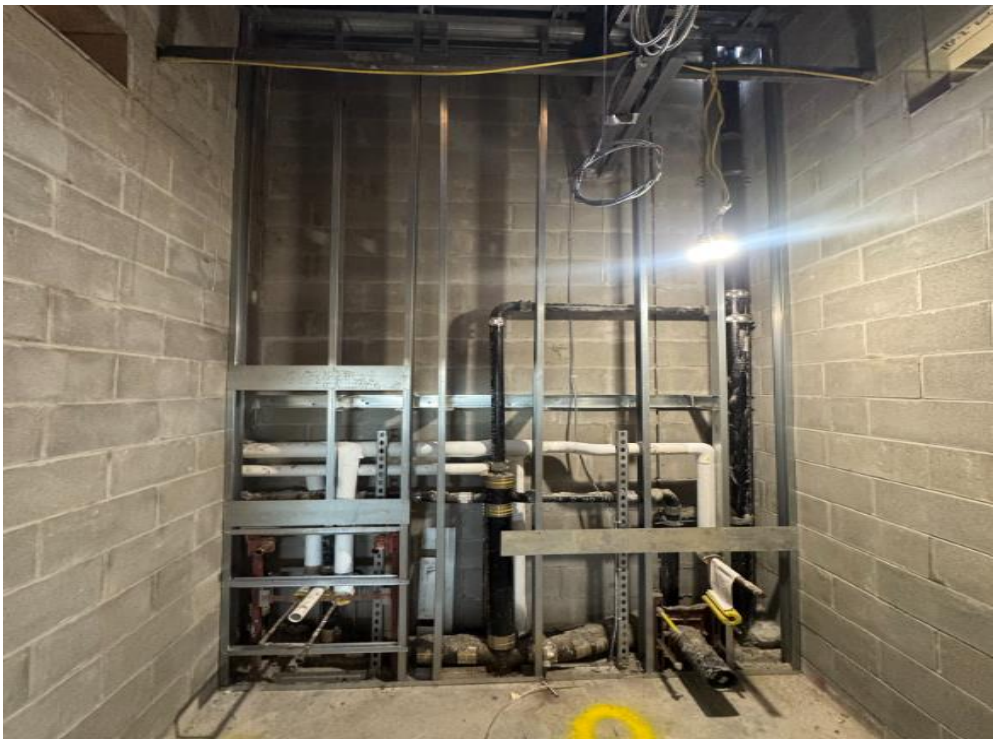

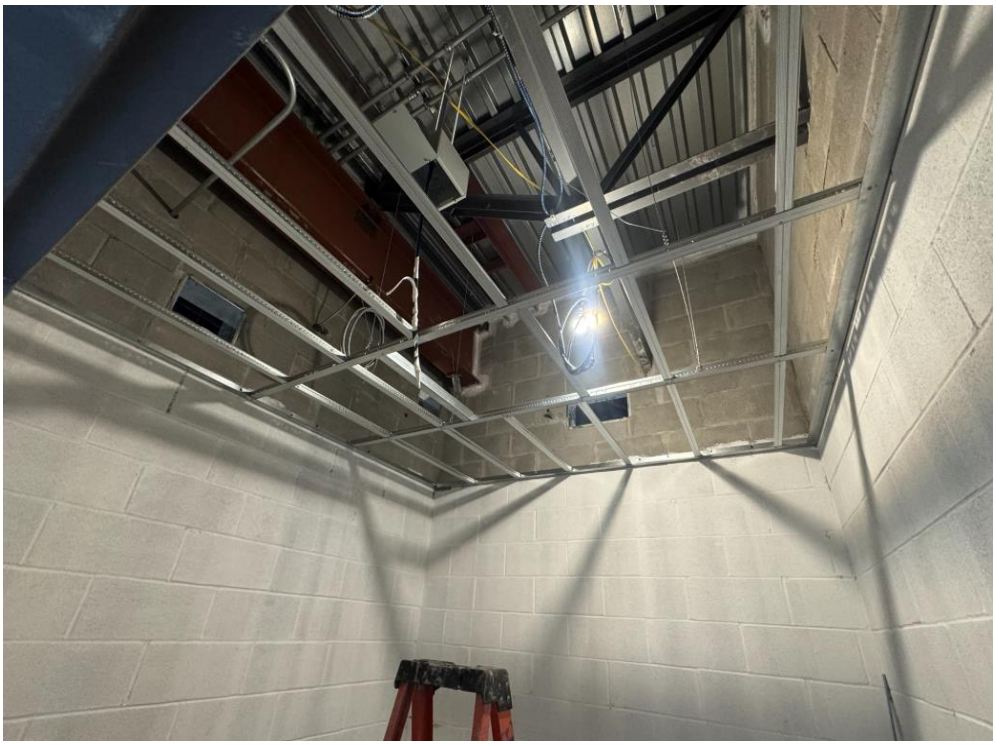


Hempstead ABGS MS

Section V – Workforce Summary – Company/Hours

October 2026

MANPOWER GRAPH

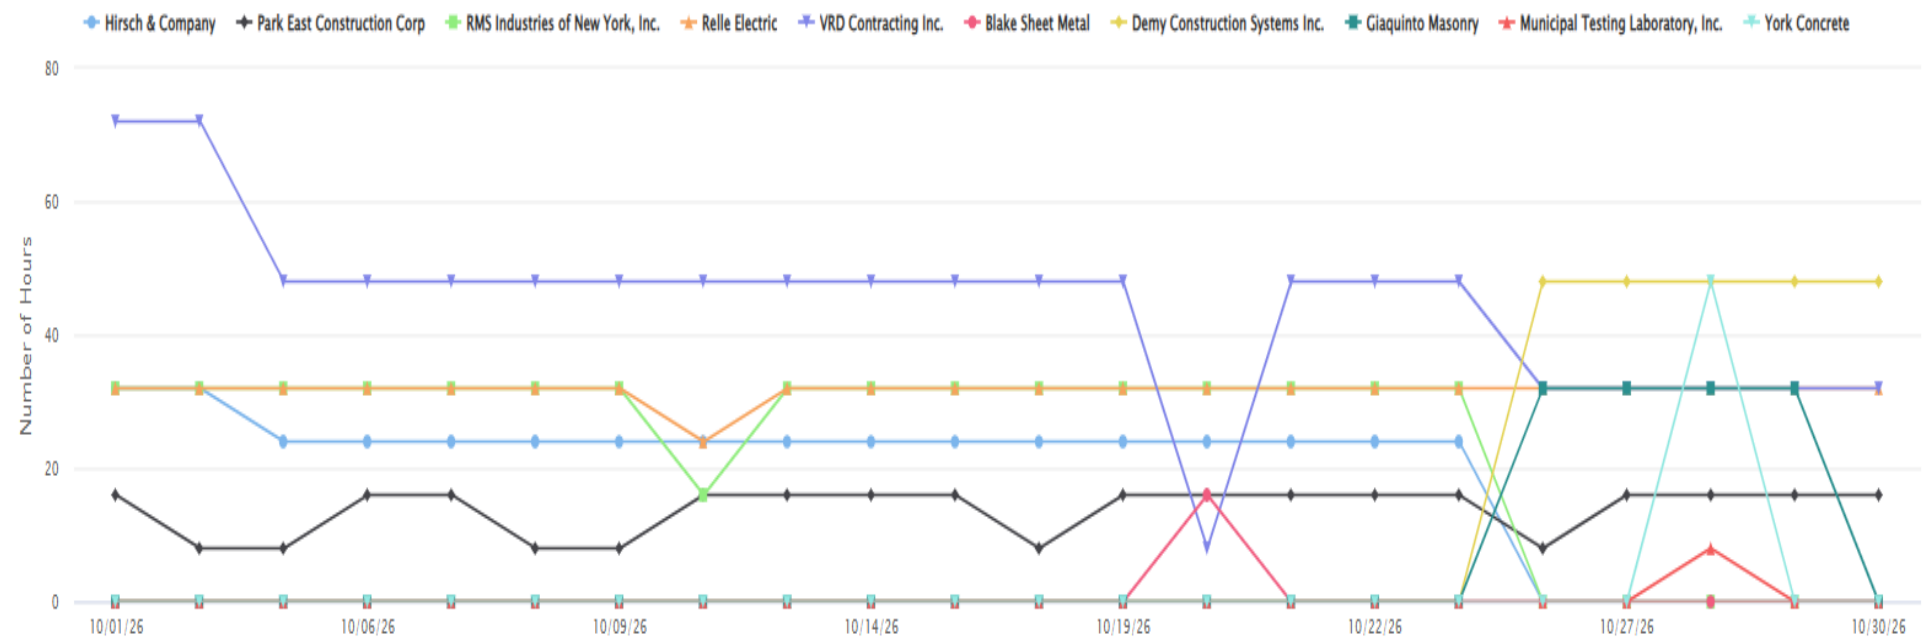

Hempstead ABGS MS

Hempstead Union Free School District (ABGS MS)

October 2026

End of Progress Report
