Hanover Community School Corporation
Construction Projects

Board Report
September 28, 2021



Hanover Community School Corporation
Construction Projects

Board Report
September 28, 2021

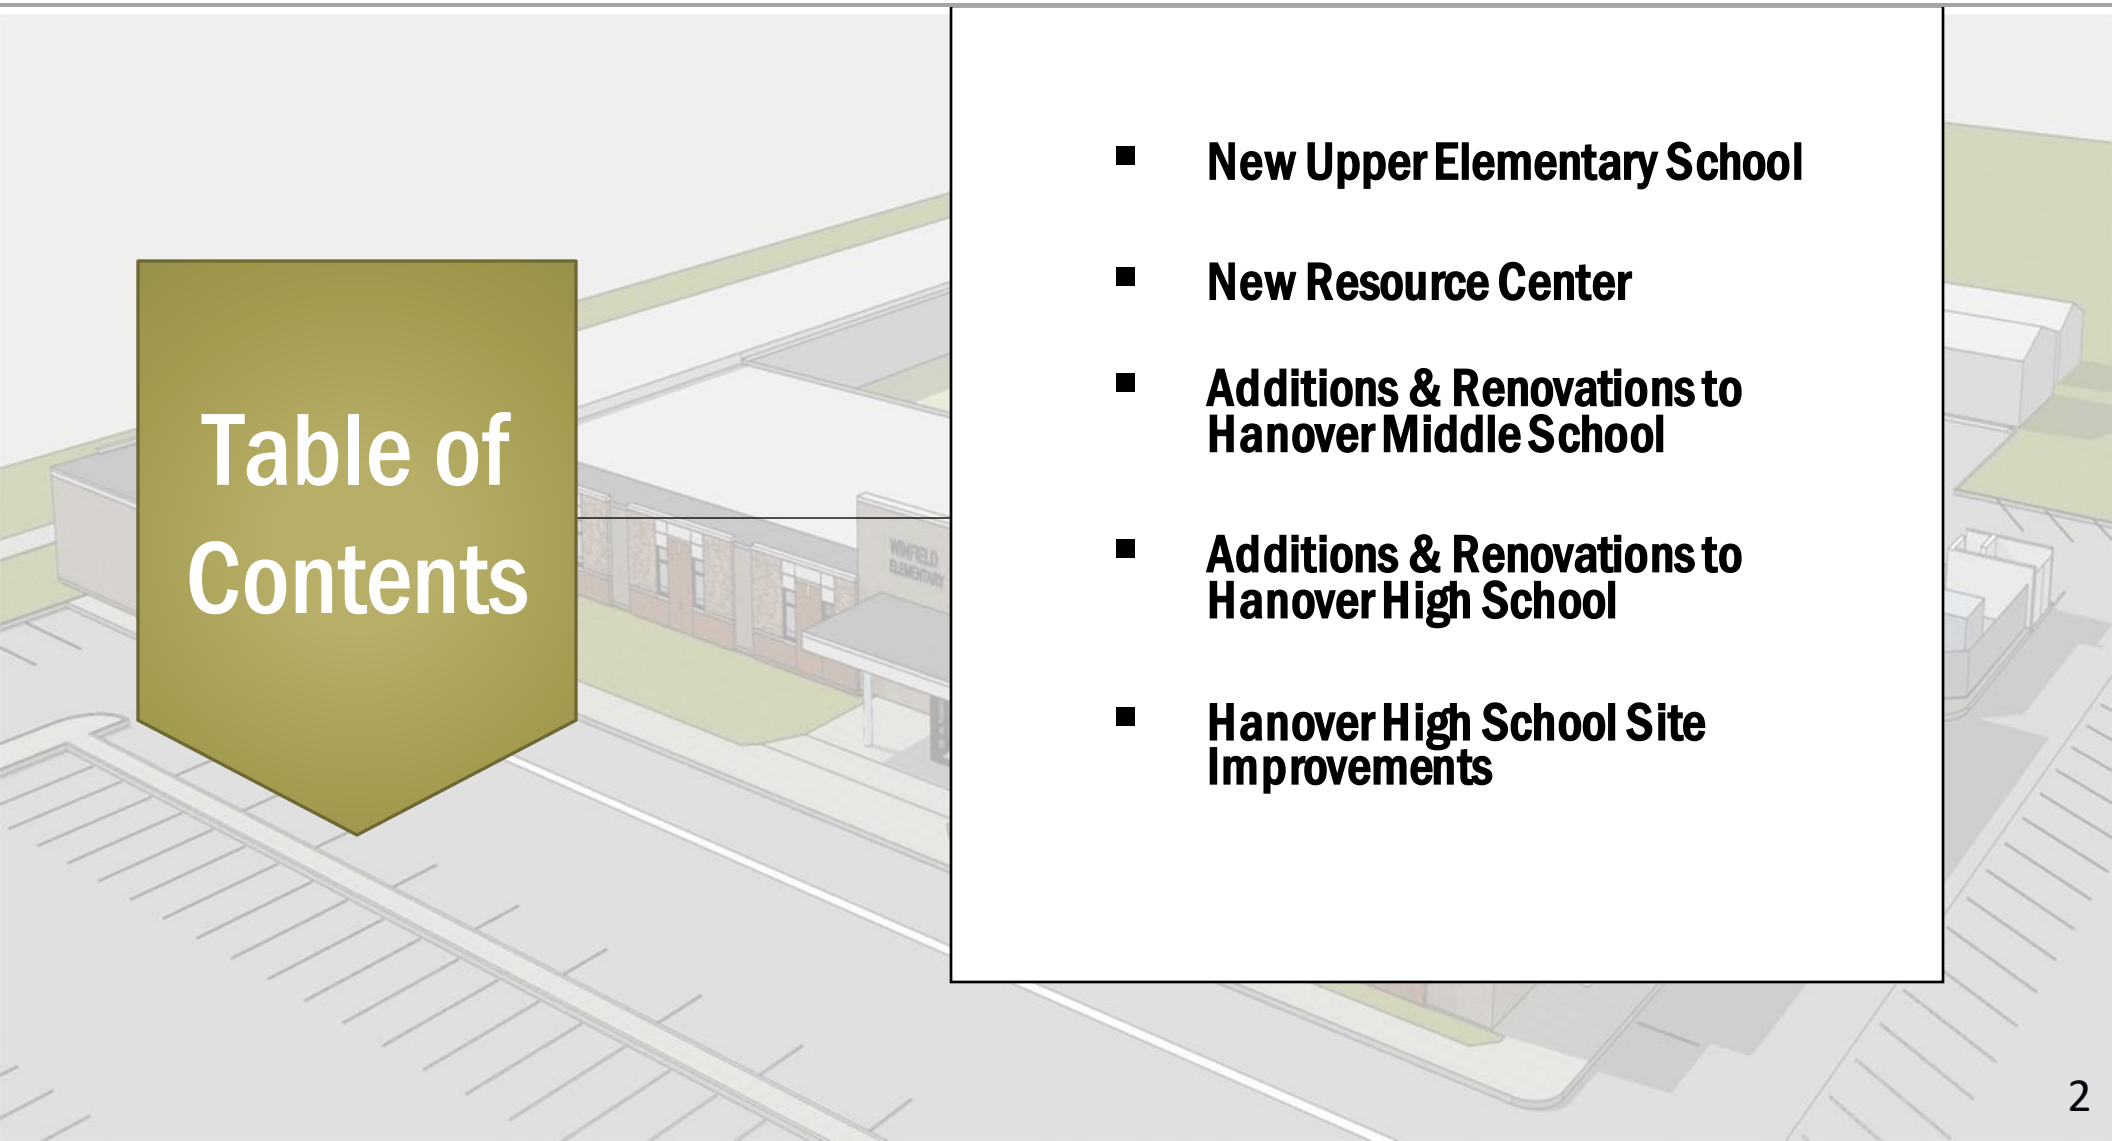


Table of Contents

- New Upper Elementary School
- New Resource Center
- Additions & Renovations to Hanover Middle School
- Additions & Renovations to Hanover High School
- Hanover High School Site Improvements

Progress Photographs



Upper Elementary Receiving Dock

New Upper Elementary:

- Completed structural framing in all areas
- Continued roof joists and deck in academic areas and cafeteria
- Continued slab on grade for academic areas
- Started exterior metal stud walls and sheathing in Admin
- Began electrical rough-ins in Admin
- Poured stage concrete
- Continued masonry interior walls in mechanical spaces and kitchen

Progress Photographs



Upper Elementary Cafeteria/Stage

New Upper Elementary:

Next Four Weeks

- Complete roof joists and deck in academic areas and cafeteria
- Continue exterior metal stud walls and sheathing
- Begin installing interior metal stud walls in Admin
- Continue electrical rough-ins in Admin
- Procuring roofing material

Progress Photographs



Resource Center – Admin Foundations

New Resource Center:

- Continued grading of Resource Center Site
- Began footing and foundations for New Admin Building

Next Four Weeks

- Complete footings and foundations for New Admin Building
- Begin footings and foundations for Bus Garage

Progress Photographs



Middle School Gymnasium and Music Additions

Middle School Additions & Renovations:

- Poured Gymnasium slab on grade
- Completed exterior metal stud and sheathing for Gym Addition
- Completed masonry block walls for Music and Cafeteria Addition
- Installed roof joists for Cafeteria Addition
- Began installing plumbing rough-ins for Gymnasium Restrooms
- Began interior metal studs for Gymnasium/Classroom Addition

Progress Photographs



Middle School Classroom Addition

Middle School Additions & Renovations:

Next Four Weeks

- Complete interior metal studs in Classroom Addition
- Complete plumbing and electrical rough-ins for Gymnasium and Classroom Addition
- Complete roof joists and deck for Music and Cafeteria Addition
- Install roofing materials at all three additions

Progress Photographs



Admin Addition

High School Additions & Renovations:

- Completed slab on grade for Classroom Addition
- Erected structural steel framing for Admin and Classroom Additions
- Began steel roof joists for Admin and Classroom Additions
- Completed drywall in Classroom Renovations
- Began painting in Classroom Renovations

Progress Photographs



Classroom Renovations

High School Additions & Renovations:

Next Four Weeks

- Complete roof joists and deck in Admin and Classroom Additions
- Install exterior stud walls and sheathing for Admin and Classroom Additions
- Begin installing roofing materials for Admin and Classroom Additions
- Install ceilings in Classroom Renovations
- Complete electrical devices in Classroom Renovations
- Begin casework install in Classroom Renovations

Progress Photographs



Locker Room/Concession Stand

High School Site Improvements:

- Completed wood roof trusses and sheathing at locker room building
- Began roof shingles for locker room building
- Installed site lighting at new parking lots
- Completed irrigation install at west practice fields
- Completed bleacher install at practice baseball field

Progress Photographs



West Campus Practice Fields

High School Site Improvements:

Next Four Weeks

- Complete final grades of practice fields
- Install clay infield mix at baseball
- Install plants and seeding
- Complete roofing install at locker room
- Install drywall ceilings in locker room
- Install ductwork in locker room
- Begin painting in locker room
