Witter Field
3-Week Look Ahead Schedule
JULY UPDATE

ID	Task Name	Duration	Start	Finish	Predecessors
1	**3 Week Look Ahead Schedule (JULY UPDATE)**				
2	No Parking Signs (El Cerrito)	23 days	Thu 7/27/23	Mon 8/28/23	
3	Parking Allowed on Palm	5 days	Mon 7/31/23	Fri 8/4/23	2SS
4	No Parking Signs (Palm)	20 days	Mon 8/7/23	Fri 9/1/23	3
5	Encroachment Permit Received	0 days	Fri 8/4/23	Fri 8/4/23	3
6	Field Storm Drainage	10 days	Mon 8/7/23	Fri 8/18/23	5
7	Channel Drains	5 days	Mon 8/21/23	Fri 8/25/23	6
8	Grading at Upper Bleachers	10 days	Tue 7/25/23	Mon 8/7/23	
9	Concrete at Upper Bleachers	9 days	Tue 8/8/23	Fri 8/18/23	8
10	Upper Bleachers Opened for Campus	1 day	Mon 8/21/23	Mon 8/21/23	9

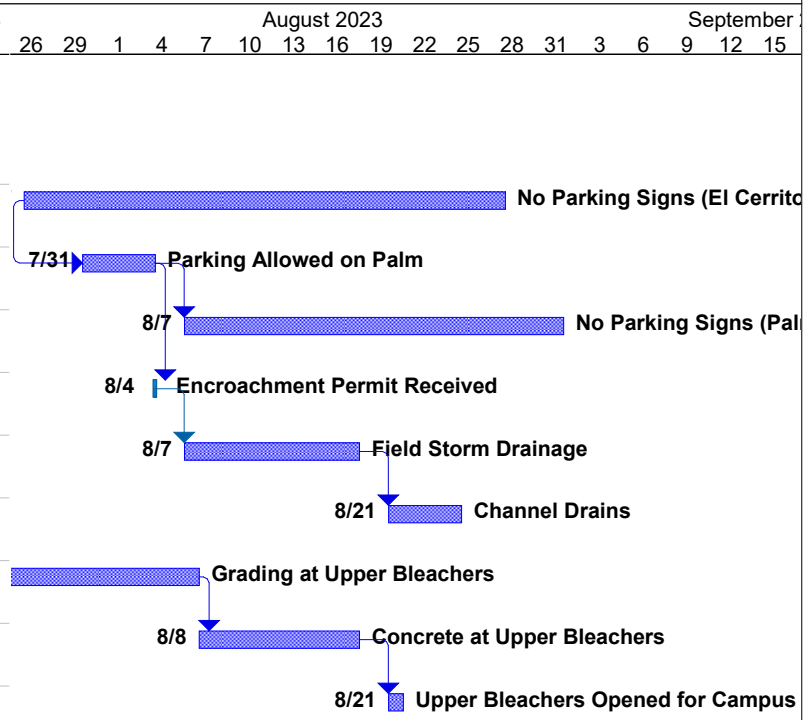

Robert A. Bothman, Inc.
2690 Scott Boulevard, Santa Clara, CA 95050
