School Reopening and Summer 2021 Maintenance & Capital Projects Update

Board of Education Meeting

September 22, 2021

GREAT NECK PUBLIC SCHOOLS

Where Discovery Leads to Greatness

2021 GNPS Summer Programs











GNPS New Teacher Orientation

- Forty-nine (49) teachers attended New Teacher Orientation on August 23
- Program included district presentations from:
  - Board of Education
  - Superintendent & Assistant Superintendents
  - Special Education (PPS)
  - Human Resources
  - District Technology Director
  - Security

New Teacher Orientation











Building Preparation for Opening of Schools





- Furniture is washed
- Rooms are emptied
- Ceiling tiles are changed
- Light fixtures are cleaned
- White boards are cleaned
- Minor maintenance repairs
- Walls are cleaned or painted
- Water fountains are sanitized
- Horizontal surfaces are dusted
- Corridor walls are painted, if needed
- Bathrooms are cleaned and sanitized
- Window blinds are dusted; Windows are washed
- Lockers are cleaned; high school locker combinations are changed
- Corridor floors are cleaned, stripped and waxed
- Floors are stripped of old floor wax; 5-7 coats of new wax is applied
- Gymnasium floors and bleachers are cleaned; floors are screened and polyurethane is applied.

Building Preparation: In-House Maintenance

- Renovated faculty bathroom in teacher's lunch room at Saddle Rock
- Nearly 200 lighting fixtures upgrades from fluorescent to LED in certain areas at JFK, Saddle Rock, North High School
- New smart TV's installed throughout district
- Four rooms at Lakeville were re-painted and new lighting installed
- Kitchen area at Phipps Administration under renovation
- Nearly a dozen classrooms were freshly painted throughout district
- Repaired drainage on South High School baseball field
- Exterior masonry work performed at some sites
- Replaced rotted piping under the pool at North Middle School
- Constructed and delivered over 700 student desks (COVID protocol)
- Installed 3 new stainless steel trough sinks for art rooms at North High School
- Replaced two original electrical panels at Parkville School
- Installed multiple new window air conditioner units throughout the district

Building Preparation: Outside Vendor Work

- New floors installed in several rooms at North High School
- The large gym floor at North High School was sanded, new game lines and center court logo painted and polyurethane applied
- Ten new doors were installed at Parkville School
- The South Complex kitchen manager's office floor tile was abated and replaced
- New ductless split air conditioner installed in art room at South High School
- Two new ductless split air conditioners were installed in rooms at North Middle School
- New intrusion door alarms are being installed at all buildings (still in progress)
- Tree work maintenance and removal performed in district

Summer 2021 Construction Projects

Our busiest time of year…


Clover Drive

Sitework

- New asphalt parking lot underway
- New entrance, curbs, road, walkways and drainage





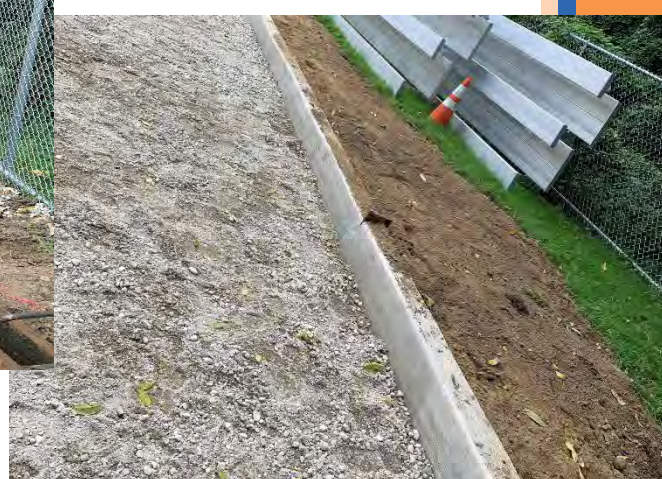

E.M. Baker Elementary

- Construction of a new auditorium completion date November
- Cafeteria expansion
- New bathrooms
- Nurse's office renovation





Lakeville Elementary

Reading Room

- Complete renovation and remodel
- Two new HVAC units will be installed next month





Lakeville Elementary

New PA system should be ready by November

- New PA rack
- New speakers to be installed
- New equipment pending installation







North Middle School

FACS room

- Complete renovation of FACS room (Family & Consumer Science)
- Remodel includes new appliances, furnishings, ceilings, and epoxy floors



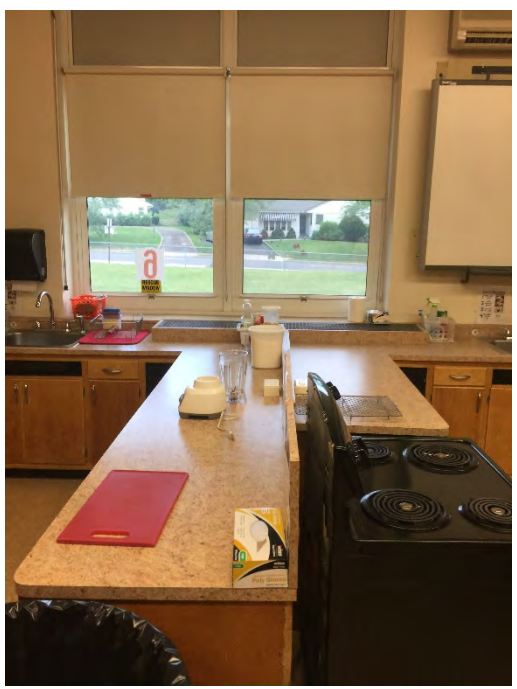

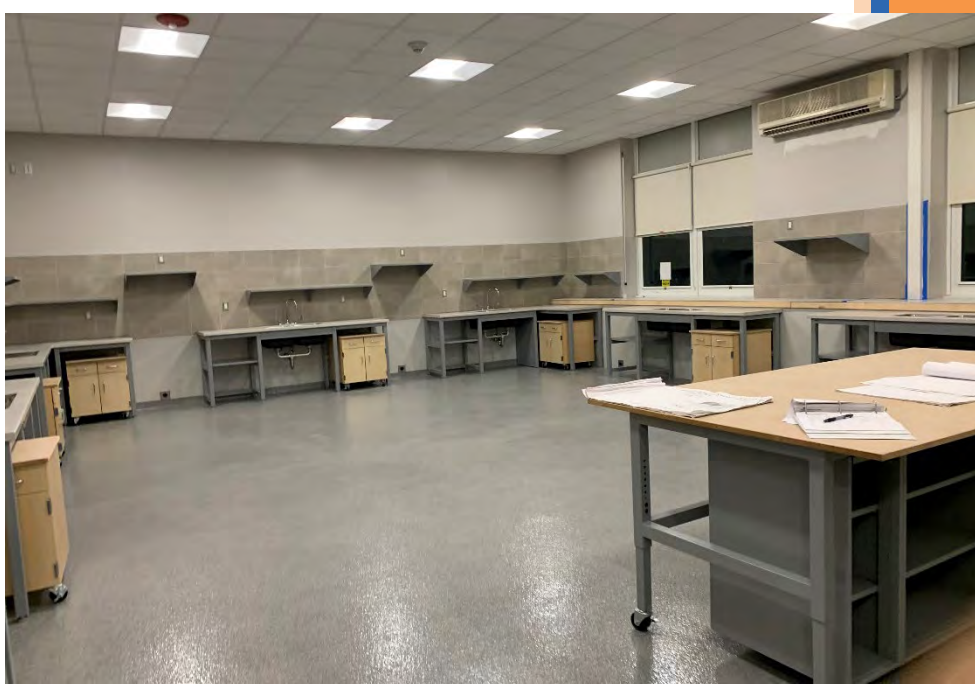

North Middle School

Library Renovation

- New ceilings, carpet and luxury vinyl tile (LVT) flooring
- Glass enclosed office
- Audio-visual, makerspace room
- Renovated Librarian's Office





North Middle School

Masonry restoration & window replacement

- Brick removal
- Structural backwall repair and reinforcement
- New brick installation
- New window and glass block installations





Saddle Rock Elementary

Library renovation

- Renovation of library, room 35 and makerspace room
- New furnishings and lighting fixtures on order
- New ceilings, carpeting and luxury vinyl tile (LVT) flooring
- Glass partition walls





Saddle Rock Elementary

Asphalt replacement and new drainage

- New asphalt replaced for two parking lots and one playground surface
- New leaching pools and catch basin
- New exterior lighting and concrete piers in upper parking lot





Saddle Rock Elementary

New roof top unit

- Roof top unit (RTU) will provide heating and air-conditioning for auditorium
- Delivery of RTU has been delayed





Pending RTU installation

South Middle & High Schools

Phase II of the window replacement project

- Window installation for gymnasiums, natatorium, hallways and corridors
- Kalwall translucent panel windows for natatorium (indoor swimming pool)





South Middle & High Schools

Heating plant improvements

- Replacement of old vacuum and condensate pumps and tanks in boiler room
- New equipment installed





Special Thanks To…

- Alfredo Cavallaro, Director of Facilities
- Steve Challis, Supervisor of School Facilities & Operations
- Dr. Joseph Hickey, Assistant Superintendent
- Maintenance, Custodial and Building & Grounds Crew
- District architects and engineers at BBS
- Construction managers at Savin Engineers




WELCOME BACK !
