Long Range Facility Master Plan

Addendum 01

Transitional Kindergarten Facility Plan

Fontana Unified School District
01-27-2023

Executive Summary

In the summer of 2022, the Fontana USD engaged PBK to assist with analyzing how the newly added Transitional Kindergarten (TK) grade level by the State of California would impact the existing school facilities at Fontana Unified School District. This initial study focuses mainly on capacity at each school site and how projected enrollment for TK students will impact each site.

This expanded Transitional Kindergarten initiative is to include all 4-year-olds incrementally into the TK classrooms. This phased implementation started in the 2022-23 school year and will continue through the 2025-26 school year. The requirements outlined by the State of California indicate that any classrooms used for the TK program must meet the Title 5 requirements, similar to Kindergarten classrooms. An analysis of the existing capacity, projected TK enrollment, and how to address needs conceptually, was needed.

PBK, in collaboration with the Fontana USD Facilities Department, reviewed existing and projected data to understand how each site will be impacted. Conceptual solutions were proposed that would help address TK needs at each site. Conceptual project costs were also identified to assist the district with planning exercises. An implementation approach was also identified and prioritized based on funding application submittals.

The findings of this report identified eight (8) schools that will be impacted sooner than other sites. The district has prioritized those funding applications submittals. A closer look at the funding outlook is found on the next page. The proposed solutions identified to address this increased TK student enrollment include the reconfiguration of classrooms to provide a compliant TK classrooms. Another approach could be the addition of new buildings to accommodate this new grade level. The use of portable classrooms to satisfy this projected TK enrollment growth does not meet the requirements outlined by the State of California.

It is recommended that the Fontana USD continue monitoring projected TK enrollment figures to assist with planning. A more detailed architectural design analysis should also be done at the group of eight (8) schools that will be impacted sooner to identify in further detail how each site will address the added students. Specifically identify which classrooms to reconfigure or where new additions will be located. These efforts will help the Fontana USD be better prepared when these new TK students arrive in larger numbers.

In April 2022, the first UPK funding round window for approximately $225 million opened up with the Office of Public School Construction (OPSC). Fontana USD submitted applications for the following projects:

1. Sierra Lakes Elementary School
2. Cypress Elementary School
3. Palmetto Elementary School
4. Oleander Elementary School
5. Hemlock Elementary School
6. Grant Elementary School
7. Mango Elementary School
8. Beech Elementary School

The second funding round for approximately $360 million is scheduled for February 1, 2023 - March 2, 2023. The following sites have identified for application submittal.

1. South Tamarind Elementary School
2. Randall Pepper Elementary School
3. West Randall Elementary School
4. Canyon Crest Elementary School
5. Date Elementary School
6. North Tamarind Elementary School
7. Redwood Elementary School
8. Juniper Elementary School

The Governor's fiscal year 2022-2023 budget provided a one-time General Fund amount of $100 million. The Governor had planned on allocating an additional $550 million for the fiscal year 2023-2024 for TK, full-day Kindergarten, and Preschool facilities but the most recent budget updates in January 2023 show that being postponed until the 2024-2025 fiscal year. The commitment from the Governor to provide operational costs to support this UPK implementation appears to be softening per latest reports.

Fontana USD will continue to submit applications in efforts of obtaining any funding that is made available by the state.

UPK STATE FUNDING OUTLOOK

FONTANA
UNIFIED SCHOOL DISTRICT

2022-2023 Elementary School Attendance Areas

Elementary Schools
Streets
Highways
RR

ELEMENTARY ATTENDANCE AREAS

- Almond
- Beech Avenue
- Canyon Crest
- Chaparral
- Citrus ES
- Cypress
- Date
- Dolores Huerta
- Dorothy Grant
- Hemlock
- Juniper
- Kathy Binks
- Live Oak
- Locust
- Mango
- Maple
- North Tamarind
- Oak Park
- Oleander
- Palmetto
- Poplar
- Primrose
- Randall-Pepper
- Redwood
- Shadow Hills
- Sierra Lakes
- South Tamarind
- Ted J. Porter
- Tokay
- West Randall

Dolores Huerta - no attendance boundary

NORTH

LYTLE CREEK RD
DUNCAN CANYON RD
CASA GRANDE RD
SUMMIT AVE
SIERRA LAKES ELEM K-5
SIERRA LAKES PKY
W HIGHLAND AVE
S HIGHLAND AVE
WALNUT AVE
WALNUT ST
W WALNUT ST
DOROTHY GRANT ELEM K-5
BASELINE AVE
W BASE LINE RD
KATHY BINKS ELEM K-5
MANGO ELEM TK-5
LOCUST ELEM TK-6
MILLER AVE
HEMLOCK ELEM TK-5
JUNIPER ELEM TK-5
PRIMROSE ELEM K-5
TOKAY ELEM TK-5
NORTH TAMARIND ELEM TK-6
FOOTHILL BLVD
ALMOND ELEM TK-6
TED PORTER ELEM TK-5
ARROW BLVD
SOUTH TAMARIND ELEM TK-5
WHITTRAM AVE
REDWOOD ELEM TK-6
OLEANDER ELEM TK-5
DOLORES HUERTA INT. ACADEMY K-6
MERRILL AVE
WEST RANDALL ELEM TK-6
DATE ELEM TK-5
RANDALL-PEPPER ELEM TK-5
MAPLE ELEM TK-5
W RANDALL AVE
RANDALL AVE
BEECH ELEM K-6
CITRUS ELEM K-6
PALMETTO ELEM K-5
LIVE OAK ELEM TK-6
CYPRESS ELEM K-5
VALLEY BLVD
POPLAR ELEM TK-6
W VALLEY BLVD
SLOVER AVE
SANTA ANA AVE
JURUPA AVE
E JURUPA ST
CHAPARRAL ELEM K-5
SHADOW HILLS ELEM TK-5
MARLAY AVE
LIVE OAK AVE
CANYON CREST ELEM TK-5
OAK PARK ELEM TK-5

15
210
10

SIERRA AVE
CYPRESS AVE
CITRUS AVE
KNOX AVE
LYTLE CREEK RD
CHERRY AVE
JUNIPER AVE
MANGO AVE
TAMARIND AVE
ALMERIA AVE
ETIWANDA AVE
REDWOOD AVE
HEMLOCK AVE
LIME AVE
OLEANDER AVE
LOCUST AVE
N LINDEN AVE
ALMOND AVE
ALDER AVE
POPLAR AVE
MAPLE AVE
LARCH AVE
LAUREL AVE
CEDAR AVE
LINDEN AVE
PALMETTO AVE
CALABASH AVE
BANANA AVE
BEECH AVE
N ETIWANDA AVE

0 0.375 0.75 1.5 2.25 3 Miles

BOUNDARIES APPROVED APRIL 2018

5/31/2022 jm

Methodology for Fall 2021/2022 Projections

District-Wide Resident Transitional Kindergarten Student Projections

	Actual	Projected TK Students			Projection Date 10/06/2021		
	SY2021	SY2022	SY2023	SY2024	SY2025	SY2026	SY2027 SY2028
TK	400	631	861	1081	1467		

Resident Transitional Kindergarten Student Projections by Elementary

Elementary Attendance Area	Actual SY2021	Projected TK Students SY2022	SY2023	SY2024	Projection Date 10/06/2021 SY2025	SY2026	Rooms@20	Existing TK Rms	Future Planned TK Rms	Priority	Proposed Solution	Projected Conceptual Costs	Proposed Solutions A	B
Almond Elementary	15.00	23.80	32.40	41.20	55.90	55.90	2.80	1.00			B	$ 2,109,375	0	$ 2,109,375
Beech Ave Elementary	10.00	15.90	21.60	27.50	37.30	37.30	1.87	-	1.00	1	A	$ 1,476,563	$ 1,476,563	0
Canyon Crest Elementary	12.00	19.20	26.00	34.00	45.50	45.50	2.28	-	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Chaparral Elementary	12.00	19.20	26.00	34.00	45.50	45.50	2.28	-			B	$ 2,109,375	0	$ 2,109,375
Citrus Elementary	12.00	19.00	26.00	33.00	44.70	44.70	2.24	-			B	$ 2,109,375	0	$ 2,109,375
Cypress Elementary	22.00	35.00	47.60	60.80	82.30	82.30	4.12		3.00	1	A	$ 3,164,063	0	$ 3,164,063
Date Elementary	12.00	19.00	26.00	33.00	44.70	44.70	2.24	1.00	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Dorothy Grant	11.00	16.70	22.90	27.50	37.50	37.50	1.88	-	2.00	1	A	$ 2,953,125	$ 2,953,125	0
Hemlock Elementary	15.00	22.80	31.30	37.50	51.10	51.10	2.56	1.00	2.00	1	A	$ 2,953,125	$ 2,953,125	0
Juniper Elementary	10.00	15.20	20.80	25.00	34.10	34.10	1.71	-	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Kathy Binks Elemenetary	14.00	21.30	29.20	35.00	47.70	47.70	2.39	-			B	$ 2,109,375	0	$ 2,109,375
Live Oak Elementary	16.00	25.40	34.60	44.00	59.60	59.60	2.98	1.00			C	$ -	0	0
Locust Elementary	11.00	16.70	22.90	27.50	37.50	37.50	1.88	-	1.00		A	$ 1,054,688	0	$ 1,054,688
Mango Elementary	10.00	15.20	20.80	25.00	34.10	34.10	1.71	-	1.00	1	A	$ 2,953,125	$ 2,953,125	0
Maple Elementary	18.00	30.20	41.30	53.20	72.90	72.90	3.65	1.00			B	$ 1,484,375	0	$ 1,484,375
North Tamarind Elementary	13.00	19.70	27.10	32.50	44.30	44.30	2.22	-	1.00	2	B	$ 2,109,375	0	$ 2,109,375
Oak Park Elementary	12.00	19.20	26.00	34.00	45.50	45.50	2.28	1.00			C	$ -	0	0
Oleander Elementary	19.00	30.20	41.10	52.20	70.80	70.80	3.54	1.00		1	B	$ 2,109,375	0	$ 2,109,375
Palmetto Elementary	18.00	28.60	38.90	49.50	67.10	67.10	3.36	-	3.00	1	A,B	$ 4,007,813	$ 2,953,125	$ 1,054,688
Poplar Elementary	14.00	22.20	30.30	38.50	52.20	52.20	2.61	1.00			B	$ 1,484,375	0	$ 1,484,375
Primrose Elementary	8.00	13.50	18.50	23.60	32.50	32.50	1.63	-			B	$ 2,109,375	0	$ 2,109,375
Randall Pepper Elementary	17.00	27.00	36.80	46.70	63.40	63.40	3.17	1.00	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Redwood Elementary	11.00	17.50	23.80	30.20	41.00	41.00	2.05	-	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Shadow Hills Elementary	6.00	9.60	13.00	17.00	22.80	22.80	1.14	1.00			C	$ -	0	0
Sierra Lakes Elementary	21.00	31.90	43.80	52.50	71.60	71.60	3.58	-	2.00	1	B	$ 2,109,375	0	$ 2,109,375
South Tamarind Elementary	18.00	28.60	38.90	49.50	67.10	67.10	3.36	1.00	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Ted Porter Elementary	13.00	21.60	29.50	37.90	51.80	51.80	2.59	2.00			C	$ -	0	0
Tokay Elementary	17.00	25.80	35.40	42.50	57.90	57.90	2.90	2.00			C	$ -	0	0
West Randall Elementary	13.00	20.60	28.10	35.70	48.50	48.50	2.43	1.00	1.00	2	B	$ 1,054,688	0	$ 1,054,688
Totals	400.00	630.60	860.60	1,080.50	1,466.90	1,466.90	**73.35**	**16.00**	**23.00**			**$ 45,789,063**	**$ 13,289,063**	**$ 32,500,000**
Change		230.60	230.00	219.90	386.40				39.00					
Required Classroom (24/20)	16.67	26.28	43.03	54.03	73.35	73.35								
Average for 30 Schools	13.33	21.02	28.69	36.02	48.90	48.90	2.44							
Average for 15 Schools	26.67	42.04	57.37	72.03	97.79	97.79	4.89							
Average for 18 Schools	22.22	35.03	47.81	60.03	81.49	81.49	4.07							

Priority		Proposed Solution:	
1	First Round of Funding Application	A	Addition of Building(s)
2	Second Round of Funding Application	B	Major Reconfiguration/Modernization
		C	No Construction Needed

Note: Priority determined by anticipated need.

Notes:
Conceptual Costs are shown as total project costs. No escalation included at this time.
Addition of Building assumed at $700/sf.
Reconfiguration/Modernization assumed at $500/sf.
Direct Construction marked up 25% for Total Construction Cost.
Total Construction Cost marked up 25% for Soft Costs.

District-Wide UPK Projections

Fontana Unified School District
01-27-23



EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **0 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**


Priority 1

UPK Analysis
Sierra Lakes Elementary School

5740 Avenal Pl., Fontana, CA 92336

Fontana Unified School District

01-27-23

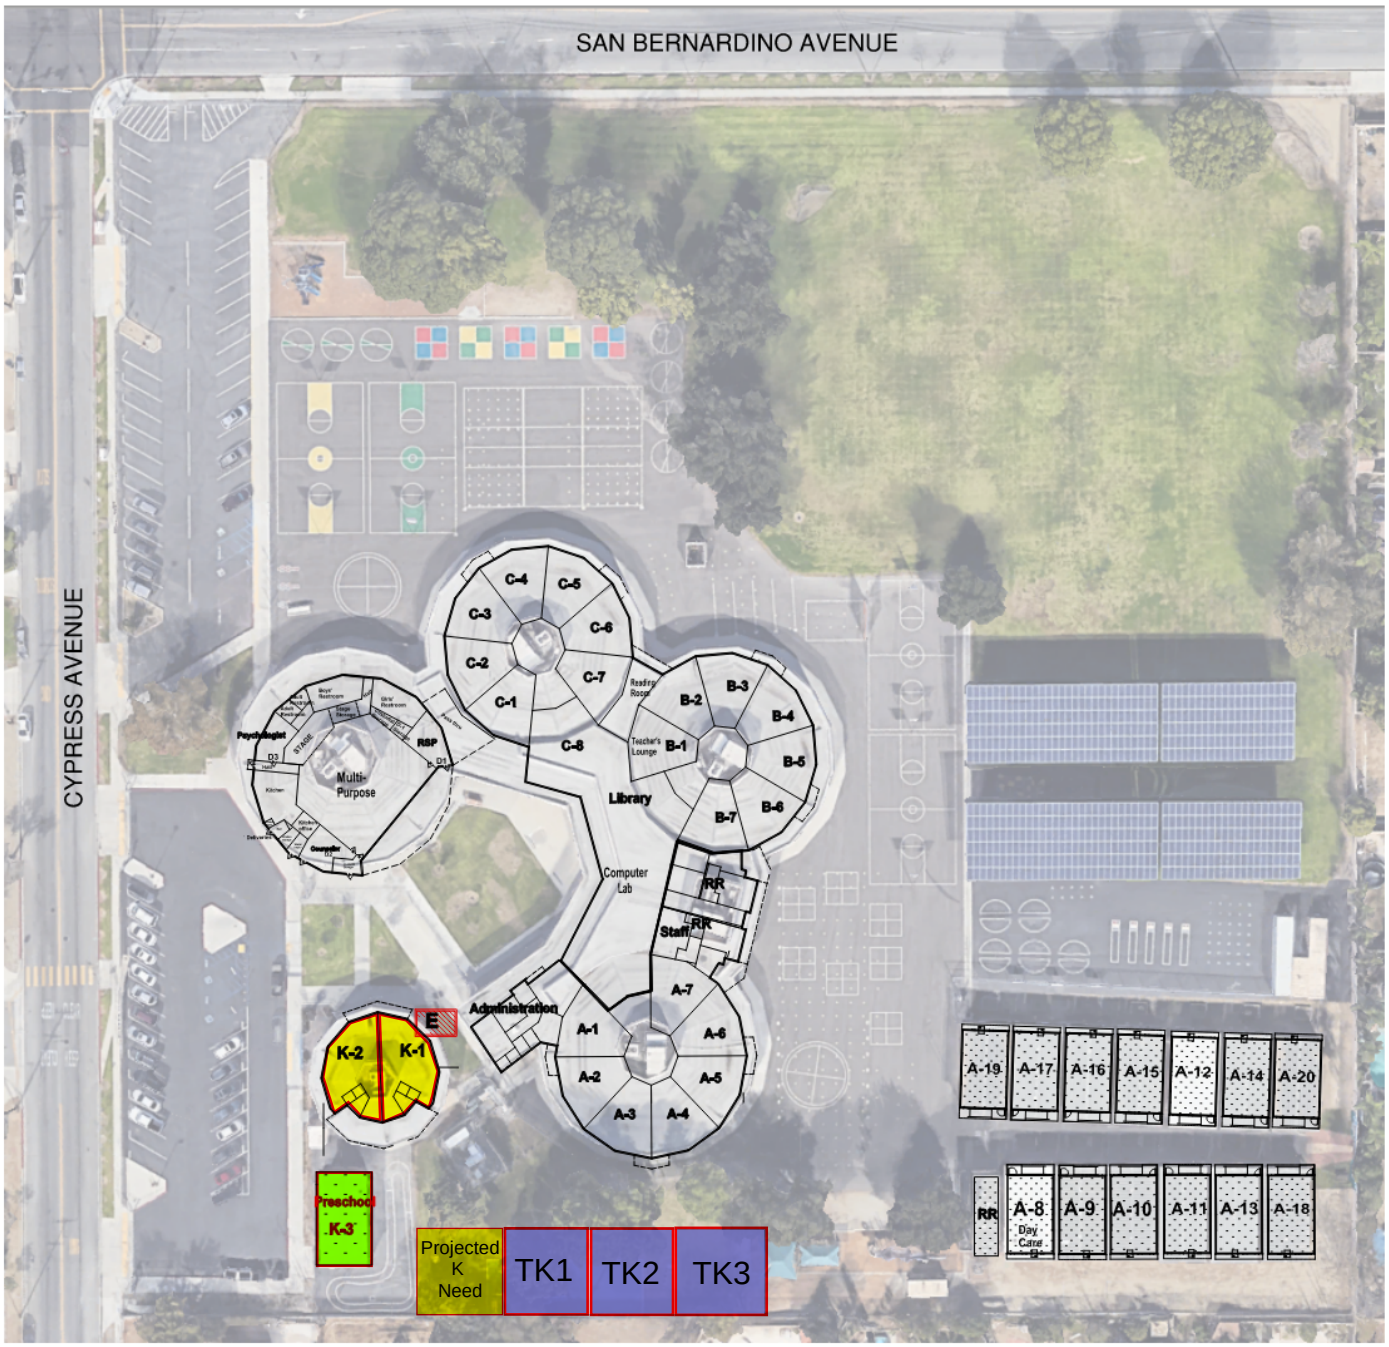

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **3 TOTAL**


Priority 1

UPK Analysis
Cypress Elementary School

9751 Cypress Ave., Fontana, CA 92336

Fontana Unified School District

01-27-23

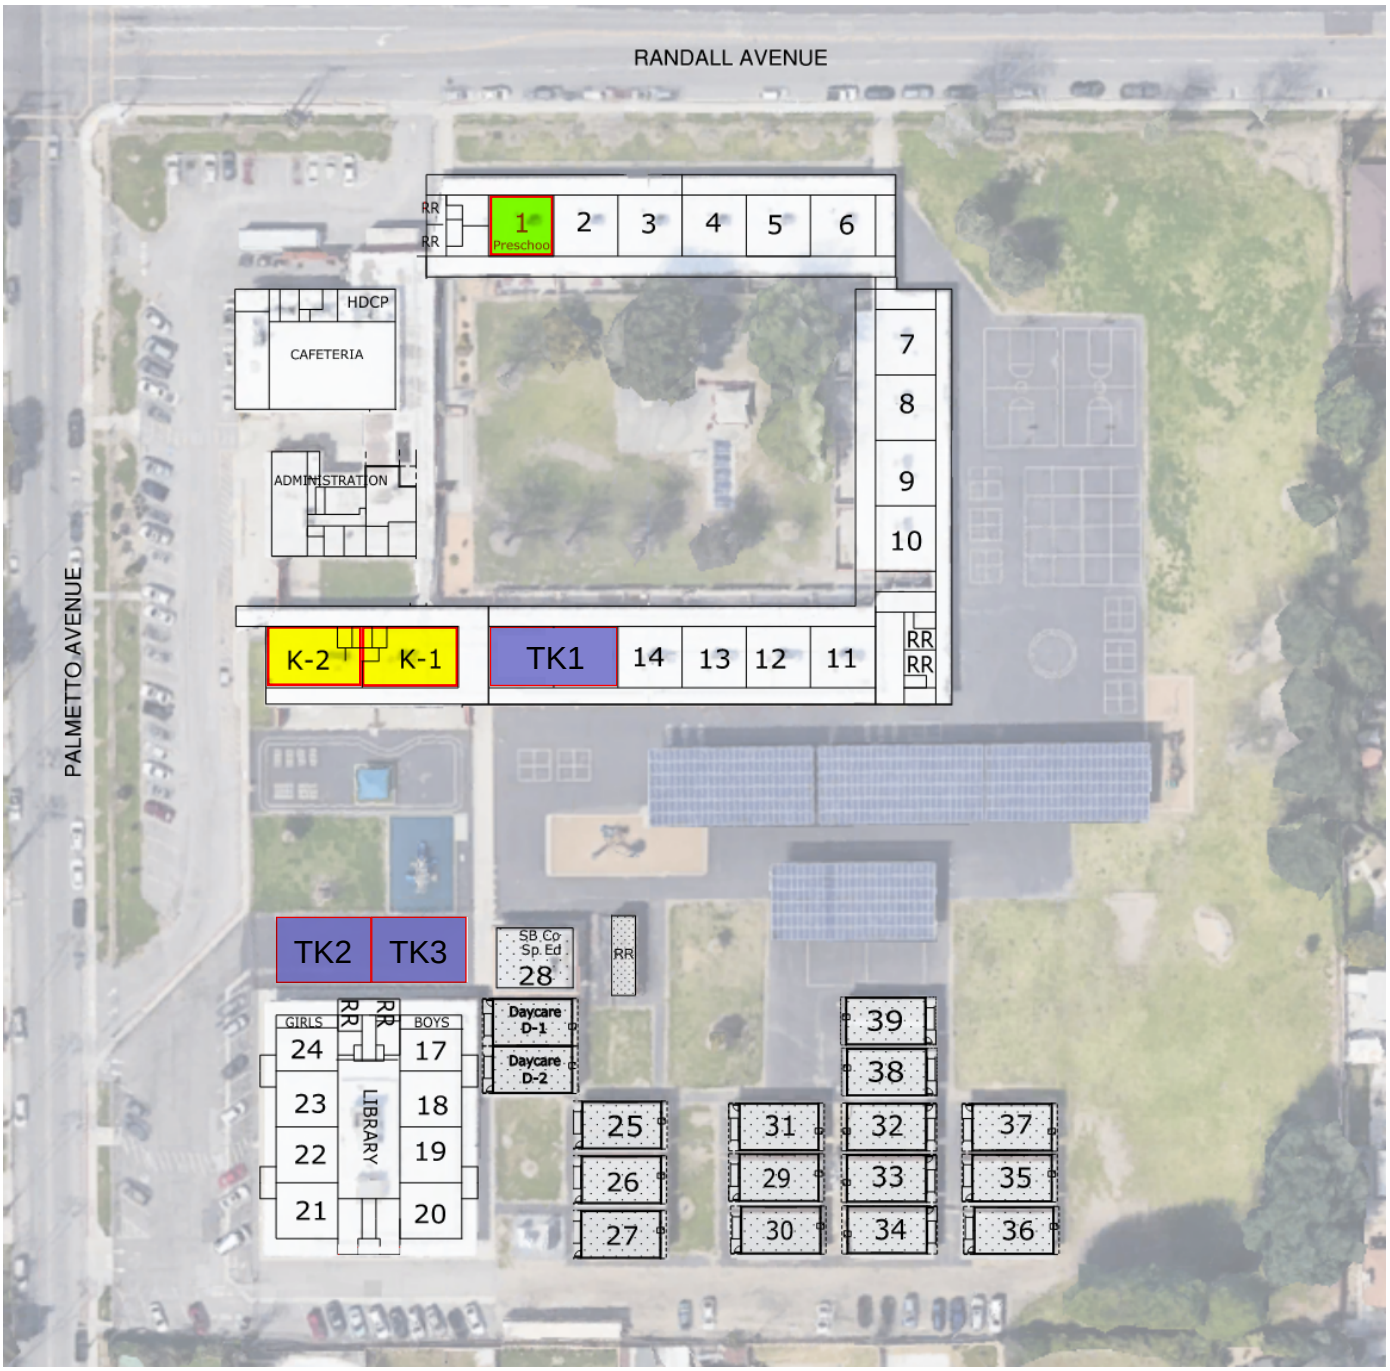

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **3 TOTAL**

Priority 1

UPK Analysis
Palmetto Elementary School

9325 Palmetto Ave, Fontana, CA 92335

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**


Priority 1

UPK Analysis
Oleander Elementary School

8650 Oleander Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

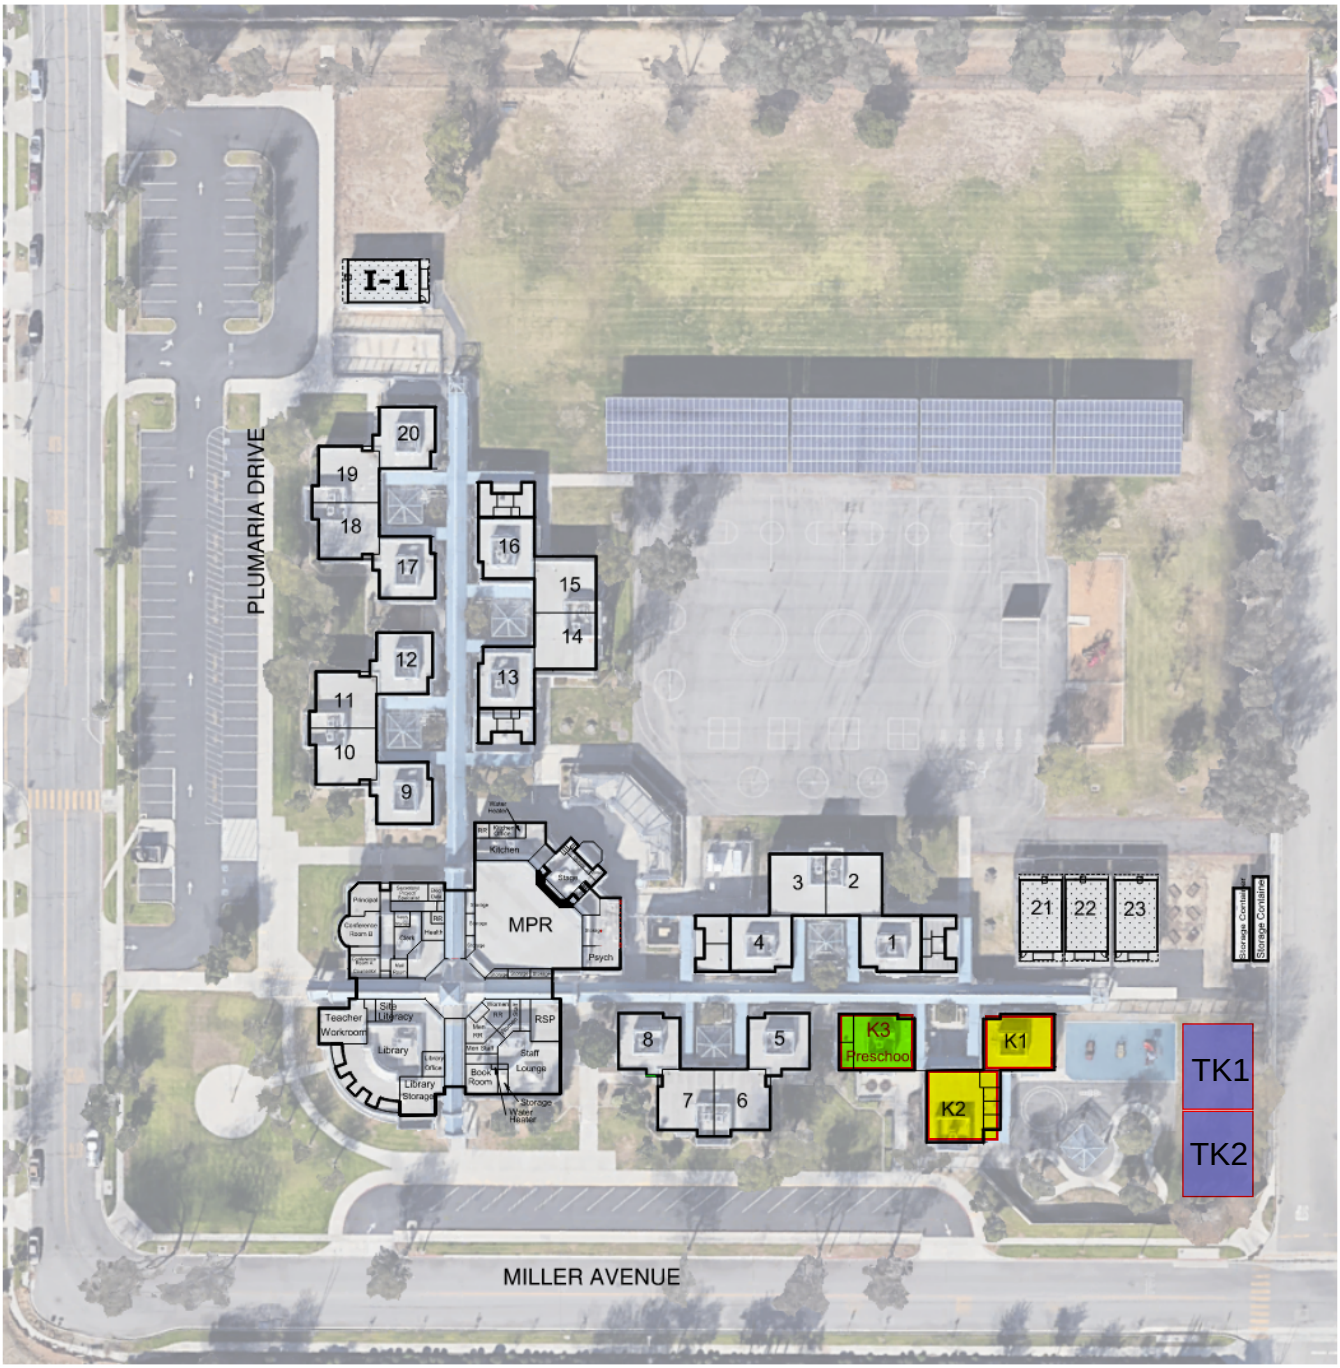

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**

Priority 1

UPK Analysis
Hemlock Elementary School

15080 Miller Ave., Fontana, CA 92336

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**


Priority 1

UPK Analysis
Dorothy Grant Innovations Academy

7069 Isabel Lane, Fontana, CA 92336

Fontana Unified School District

01-27-23

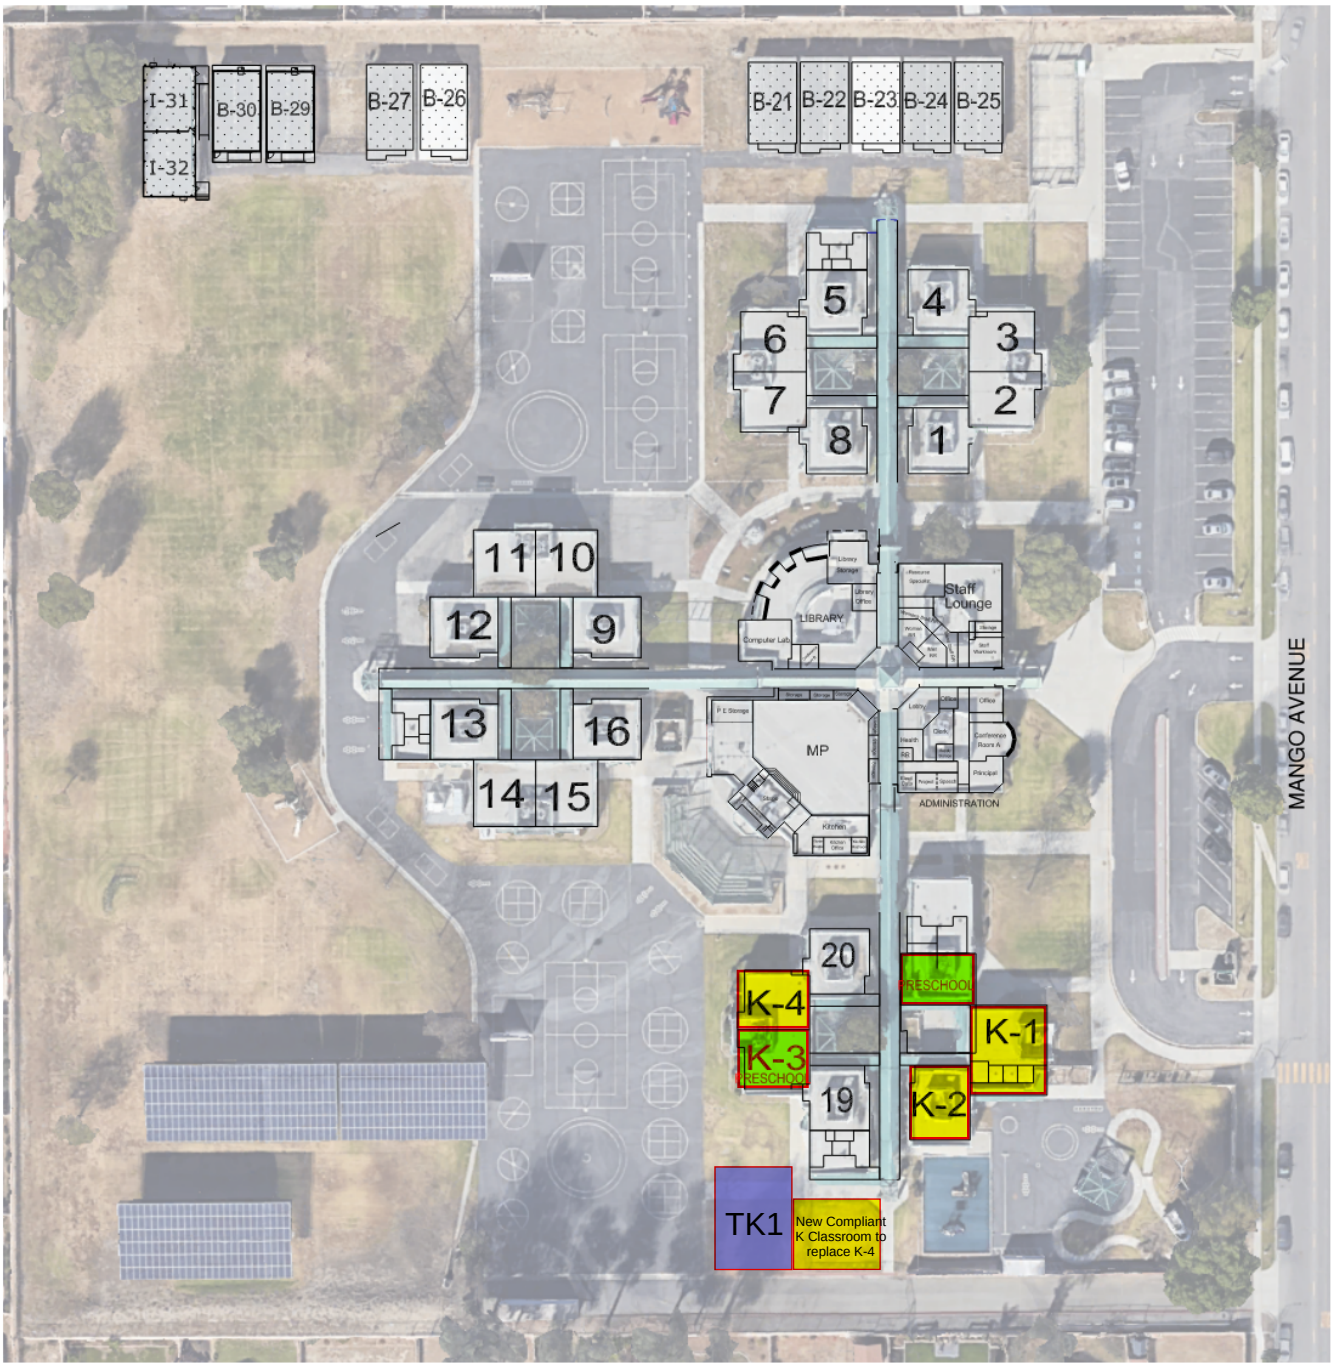

EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

Priority 1

UPK Analysis
Mango Elementary School

7450 Mango Ave., Fontana, CA 92336

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **0 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**


Priority 1

UPK Analysis
Beech Elementary School

9206 Beech Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

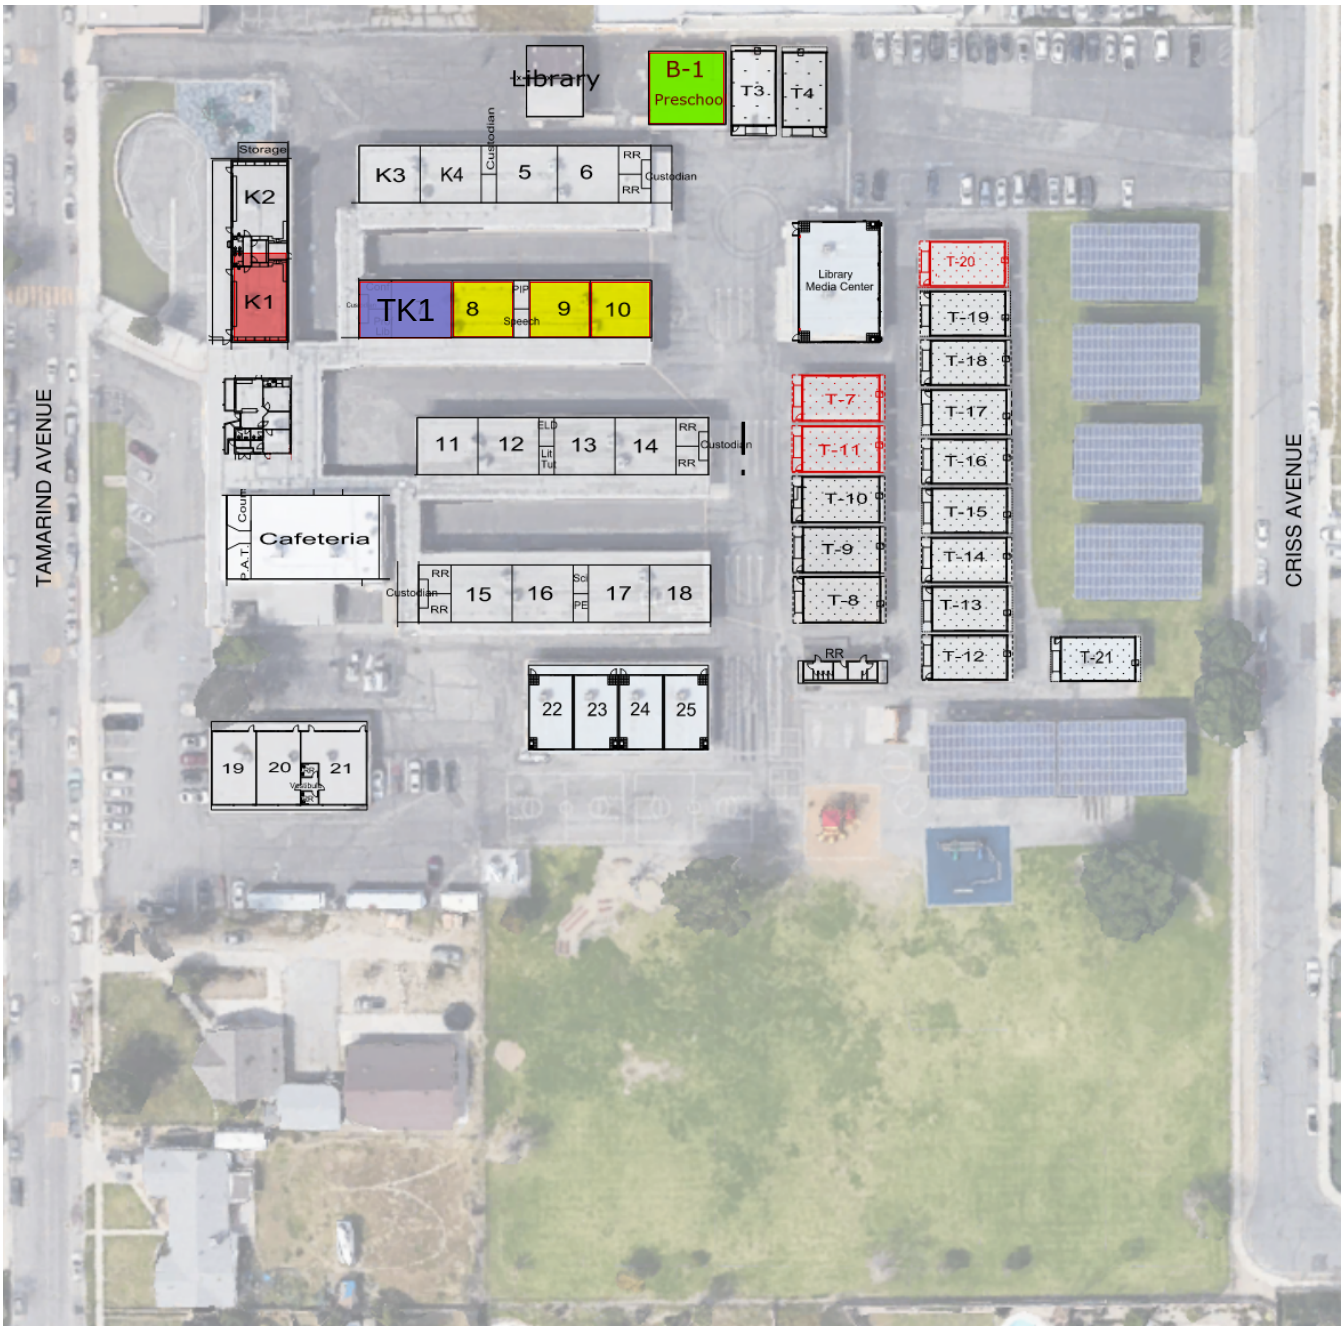

Priority 2

EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
South Tamarind Elementary School

8561 Tamarind Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**


Priority 2

UPK Analysis
Randall Pepper Elementary School

16613 Randall Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

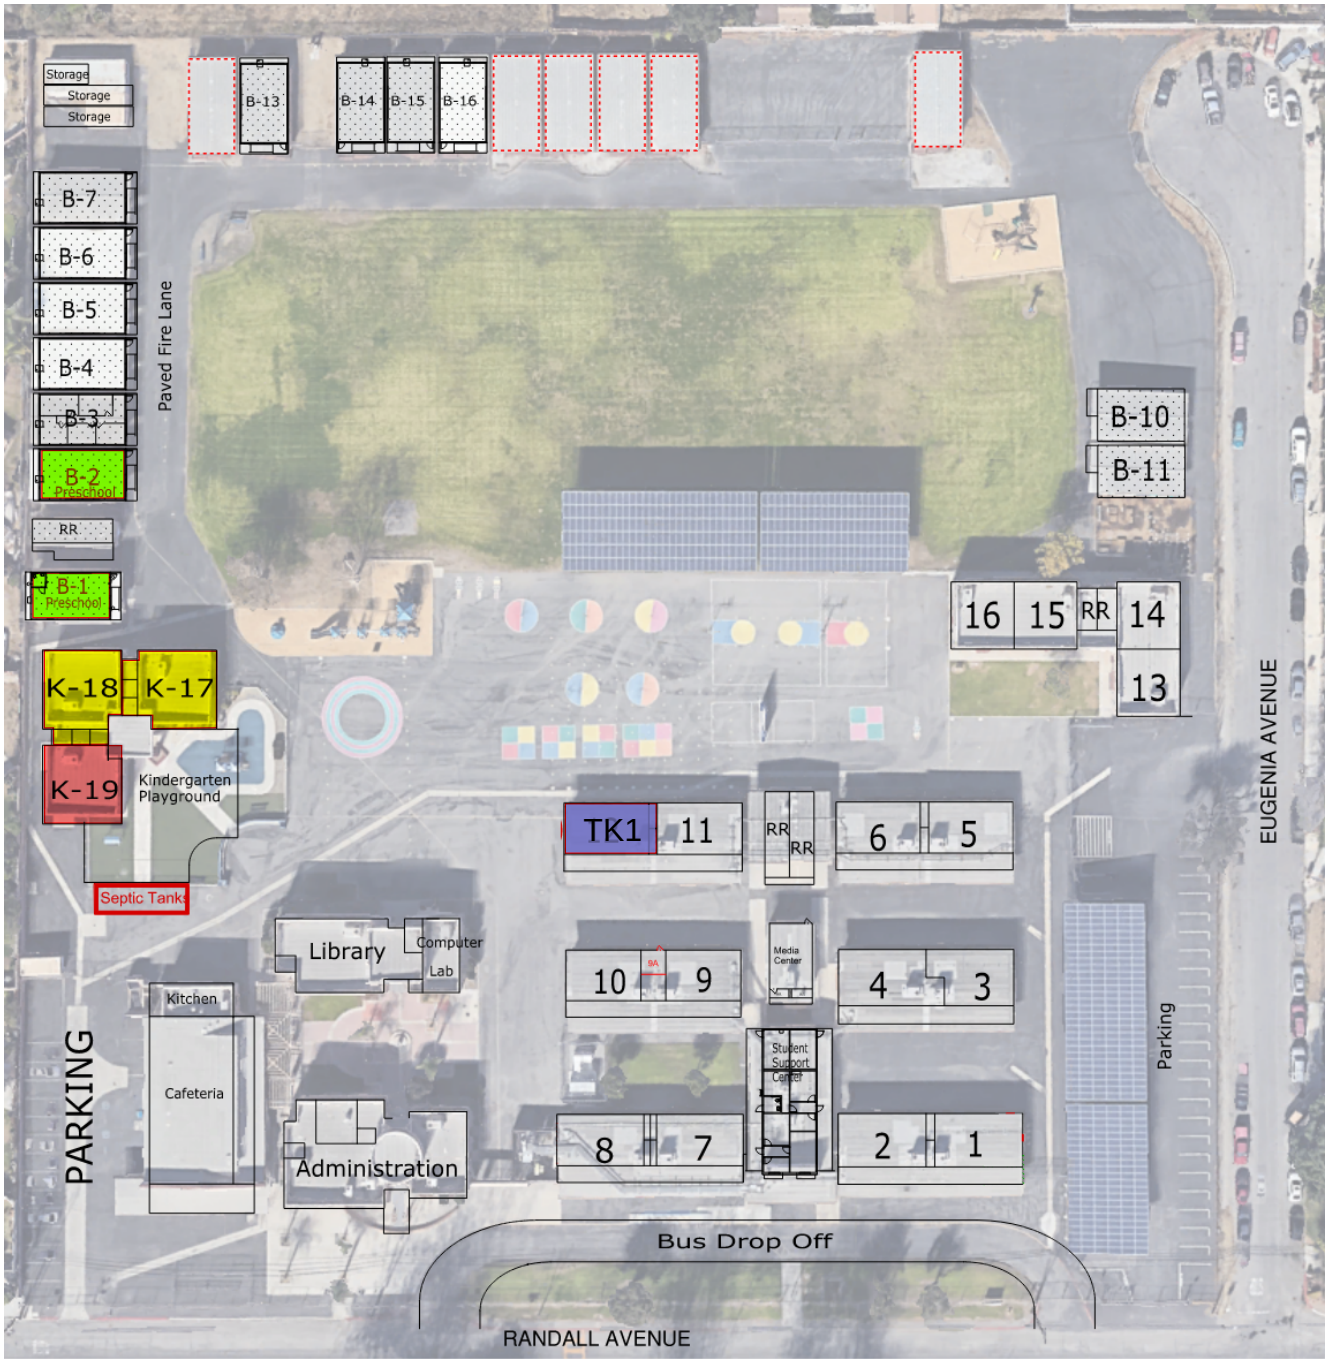

Priority 2

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**


EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
West Randall Elementary School

15620 Randall Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

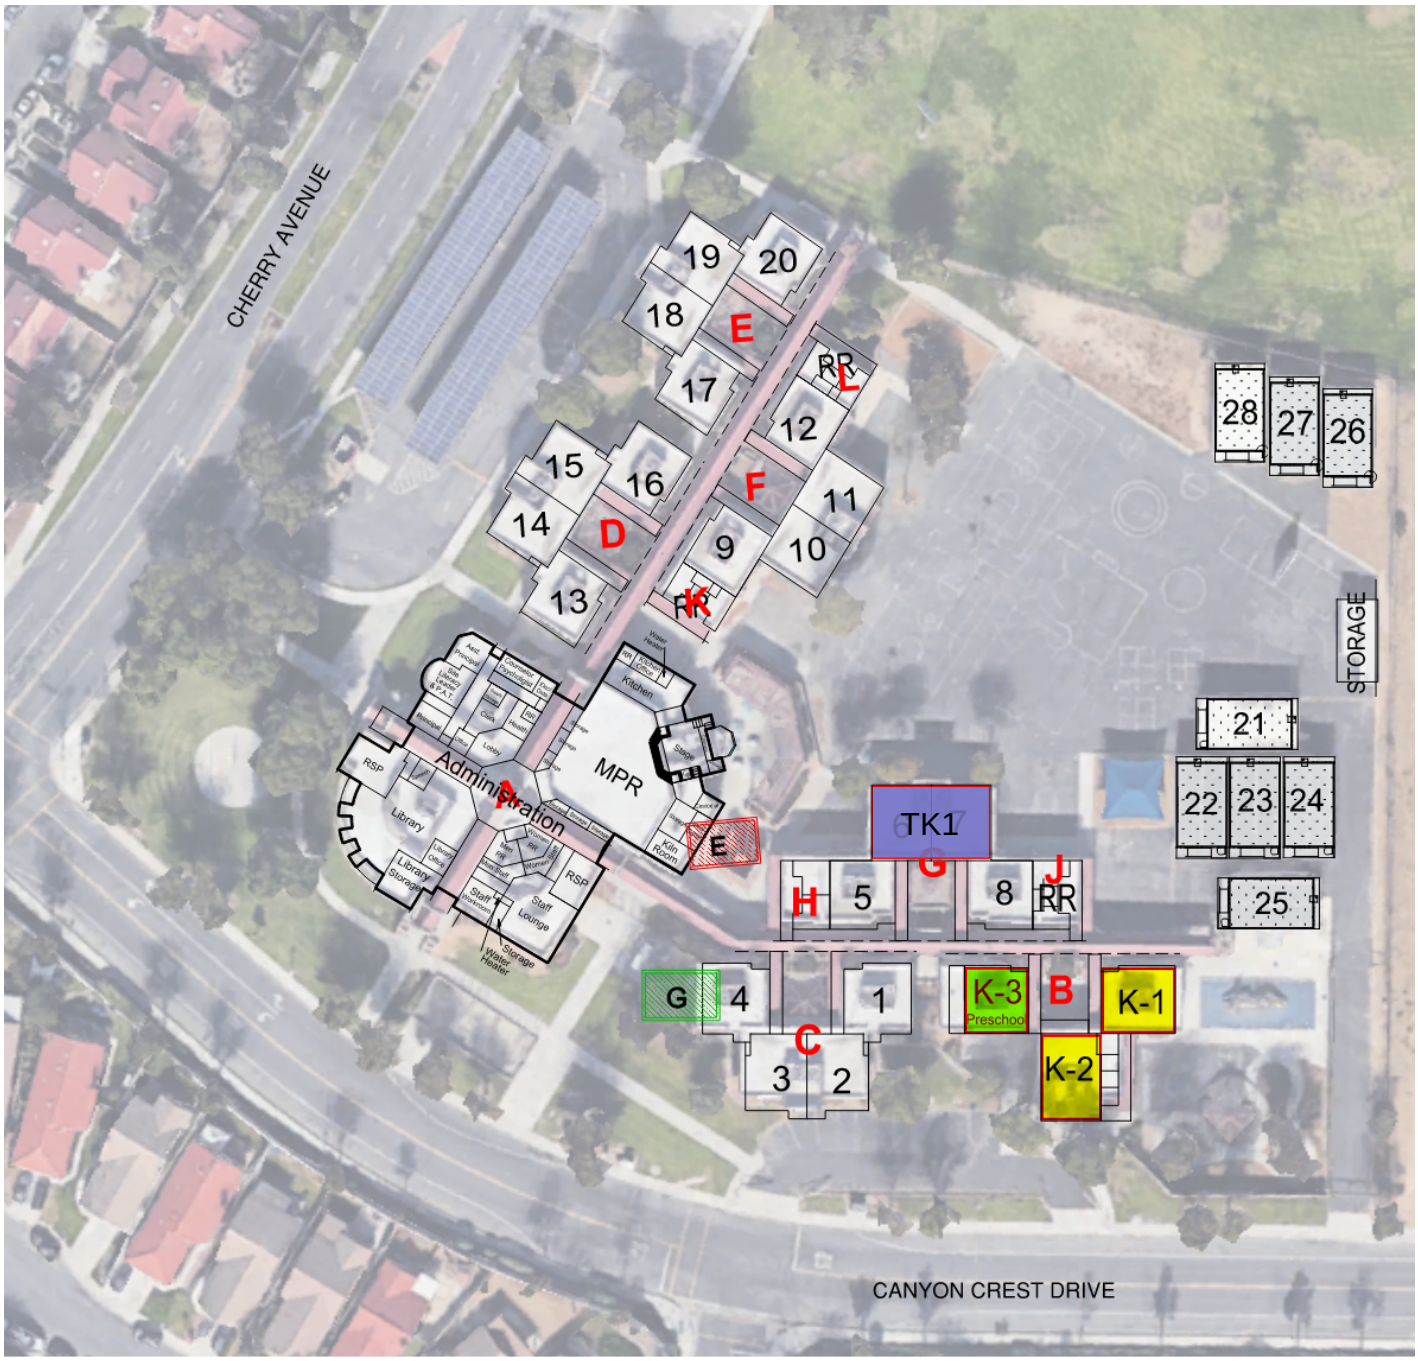


Priority 2

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

UPK Analysis
Canyon Crest Elementary School
11851 Cherry Ave., Fontana, CA 92337
Fontana Unified School District
01-27-23

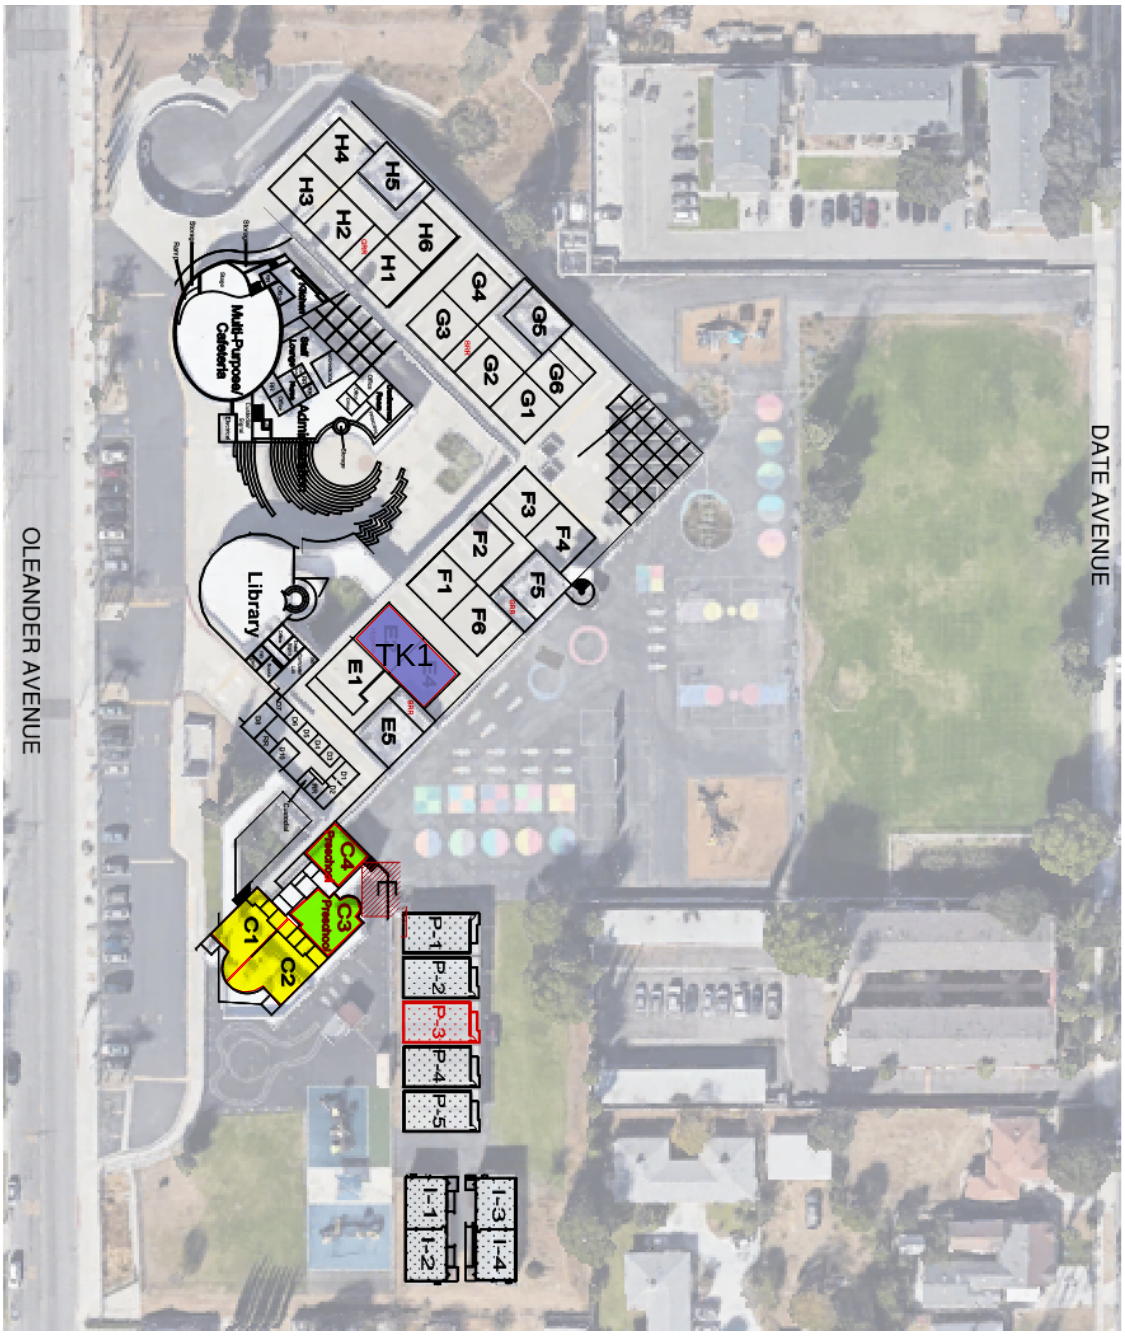

Priority 2

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

UPK Analysis
Date Elementary School

9011 Oleander Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23



Priority 2

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**


PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

UPK Analysis
North Tamarind Elementary School

7961Tamarind Ave., Fontana, CA 92336

Fontana Unified School District

01-27-23

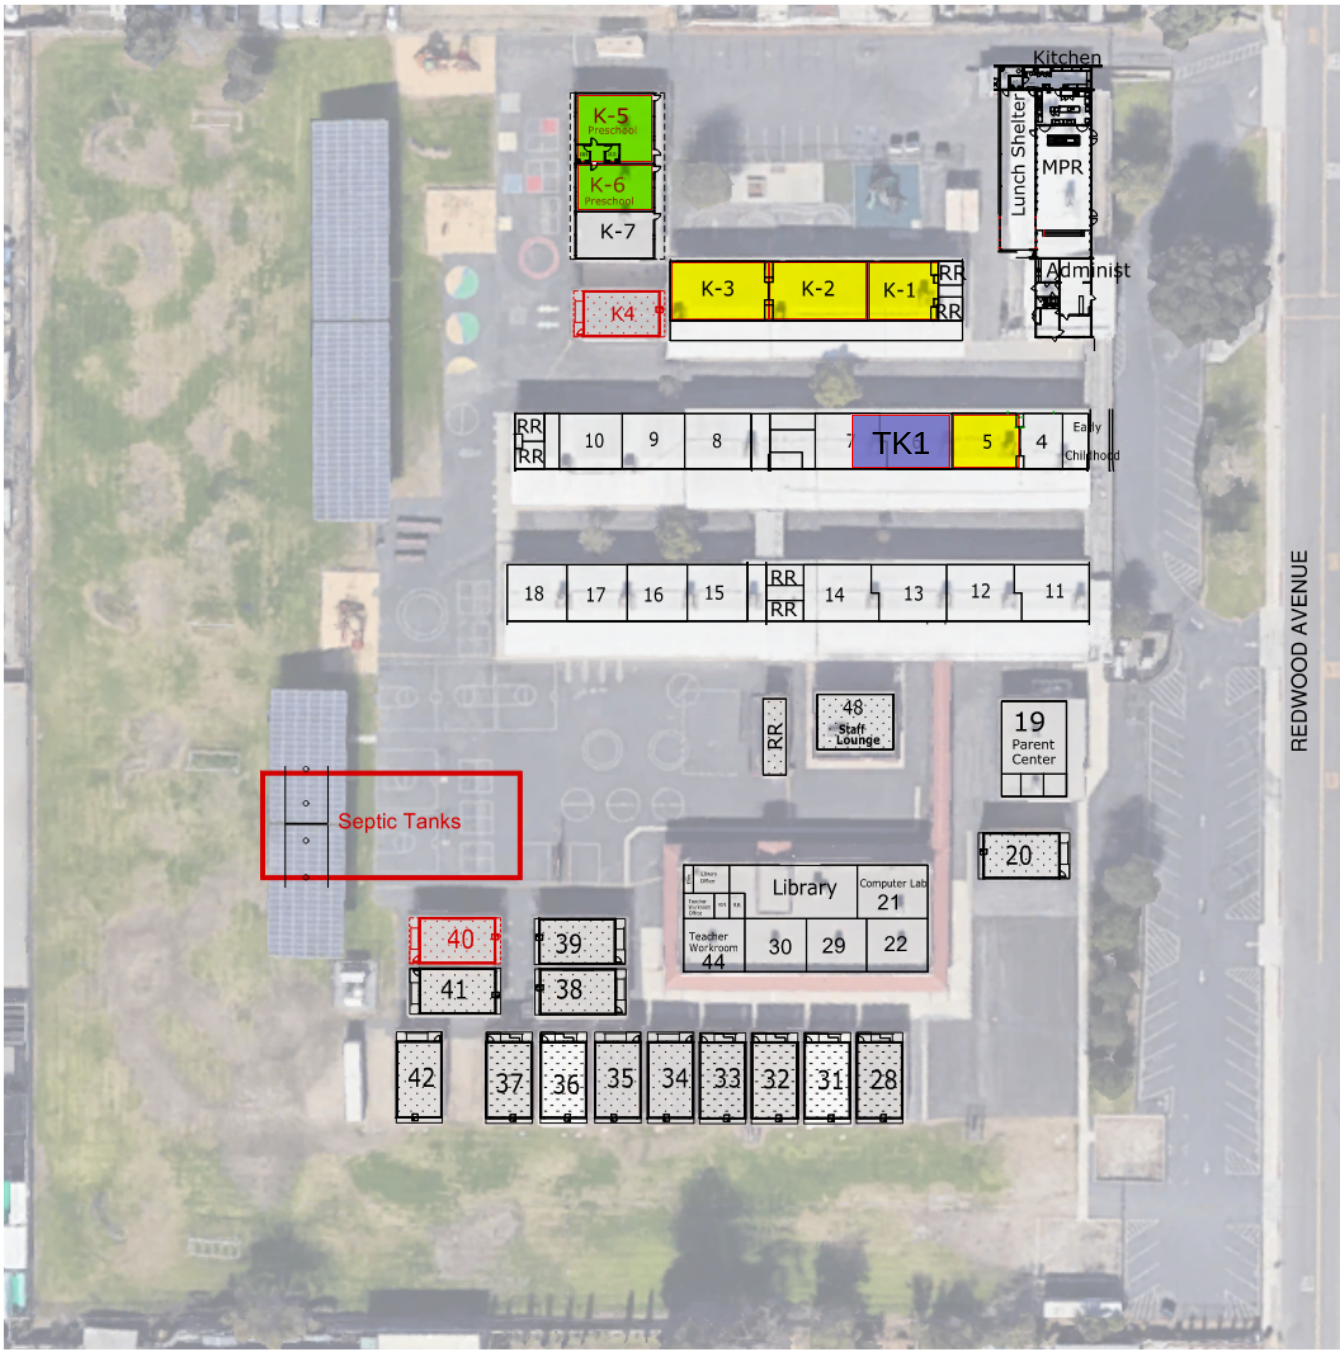

Priority 2

EXISTING **KINDER** CLASSROOMS: **4 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**


PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

UPK Analysis
Redwood Elementary School

8570 Redwood Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

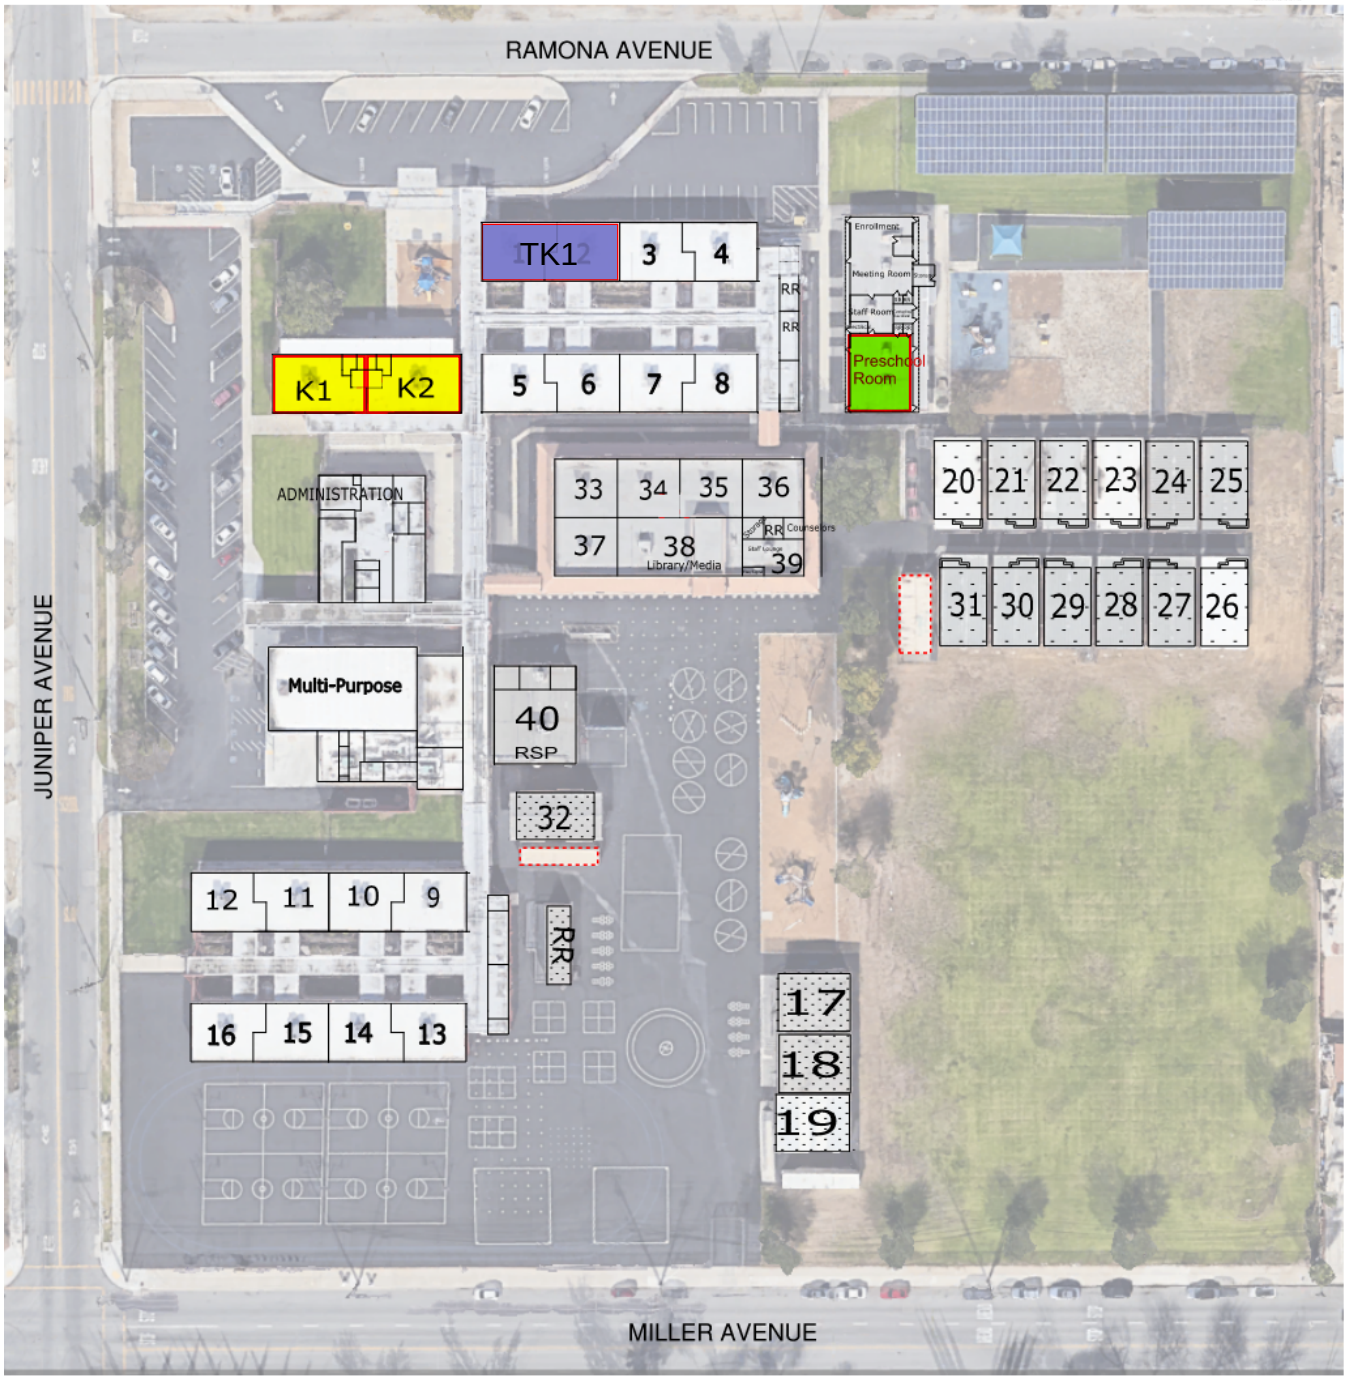

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**


Priority 2

UPK Analysis
Juniper Elementary School

7655 Juniper Ave., Fontana, CA 92336

Fontana Unified School District

01-27-23

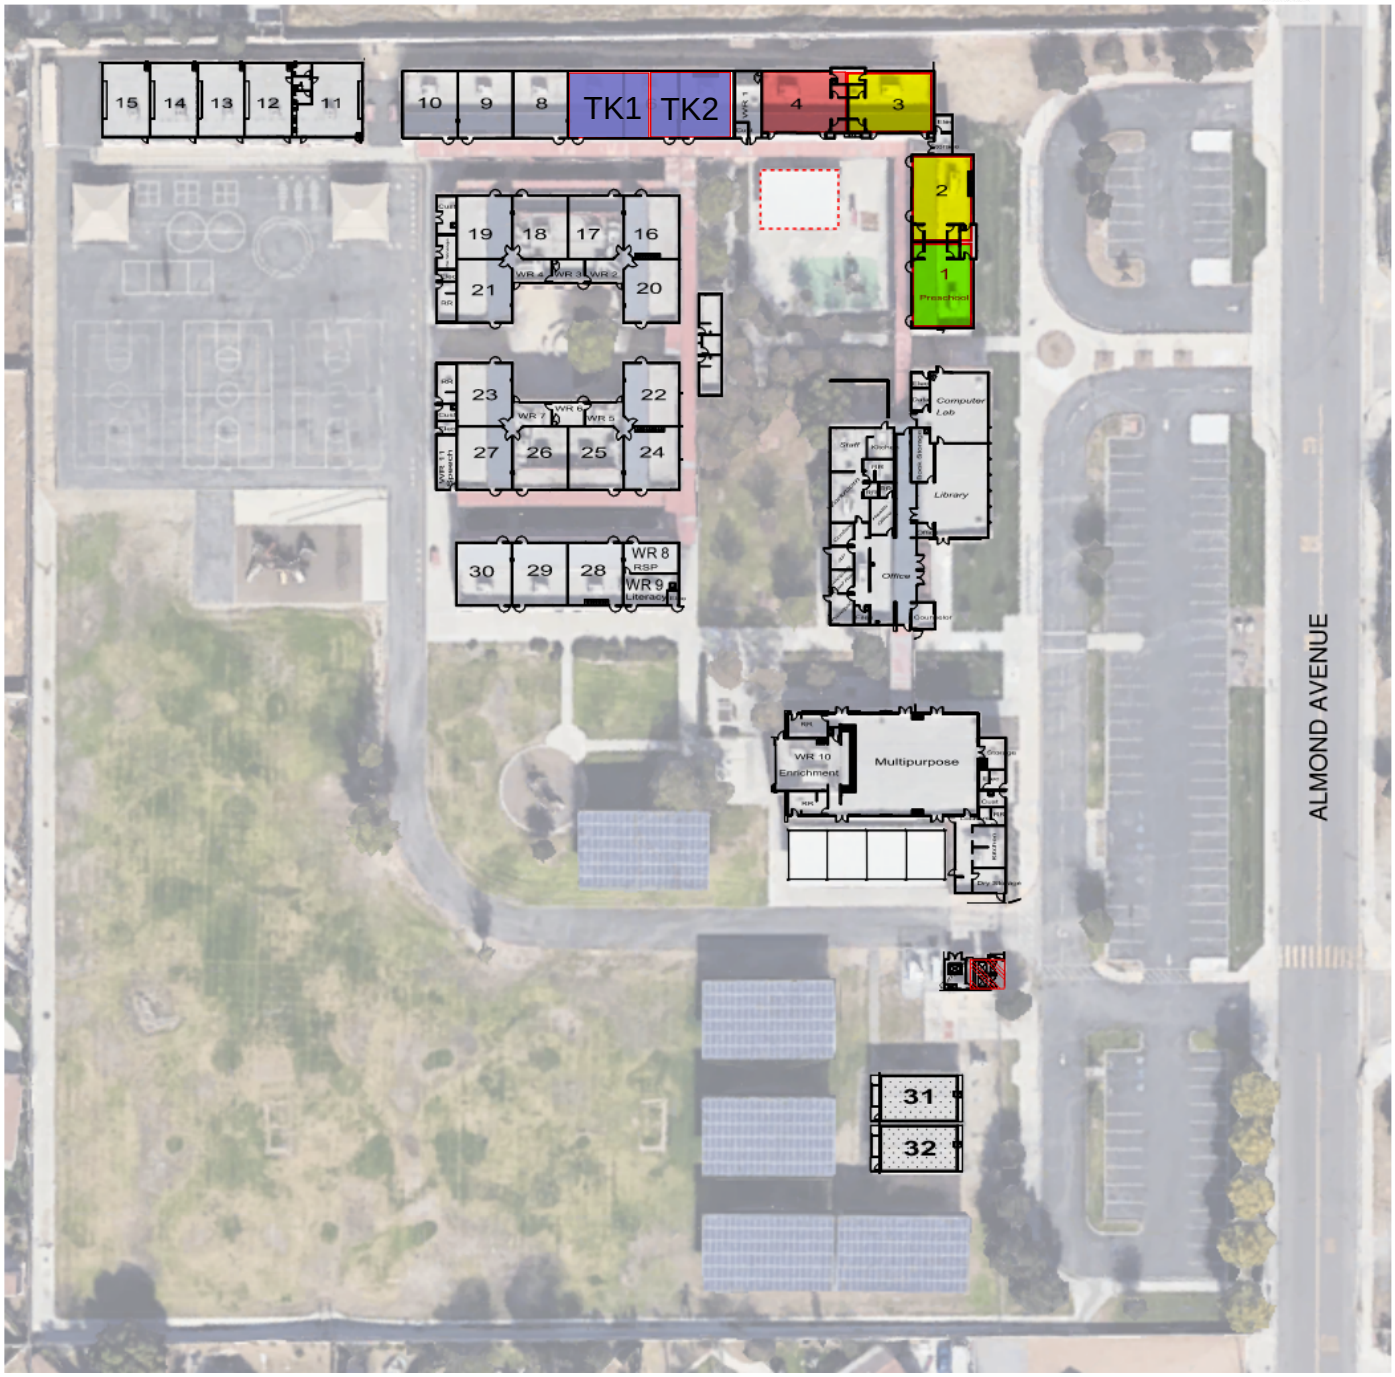

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**


EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
Almond Elementary School

8172 Almond Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

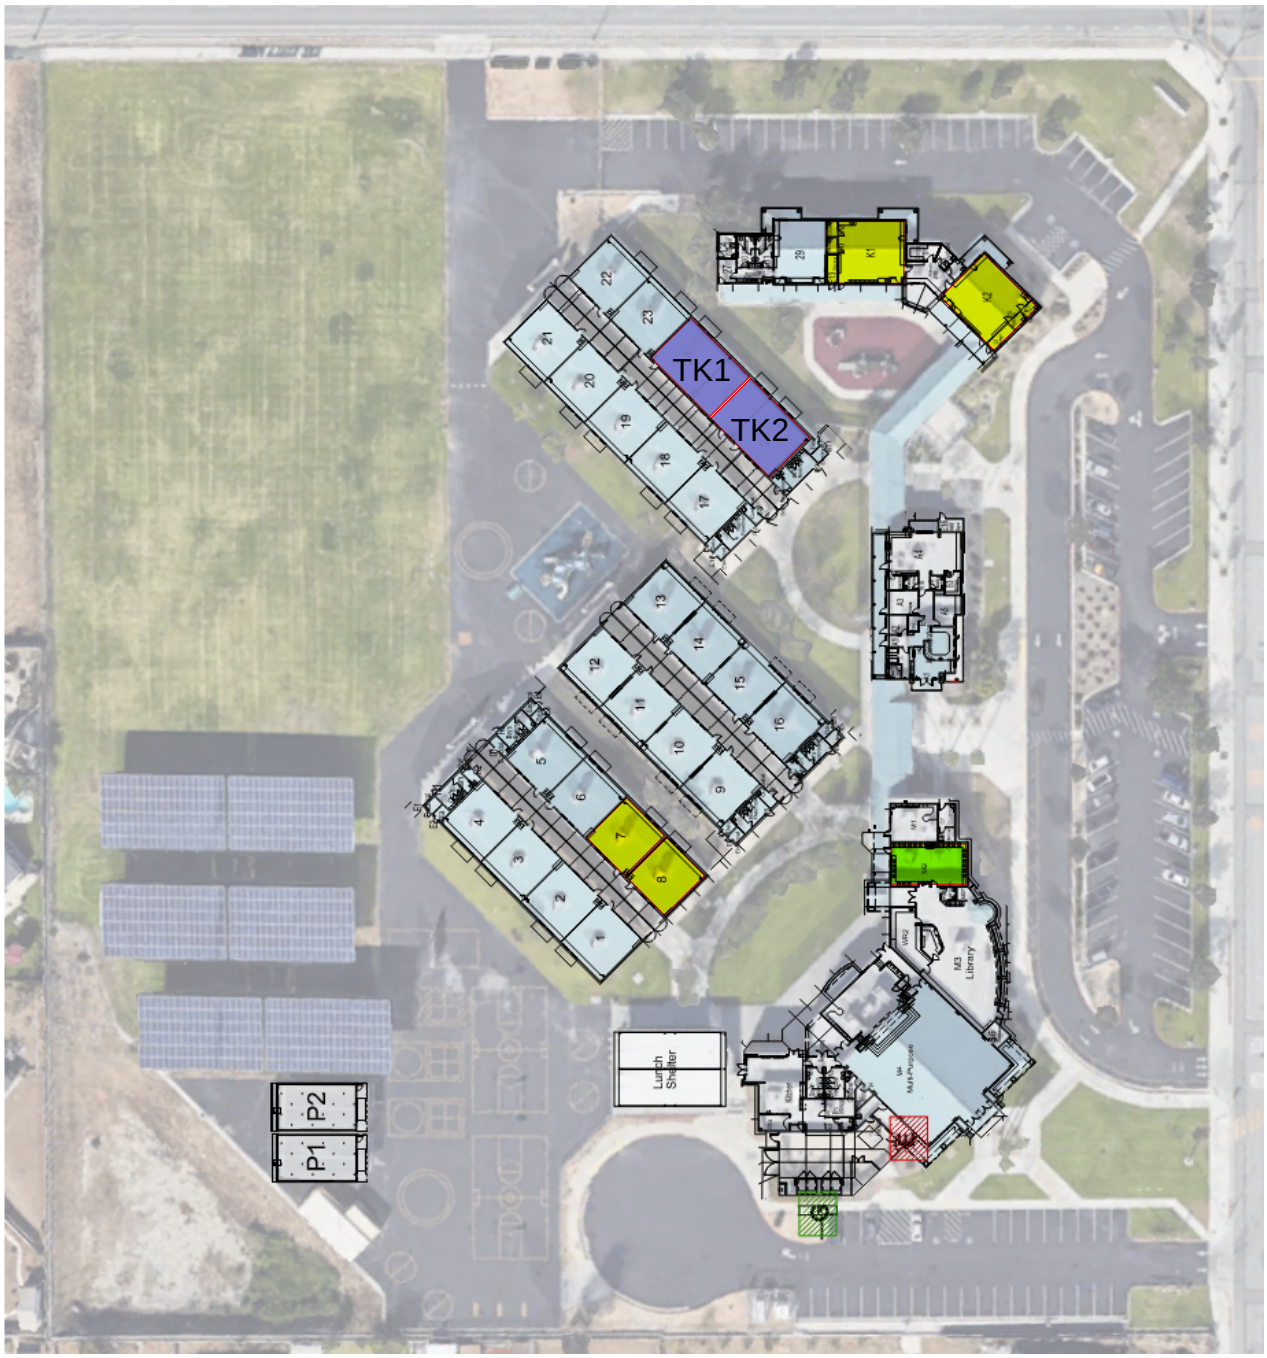

EXISTING **KINDER** CLASSROOMS: **4 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**

UPK Analysis
Kathy Binks Elementary School
7358 Cypress Ave., Fontana, CA 92336
Fontana Unified School District
01-27-23



EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**

UPK Analysis
Chaparral Elementary School

14000 Shadow Drive, Fontana, CA 92337

Fontana Unified School District

01-27-23




Note: Existing Preschool classroom to be relocated to accommodate projected TK classroom.

EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**

UPK Analysis
Citrus Elementary School
16041 Randall Ave., Fontana, CA 92336
Fontana Unified School District
01-27-23

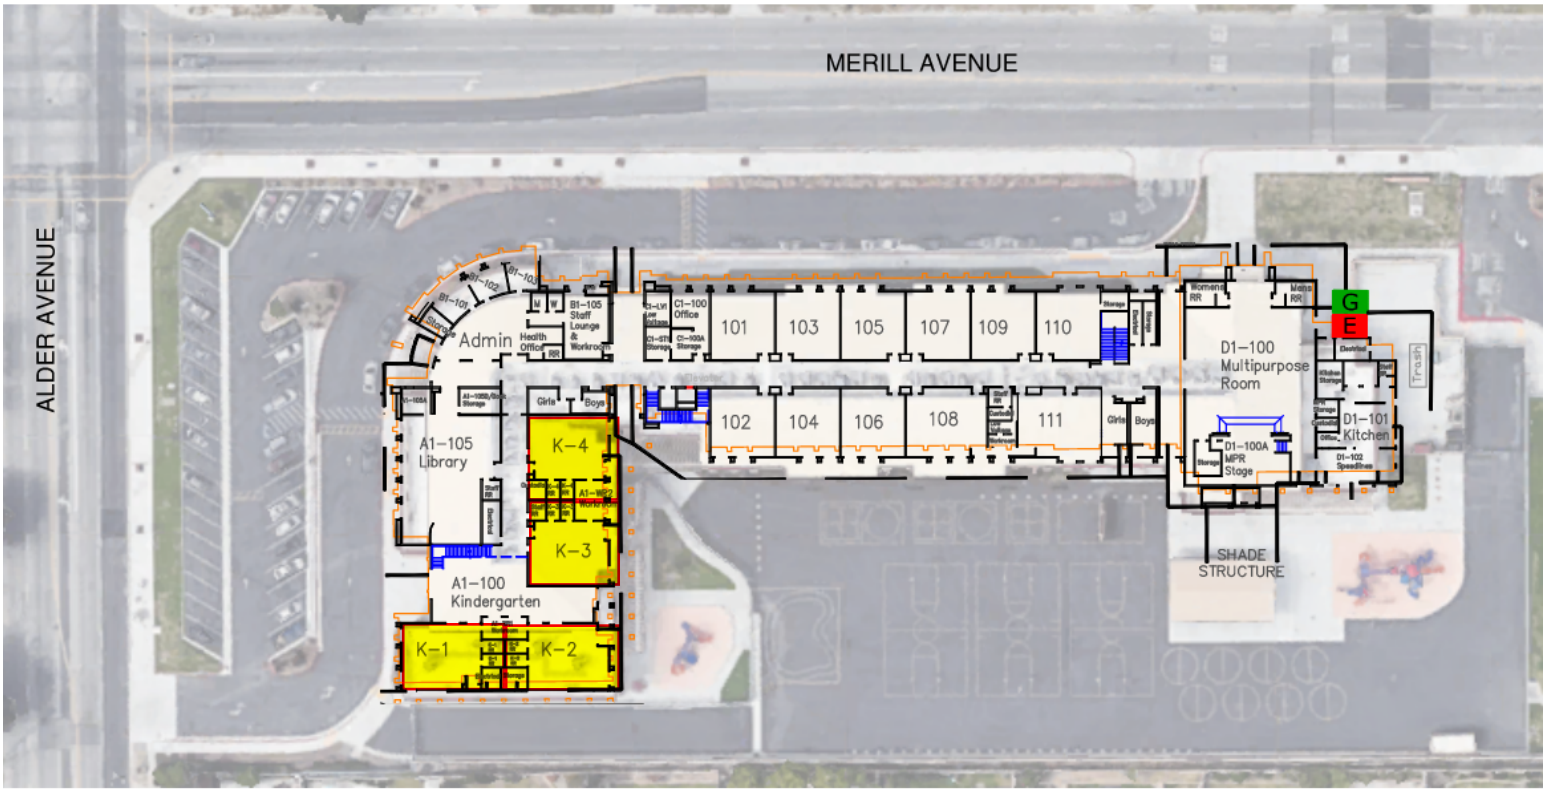

EXISTING **KINDER** CLASSROOMS: **4 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **0 TOTAL**


PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

UPK Analysis
Dolores Huerta International Academy

17777 Merrill Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23

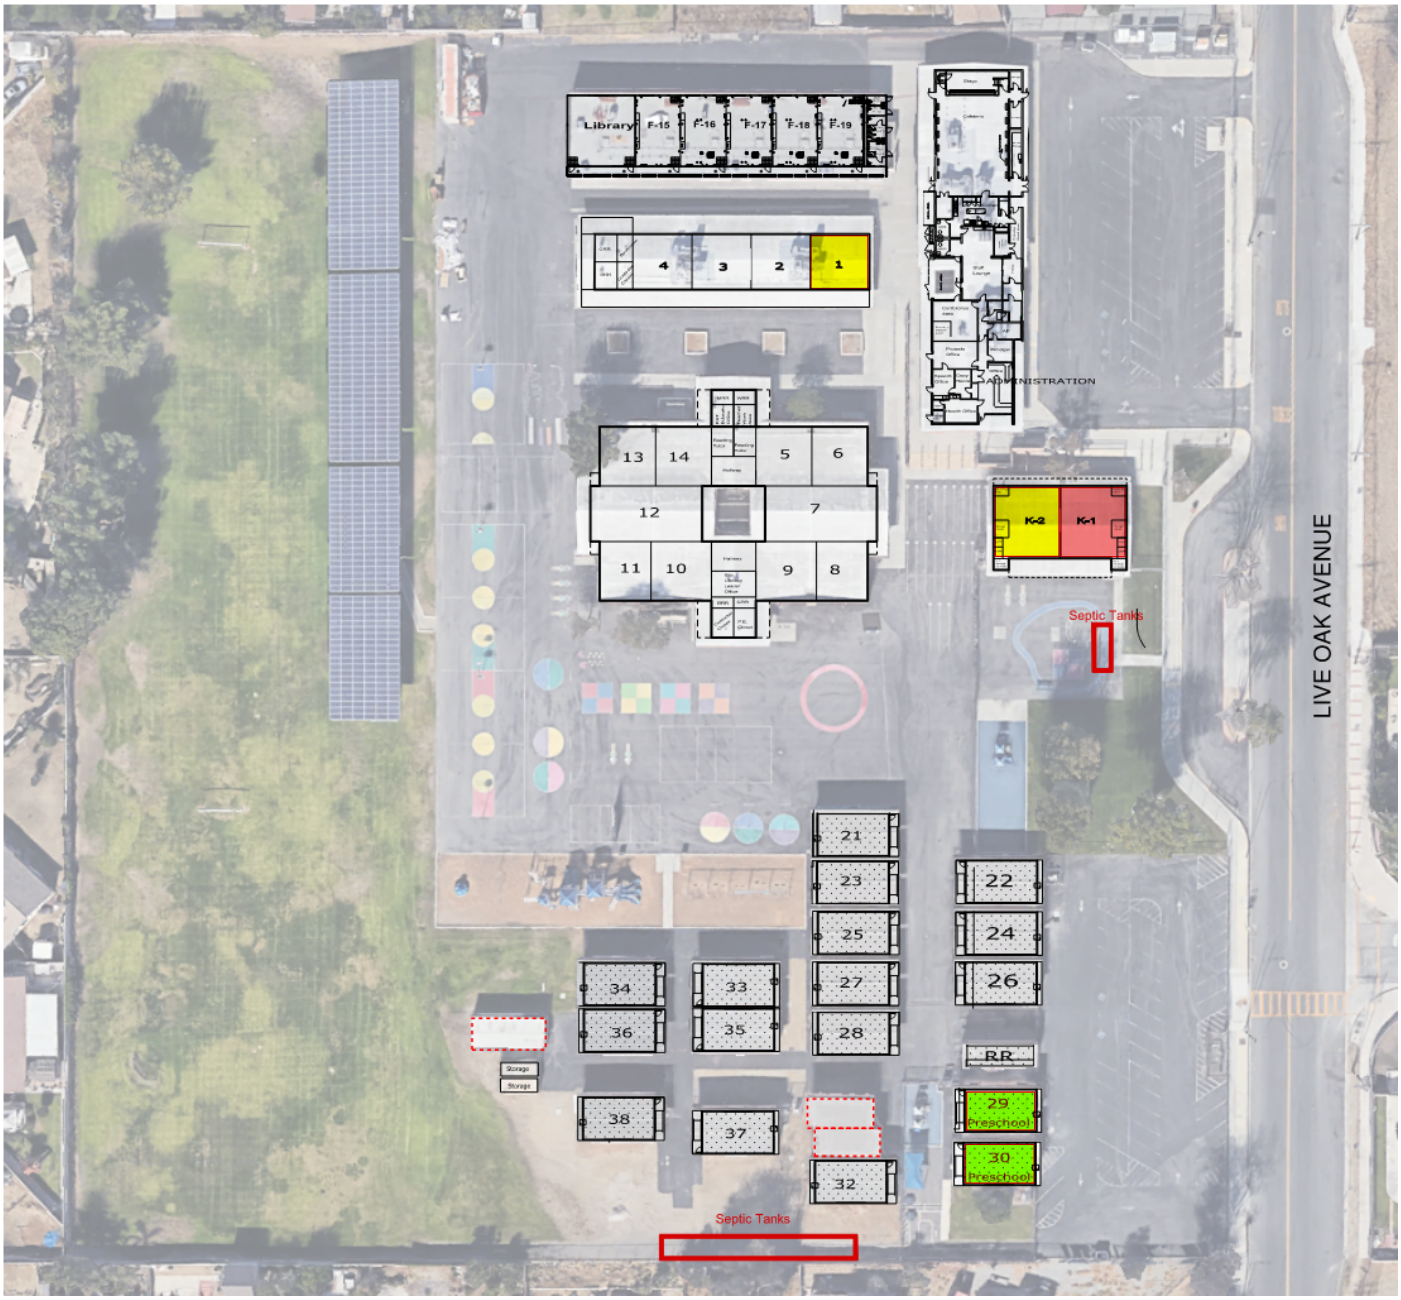

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
Live Oak Elementary School

9522 Live Oak Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23




EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **1 TOTAL**

UPK Analysis
Locust Elementary School
7420 Locust Ave., Fontana, CA 92336
Fontana Unified School District
01-27-23

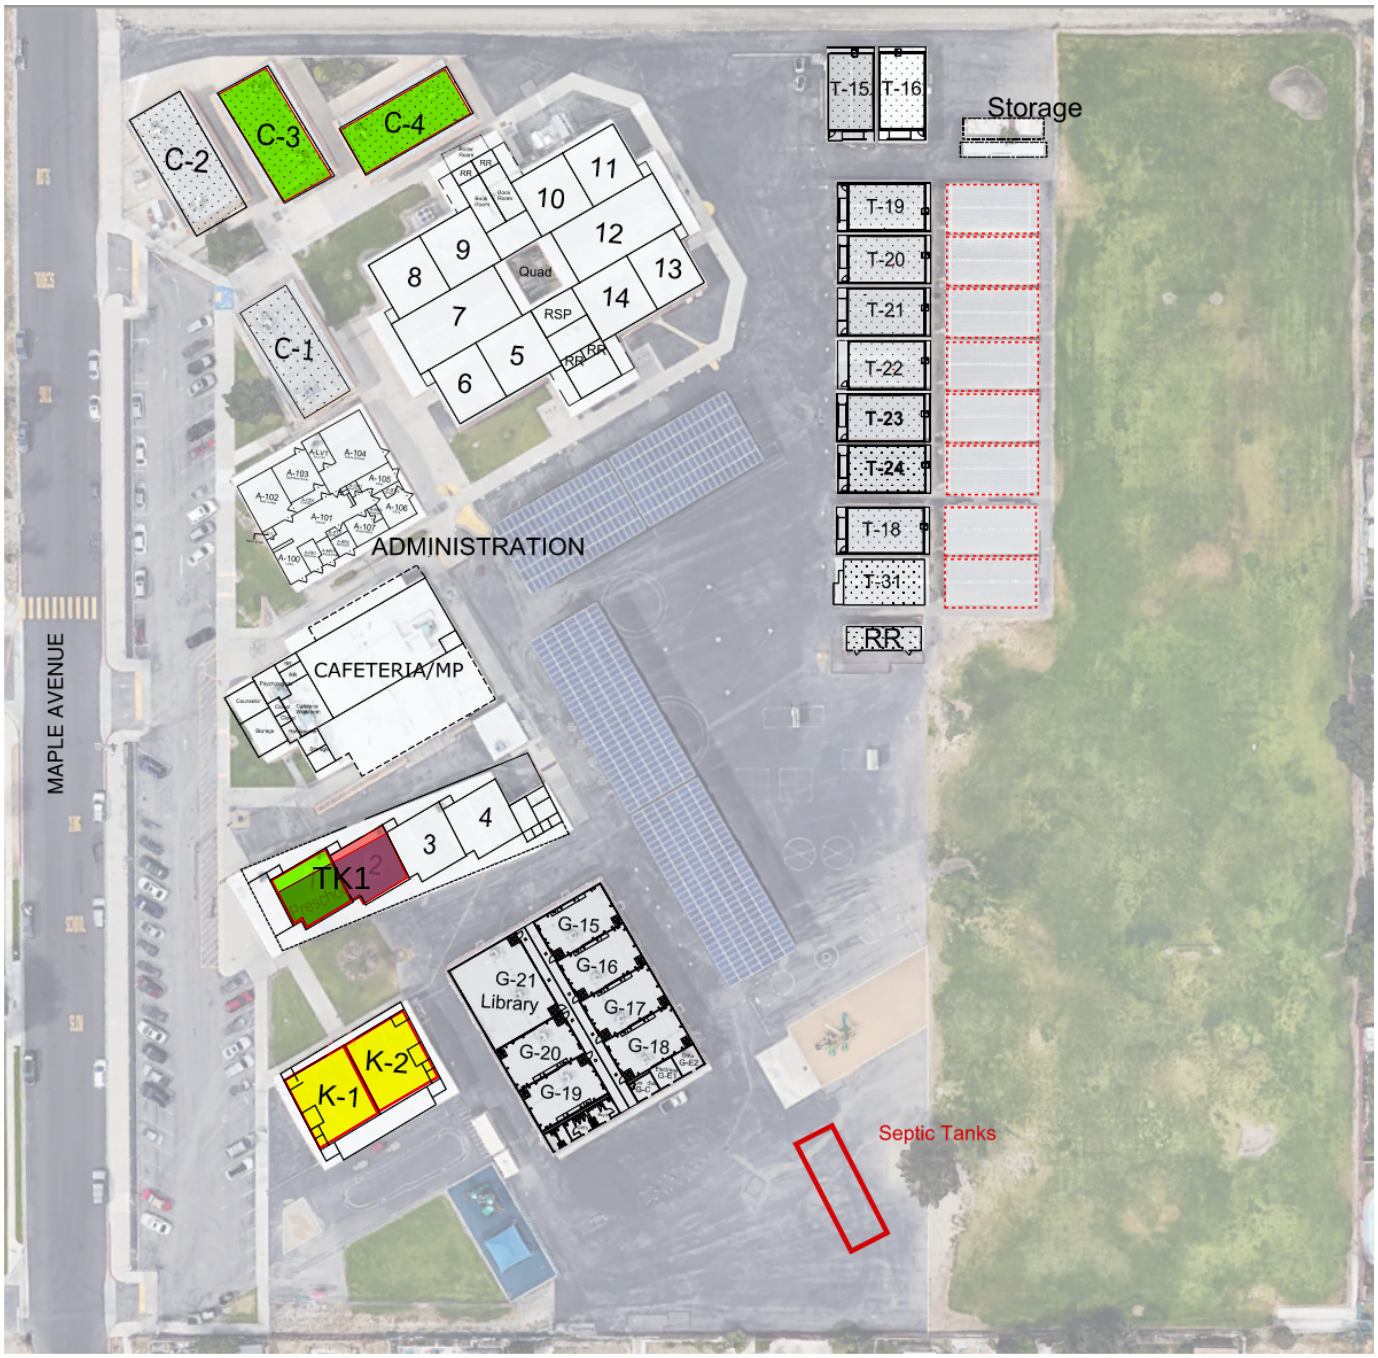

EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
Maple Elementary School
751 S. Maple Ave., Fontana, CA 92335
Fontana Unified School District
01-27-23



EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
Oak Park Elementary School

14200 Live Oak Ave., Fontana, CA 92337

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
Poplar Elementary School

9937 Poplar Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **4 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **2 TOTAL**

UPK Analysis
Porter Elementary School

8330 Locust Ave., Fontana, CA 92335

Fontana Unified School District

01-27-23




EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **2 TOTAL**

UPK Analysis
Primrose Elementary School
751 N. Maple Ave., Fontana, CA 92336
Fontana Unified School District
01-27-23

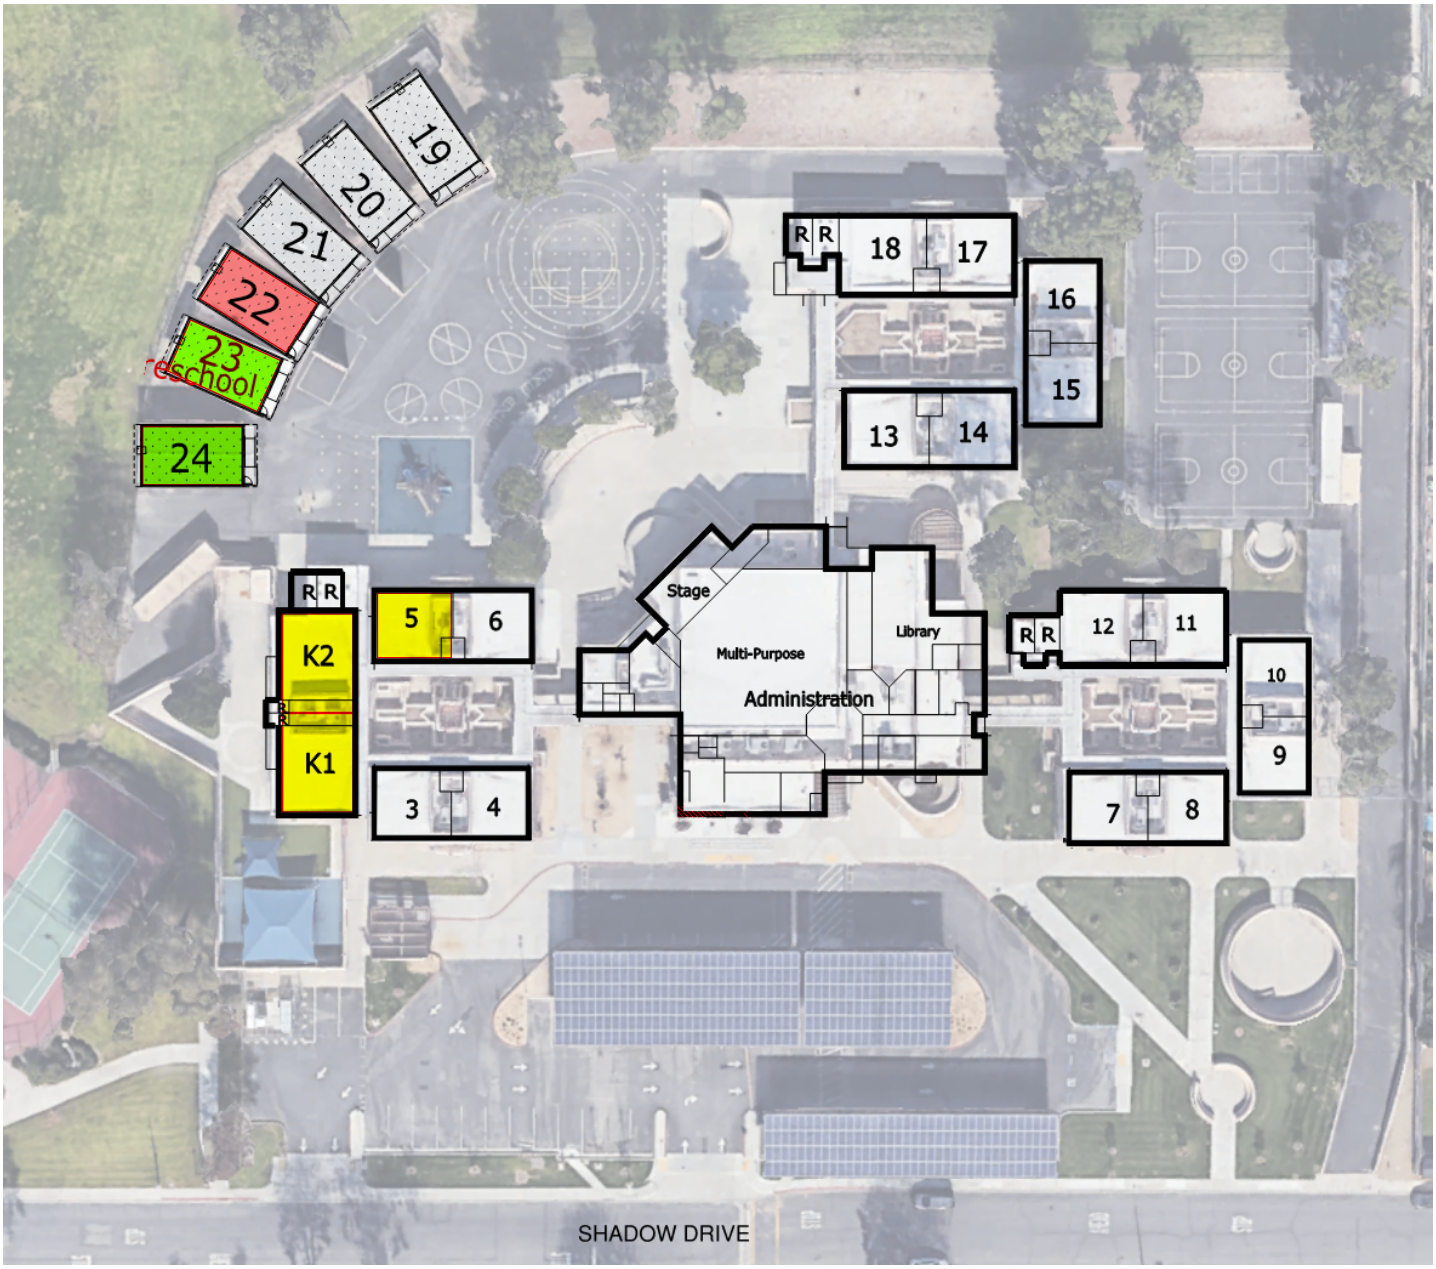

EXISTING **KINDER** CLASSROOMS: **3 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **2 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **1 TOTAL**

UPK Analysis
Shadow Hills Elementary School

14300 Shadow Drive, Fontana, CA 92337

Fontana Unified School District

01-27-23



EXISTING **KINDER** CLASSROOMS: **2 TOTAL**

EXISTING **PRESCHOOL** CLASSROOMS: **1 TOTAL**

PROJECTED **TK** CLASSROOM NEED: **0 TOTAL**

EXISTING **TK** CLASSROOMS: **2 TOTAL**

UPK Analysis
Tokay Elementary School

7846 Tokay Ave., Fontana, CA 92336

Fontana Unified School District

01-27-23



PROPOSED **KINDER** CLASSROOMS: **5 TOTAL**

PROPOSED **TK** CLASSROOM NEED: **4 TOTAL**

UPK Analysis
Elementary School # 47
Curtis Ave., Fontana, CA
Fontana Unified School District
01-27-23
