STOUGHTON AREA SCHOOL DISTICT
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

City of Stoughton, Wisconsin 5/2/25

River Bluff Campus

As finishes wrap up in the River Bluff addition, exterior site work moves forward! Site grading continues followed swiftly by Findorff cement finishers forming and pouring sidewalks. Next week light pole bases will be poured, and the poles will be set. The following week the curb and gutter will be installed throughout the new parking lot and student drop-off/pick-up lanes.

At the District Office, installation of the elevator is nearly complete. The drywall finish and paint are complete, and installation of the casework and windowsills are underway.



Above: an up-close look at the new gym floor finish in the River Bluff addition, check out that purple pop!

High School

No diving please! The High School pool has been drained, and renovation work is underway! Scaffolding is being assembled inside the pool to create a safe workspace for removing the existing tile along the pool's edge. Demolition of the existing doors, frames, and hardware is also underway. In the locker rooms, all floor-mounted accessories and furniture are being removed in preparation for the new fluid-applied epoxy flooring. Demo of the pool area flooring will soon begin as well.

The plumbers have completed the installation of a new floor drain in the men's restroom and have begun replacing the drinking fountains with new units equipped with bottle fillers.

Outside the pool area, new flooring is being installed in the pool entry vestibule, along with the remaining flooring outside the PAC.



Above: a view of the High School pool as it is drained and renovation work begins in the space

DID YOU KNOW?

The new main entrance to the River Bluff Middle School will feature a large courtyard for students to safely gather away from traffic during student drop-off and pick-up. The courtyard space spans over 5,000 square feet and will include multiple landscaping beds.

Questions?

Senior Project Manager, Matt Claggett / 608.729.2155 / mclaggett@findorff.com

Findorff
BUILDING & BEYOND


STOUGHTON AREA SCHOOL DISTICT
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

City of Stoughton, Wisconsin 5/2/25



Top Left: a view of the River Bluff entrance following the first couple concrete sidewalk pours

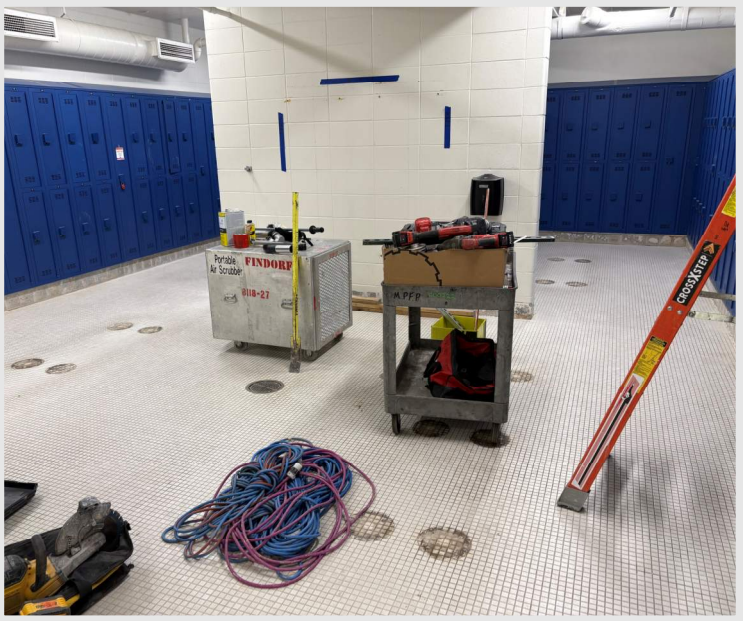

Top Right: a photo of High School locker room as demo of the existing finishes begin



Below: another photo of the finished gym floor in the River Bluff addition

Questions?

Senior Project Manager, Matt Claggett / 608.729.2155 / mclaggett@findorff.com

Findorff
BUILDING & BEYOND
