STOUGHTON AREA SCHOOL DISTICT
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

City of Stoughton, Wisconsin 5/30/25

High School

Check out the exciting progress on the High School pool renovations! All the existing pool tile has been removed, and the final coat of the fluid-applied epoxy flooring has been poured in the locker rooms and in a portion of the pool area. This new floor system will offer a more slip-resistant and modern look to the space. Demolition of finishes like the existing acoustical panels is underway, and removal of the clerestory windows will begin next week.

Mechanical upgrades continue across the High School. The building's boilers have been replaced and preparations for new roof-top units continue. Next month, several of the heavier rooftop units will be set using a helicopter!

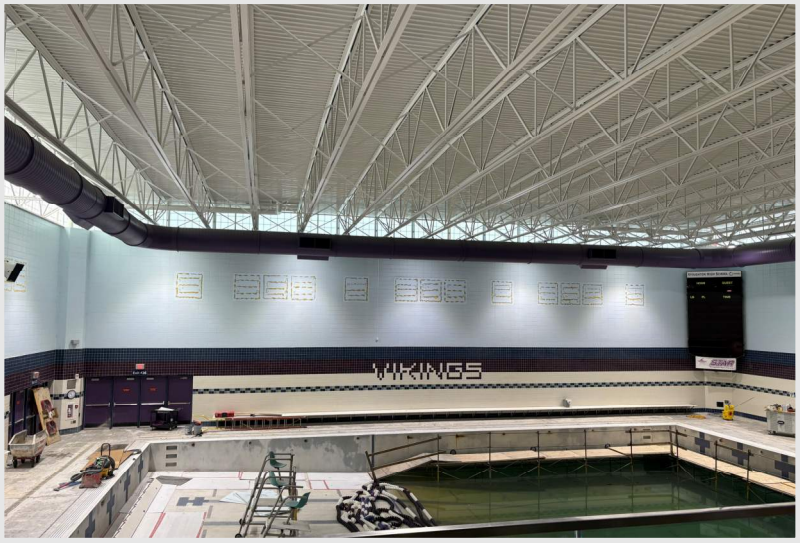

Above: a view of the overall progress in the High School gym as demo of the existing finishes continue

River Bluff Campus

The Past Few Weeks:

- Curb and gutter install complete
- Site rough grading complete
- Parking lot permeable paver install underway
- Gymnasium bleacher install complete
- District Office elevator install complete
- River Bluff addition post construction clean complete

Coming Up!:

- Site landscaping to begin
- River Bluff building signage to be installed
- District Office paint and flooring replacements to begin
- River Bluff addition punch list
- Parking lot asphalt paving
- Installation of the new River Bluff monument sign



Above: a first look at the permeable pavers that will be featured in the new River Bluff Campus parking lot

DID YOU KNOW?

The new River Bluff Campus parking lot will feature nearly 4,000 square feet of permeable pavers! Instead of allowing stormwater, often carrying pollutants, to run off into local drains, these pavers will capture a large percentage of the parking lot stormwater. The paver system then filters the water through various layers of gravel and soil to a drain tile system that returns the now clean water to the ground.

Questions?

Senior Project Manager, Matt Claggett / 608.729.2155 / mclaggett@findorff.com

Findorff BUILDING & BEYOND

STOUGHTON AREA SCHOOL DISTICT
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

City of Stoughton, Wisconsin 5/30/25



Top Left: a view of the River Bluff addition gym following a final clean of the space

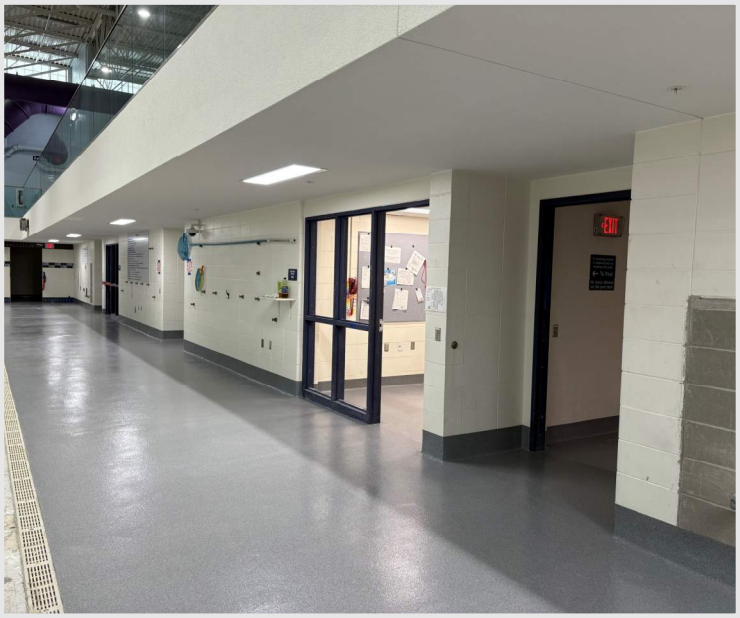

Top Right: a photo of the High School pool renovation progress following install of the fluid-applied epoxy flooring



Below: another look into the River Bluff gym highlighting the "Stoughton Vikings" lettering painted on the floor

Questions?

Senior Project Manager, Matt Claggett / 608.729.2155 / mclaggett@findorff.com

Findorff
BUILDING & BEYOND
