STOUGHTON AREA SCHOOL DISTICT
EXECUTIVE SUMMARY


PROVIDED BY FINDORFF

City of Stoughton, Wisconsin 7/25/25

High School

Progress continues in the High School pool! New underwater lights and depth markers have been installed to ensure the area remains a safe environment for all users. Installation of the tile on the pool deck is also underway!

In the Fab Lab, drywall is complete, and the new aluminum storefront window frames have been installed. Ceiling grid has been installed in the art room, and the light fixtures have been placed. Polishing of the art room's concrete floor is also underway. The new polished concrete finish will give the classrooms a sleek industrial look. The new flooring is complete in the special education classroom, including the epoxy flooring in the private restroom.

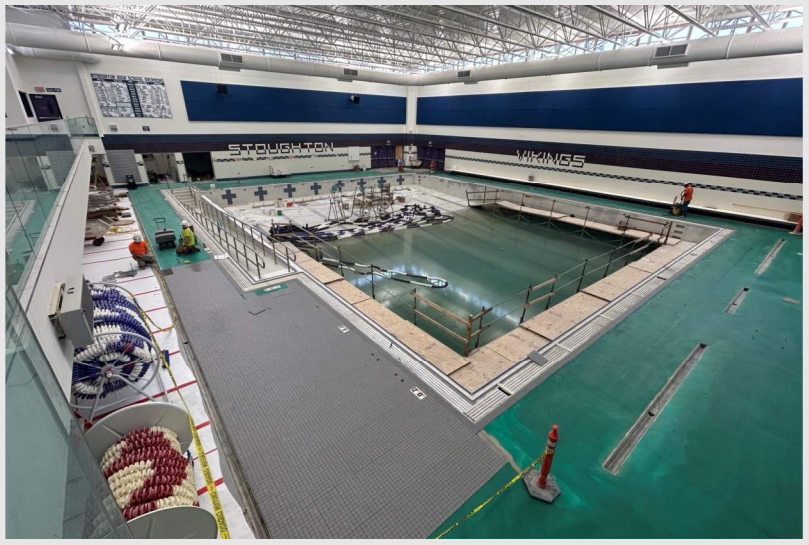

Above: a photo of the overall progress in the High School pool as floor prep is completed ahead of tile install

River Bluff Campus

We continue to check off the final items on the River Bluff Middle School addition! This past week, both the fire alarm and sprinkler system passed inspection with the Stoughton Fire Department. Landscaping continues site-wide, and installation of the monument sign metal panels is complete. In the coming weeks, we will begin work on some exciting added scope, including the removal of the existing and installation new basketball courts and hoops along the east side of the school.

The interior renovations to the District Office continue. Following the completion of the first and third floors, demo is now complete on the second floor, and installation of the new paint and flooring is underway. Earlier this week, the District Office also successfully passed its fire alarm inspection.



Above: a view of the new River Bluff Middle School entrance highlighting the recently installed landscaping

DID YOU KNOW?

Sandhill Elementary is also receiving several smaller, but equally important upgrades to benefit students and staff. These updates include the replacement of exterior guardrails for increased safety, new mechanical equipment including exhaust fans and cabinet unit heaters, drinking fountains with bottle fillers, new door auto operators, plus an added roof ladder and hatch to make access to the roof safer.

Questions?

Senior Project Manager, Matt Claggett / 608.729.2155 / mclaggett@findorff.com

Findorff
BUILDING & BEYOND

STOUGHTON AREA SCHOOL DISTICT
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

City of Stoughton, Wisconsin 7/25/25


Fox Prairie Elementary

The renovations at Fox Prairie Elementary continue to push forward! With four weeks to go, nearly all the classroom spaces have been completed, and the ceiling grid and paint are underway in the corridors. Findorff carpenters have begun swinging doors throughout the building and installing marker boards and tack boards in the classrooms. In the coming weeks, installation of the new lockers will begin. The first half of the kitchen epoxy floor has been poured, and the second half is scheduled to be poured next week.


Over the past couple of weeks, the mechanical team has successfully set the four new air handling units (AHUs) in the building. Preparations are now underway for install of the air-cooled condensing units (ACCUs). Installation of the new boilers in the mechanical mezzanine is also complete. Plumbing and electrical rough-ins for the new restroom sinks are complete, and the new sinks will soon be set.



Above: a view of the recently installed finishes in a Fox Prairie classroom including the new marker boards and tack boards

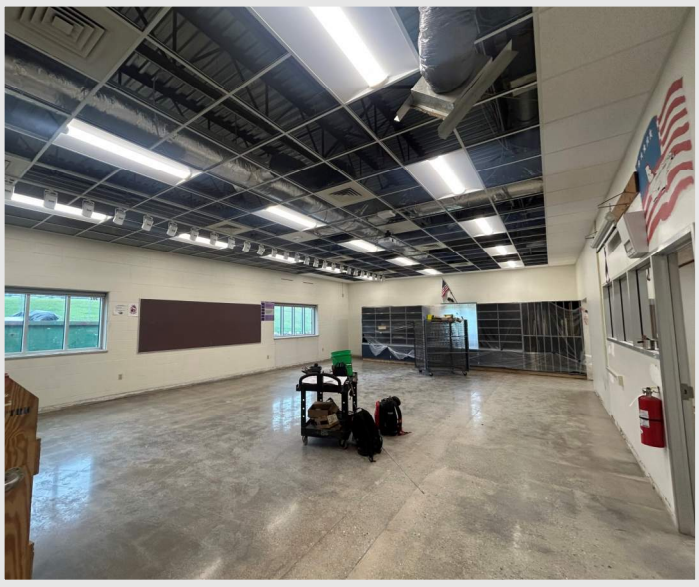

Bottom Left: a first look at the polished concrete finish in the High School art room

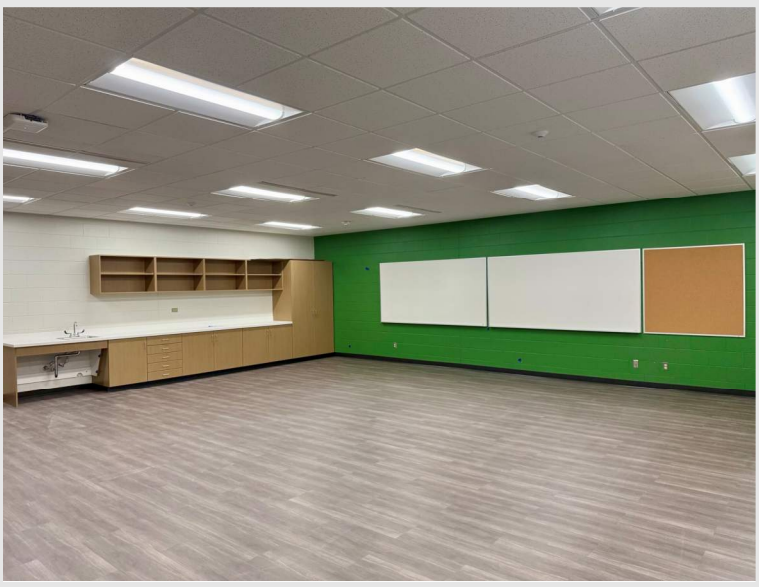

Bottom Right: another look at the progress in a classroom at Fox Prairie Elementary as finishes are completed

Questions?

Senior Project Manager, Matt Claggett / 608.729.2155 / mclaggett@findorff.com

Findorff
BUILDING & BEYOND
