Construction Field Report

Project Name: Classroom Addition at Grandview School **Field Report Number:** 40

Project Number: 4438 **Time:** 11:00 AM **Date of Observation:** 01/13/26

Weather Conditions: Mostly Sunny **Temperature Range:** 43° - H:45° L:28°

General Contractor: Pal-Pro Builders, LLC **Prepared By:** Frank Quagliotti

☐ Owner
☑ Architect
☐ Consultant
☐ Field

Work In Progress: **Est. % of Completion:** 35

Cold-applied roofing cap sheet, continuing progress of electrical plumbing and framing.

Observations:

- CFM framing between classrooms complete.
- Interior framing of soffits in progress.
- Cold-applied roofing cap sheet installation in progress.
- Roofing manufacturer conducted inspection of roof prior to cap sheet install.
- Rough electrical to be completed this week, preparing for electrical panel installation.
- Rough plumbing to be completed next week.

Follow-up Actions & Verifications Required:

- Plumbing, electrical and framing inspections to be conducted next week 1/20 & 1/22. GC to follow up upon completion.

35 waterview blvd • suite 303 • parsippany, nj 07054 • tel 973-256-0202 • fax 973-256-0227
• www.dicararubino.com •

Construction Field Report

PROJECT PHOTOS

DESCRIPTION





LOCATION:

Exterior Addition: Roof

DESCRIPTION:

Installation of cap sheet in progress.



LOCATION:

Interior Addition: Vestibule / Corridor

DESCRIPTION:

Interior CMU almost complete, installation of electrical panel in progress, rough electrical nearing end.

35 waterview blvd • suite 303 • parsippany, nj 07054 • tel 973-256-0202 • fax 973-256-0227
• www.dicararubino.com •

PROJECT PHOTOS

DESCRIPTION




LOCATION:

Interior Addition: Classroom

DESCRIPTION:

Framing installed for soffits in classrooms.

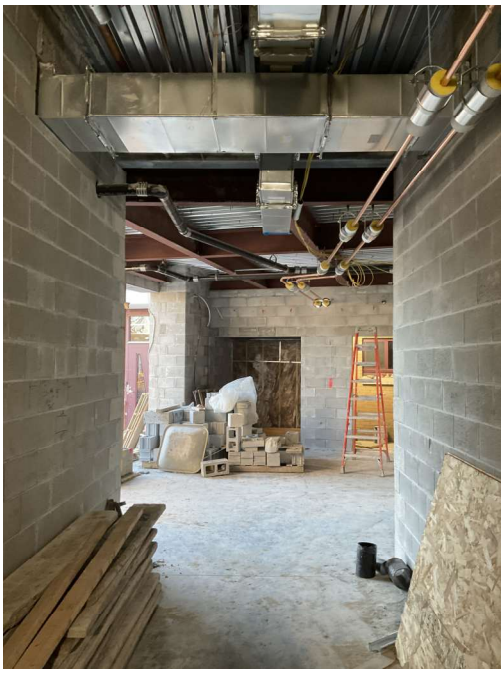

LOCATION:

Interior Addition: Corridor

DESCRIPTION:

Ductwork and piping installation nearing completion.

35 waterview blvd • suite 303 • parsippany, nj 07054 • tel 973-256-0202 • fax 973-256-0227
• www.dicararubino.com •
