Paul Laurence Dunbar High School – Roof Replacement


- **Completed/Work in Progress:**
  - Significant progress on area A and B on the classroom wing.
  - Good workmanship on SBS layer, Tremco representatives are happy with construction progress.
  - Demolition technique has been altered to allow for better screw removal and less mess during tear off.
  - Areas with slight drainage imperfections being remediated with additional membrane layers.
  - Site is generally clean and well maintained.
  - SBS crew has been doing regular checks within building for debris and water and addressing the situations as promptly as possible.

- **Upcoming Look Ahead:**
  - Additional SBS crew and masonry postponed another couple of weeks – accelerated progress expected upon their arrival.
  - Weather is hot and dry, roofers working at a steady pace, largely in the early morning hours to beat recent heat wave.
  - Architect and GC coordinating schedule and details for non-SBS trades.
  - Active construction is expected to continue at a steady pace.

Paul Laurence Dunbar High School – Roof Replacement

Overall shot of work area and detail of old meeting new roofing installation




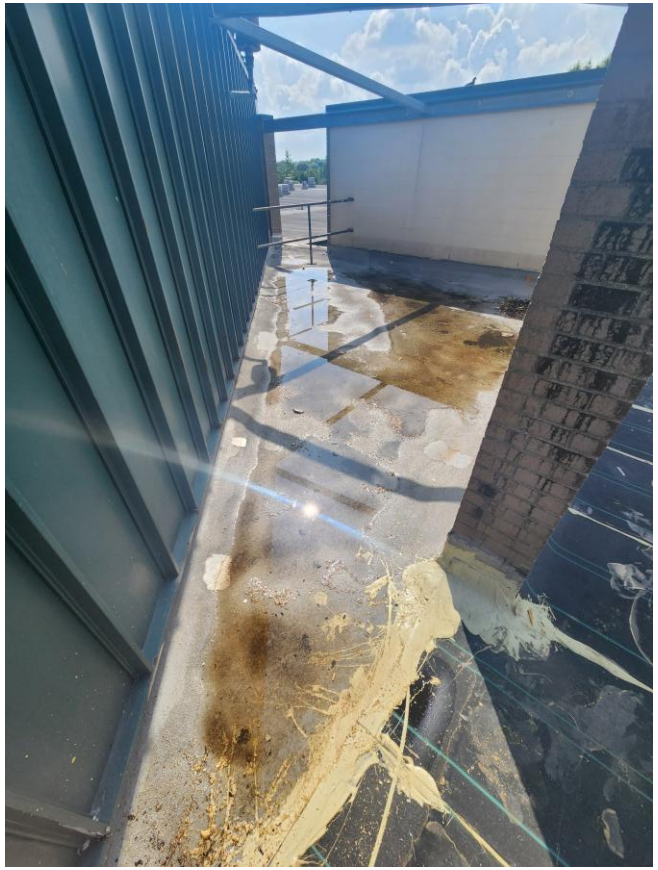

Paul Laurence Dunbar High School – Roof Replacement

Work underway and materials stored on site




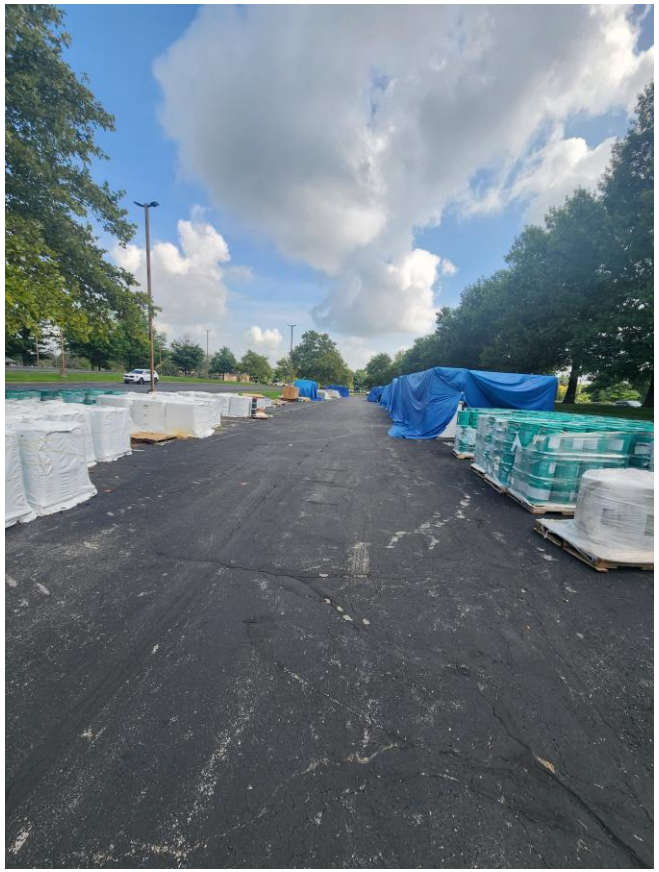

Paul Laurence Dunbar High School – Roof Replacement

Area ‘A’ and detail of area to receive additional membrane layer.



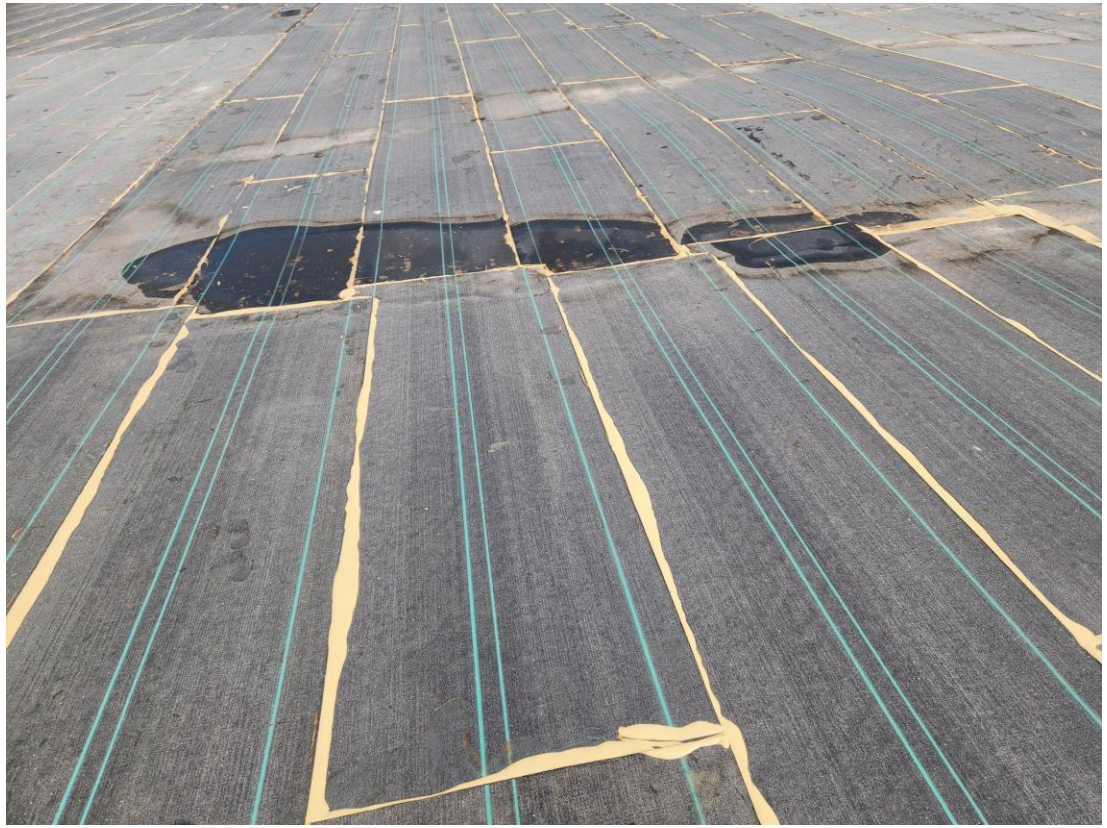

Paul Laurence Dunbar High School – Turf & Track Replacement

- **Completed/Work in Progress:**
  - Turf carpet installation is completed. Infill going on.
  - Some grading work has taken place in the lawn areas. Existing storm drains are being brought up to grade.
  - Sidewalk pouring is going on.

- **Upcoming Look Ahead:**
  - Concrete walk installation continues.
  - Entry drive paving to begin soon.
  - Track surface coating to be installed soon.
  - Site grading to continue.
  - Shotput pit installation to begin.

Paul Laurence Dunbar High School – Turf & Track Replacement

Turf Installation




Paul Laurence Dunbar High School – Turf & Track Replacement

PLD Logo at Center Field



Paul Laurence Dunbar High School – Turf & Track Replacement

Work In Progress at Jump Pit

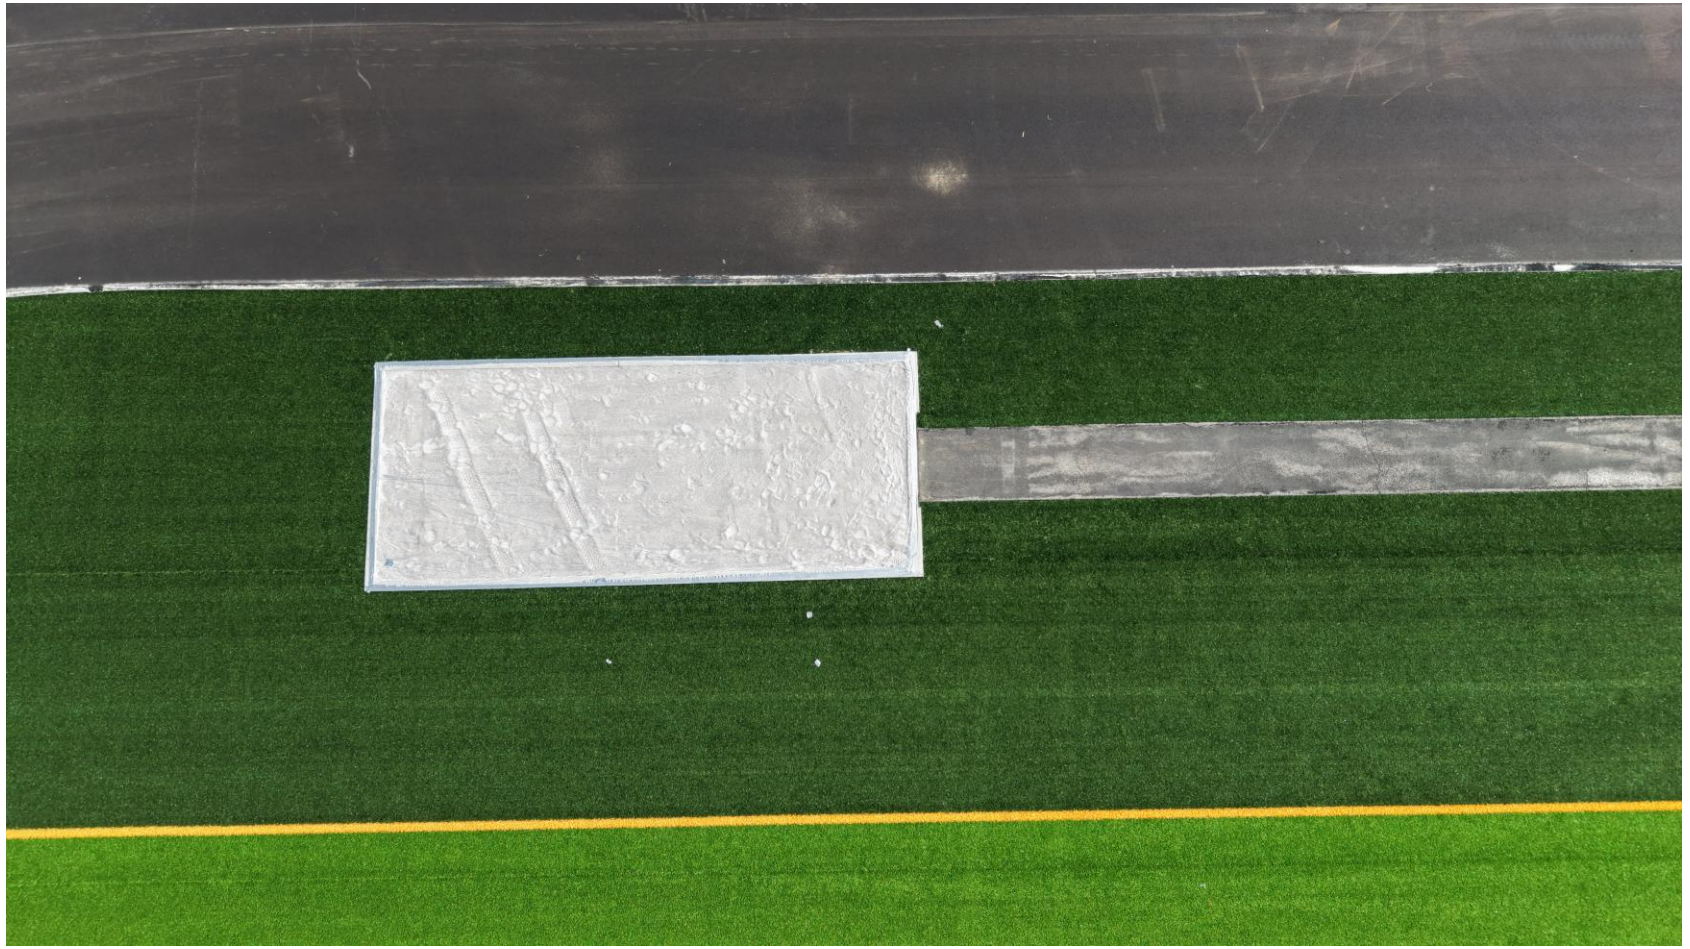

Paul Laurence Dunbar High School – Turf & Track Replacement

Various works around the site

