Lake Mills High School
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

615 Catlin Dr., Lake Mills, Wi 53551 09/04/2026


What's New?

The excitement is building as this project continues to transform before our eyes! We've reached several exciting milestones across the site, including completion of the lower-level corridor lockers, locker room lockers, and new doors, frames, and hardware. New display case framing is in place, and Room 117 is coming together with new wood paneling. Major structural progress is also underway with the north steel structure and CMU firewall complete. In Area A, interior rough grading and rough excavation for the bio-retention pond are moving forward, creating even more momentum as the building continues to take shape.

And there's no slowing down! Coming up, crews will continue with the Area A lobby steel structure and precast floors, roof joists for the lobby and gym storage areas, and continued CMU wall construction throughout Area A. The precast topping slab pour and continued work in Room 117 will bring us even closer to completion. With every beam, wall, finish, and detail, we're getting closer to seeing this vision become a reality. The transformation is happening fast, and we can't wait to see what's next!



Drone photo from August 28th

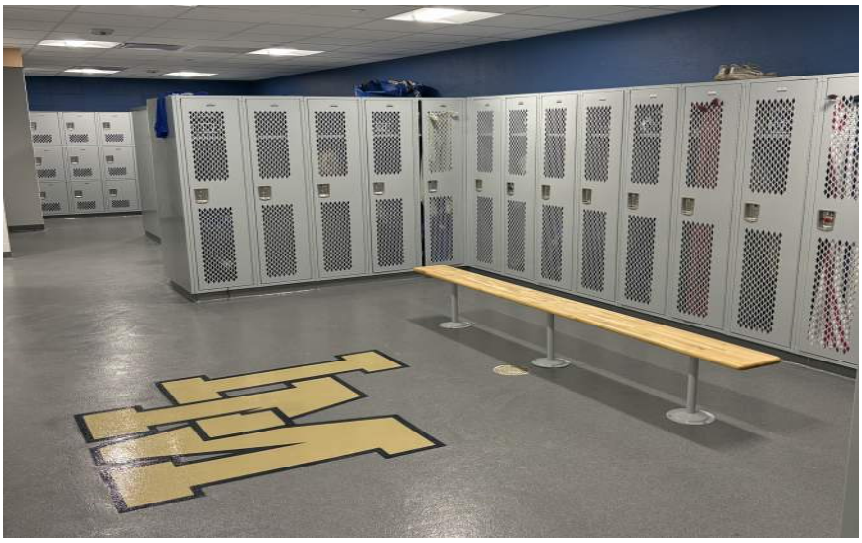

Finished Men's Team Locker Room

DID YOU KNOW?

Concrete masonry doesn't burn. Depending on the thickness of the wall, the density of the units, and the amount of grout used, concrete masonry walls can provide up to a 4-hour fire rating. Plus, concrete masonry walls pass the hose stream test, which is an integral part of many fire testing standards, and indicates an even greater level of redundancy and resiliency.

Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND

Lake Mills High School
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

Completed Work!

- Lower-level corridor lockers
- Locker room lockers
- Lower-level new doors, frames, and hardware
- New framing for display cases
- Wood paneling for room 117
- North steel structure
- CMU firewall
- Area A interior rough grading
- Rough excavation for the bio retention pond



Above: Area A west CMU walls



Left: Area A firewall and CMU walls for the lobby area

Below: Area A north steel structure



Work Coming Up

- Area A lobby steel structure
- Area A lobby precast floors
- Area A lobby and gym storage roof joists
- Continue laying Area A CMU walls
- Pour precast topping slab
- Finish room 117

Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND

Lake Mills High School
EXECUTIVE SUMMARY

PROVIDED BY FINDORFF



Progress on Room 117



New corridor lockers installed



Storm structure installed with rough pond excavation

Questions?

Sr Project Manager: Menno Huiser / mhuiser@findorff.com
Project Engineer: Ben Neumann / bneumann@findorff.com
Superintendent: Dave Ritter / dritter@findorff.com

Findorff
BUILDING & BEYOND
