
Paul Laurence Dunbar High School – Roof Replacement

- **Completed/Work in Progress:**
  - Gymnasium is based in.
  - Corridor over cafeteria is largely based-in.
  - MAUs are raised on new curbs.
  - MAU lines are prepared to be reconnected.

- **Upcoming Look Ahead:**
  - Continue SBS work over area ‘C’
  - Cap sheet and flashing installations.
  - Coping and sheet metal installation.
  - Cap sheet on Gymnasium.
  - Standing seam roofing delivery by early next month.

Paul Laurence Dunbar High School – Roof Replacement

Work in progress over gymnasium corridor.

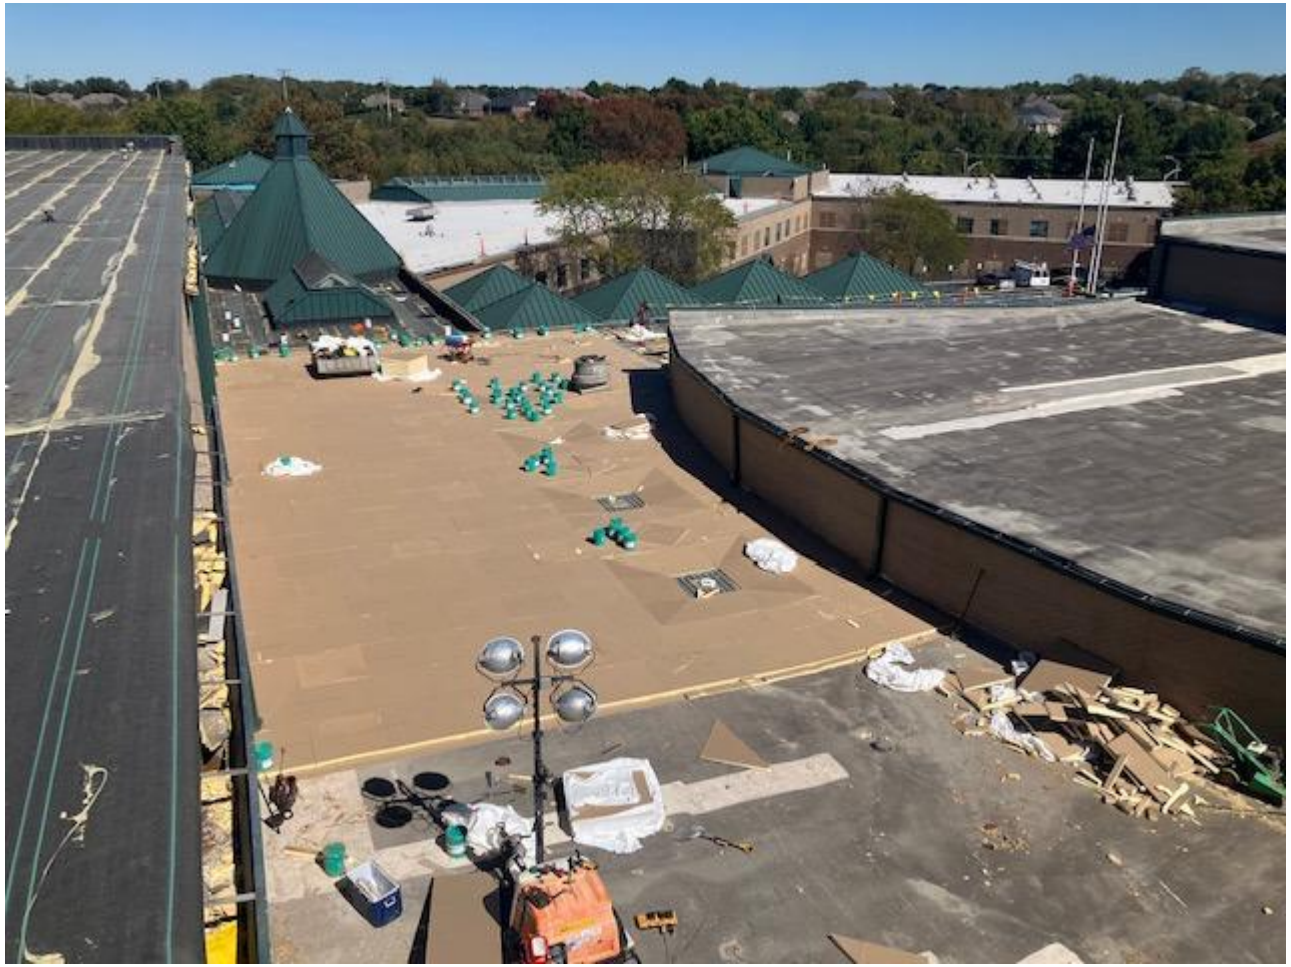

Paul Laurence Dunbar High School – Roof Replacement

Base in adjacent to auditorium awaiting high wall flashing.



Paul Laurence Dunbar High School – Roof Replacement

Close-up of insulation attachment washer and shot of base-in by front entrance.





Paul Laurence Dunbar High School – Roof Replacement

New support construction for AHUs at cafeteria.



Paul Laurence Dunbar High School – Roof Replacement

AHUs over cafeteria on new supports with new support flashing.



Paul Laurence Dunbar High School – Roof Replacement

New pan leading to existing roof drain.



Paul Laurence Dunbar High School – Roof Replacement

New high wall flashing over areas A/B.



Paul Laurence Dunbar High School – Roof Replacement

MAU PNG Supply line being prepared for reconnection.

