Paul Laurence Dunbar High School – Roof Replacement

- **Completed/Work in Progress:**
  - Base-In is 99% Complete for all roof areas requiring SBS roofing.
  - Cap sheet on areas A and B are 95% complete.
  - Roof edge work in progress.
  - Penthouses receiving new insulation.
  - Gutter installation has started on area C.

- **Upcoming Look Ahead:**
  - Masonry thru wall work on area ‘C’.
  - Small area of area ‘C’ to be based-in.
  - Edge metal installation.
  - Continue gutters and downspouts.
  - Standing seam delivery.

Paul Laurence Dunbar High School – Roof Replacement

Overall shot of Dunbar Roof.



Paul Laurence Dunbar High School – Roof Replacement

Mechanical air unit with re-installed and raised gas line.



Paul Laurence Dunbar High School – Roof Replacement

Roof edge being prepared for edge metal.




Paul Laurence Dunbar High School – Roof Replacement

Penthouse receiving new mineral fiber insulation before weather barrier and plywood installation.



Paul Laurence Dunbar High School – Roof Replacement

Old fiberglass insulation being removed from penthouse walls.

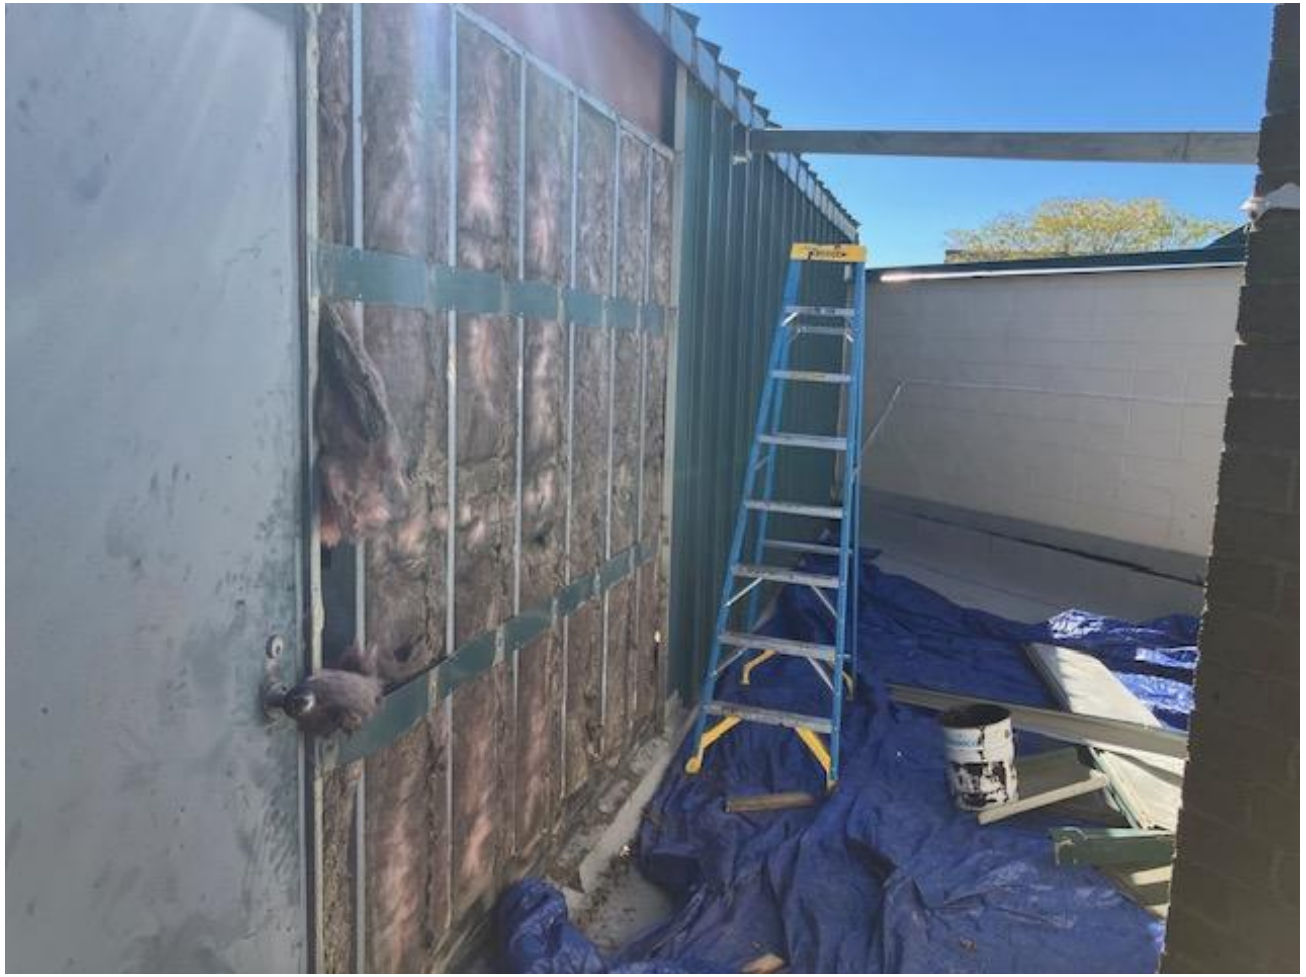

Paul Laurence Dunbar High School – Roof Replacement

Overall shot of area C with base sheet.



Paul Laurence Dunbar High School – Roof Replacement

Low roof on area C receiving mod-bit base in.



Paul Laurence Dunbar High School – Roof Replacement

Auditorium roof edge on area C receiving new gutter.

