Paul Laurence Dunbar High School – Roof Replacement

- **Completed/Work in Progress:**
  - Base-In fully complete for areas with SBS roofing.
  - Cap sheet on areas A and B are complete.
  - Cap sheet on area C and roof edge work in progress.

- **Upcoming Look Ahead:**
  - Finish capping area C.
  - Roof edge metals installation.
  - Thru wall on area C.
  - Standing seam delivery.

Paul Laurence Dunbar High School – Roof Replacement

Shot of area C from Gymnasium and detail of auditorium edge.





Paul Laurence Dunbar High School – Roof Replacement

Workers on auditorium roof installing cap sheet.



Paul Laurence Dunbar High School – Roof Replacement

Roof edge detail over stage area.



Paul Laurence Dunbar High School – Roof Replacement

Cap sheets being relaxed and installed using adhesive and propane.




Paul Laurence Dunbar High School – Roof Replacement

New roof drain and SBS roofing over penthouse area.



Paul Laurence Dunbar High School – Roof Replacement

Final area of insulation being installed in preparation for base and cap sheet.

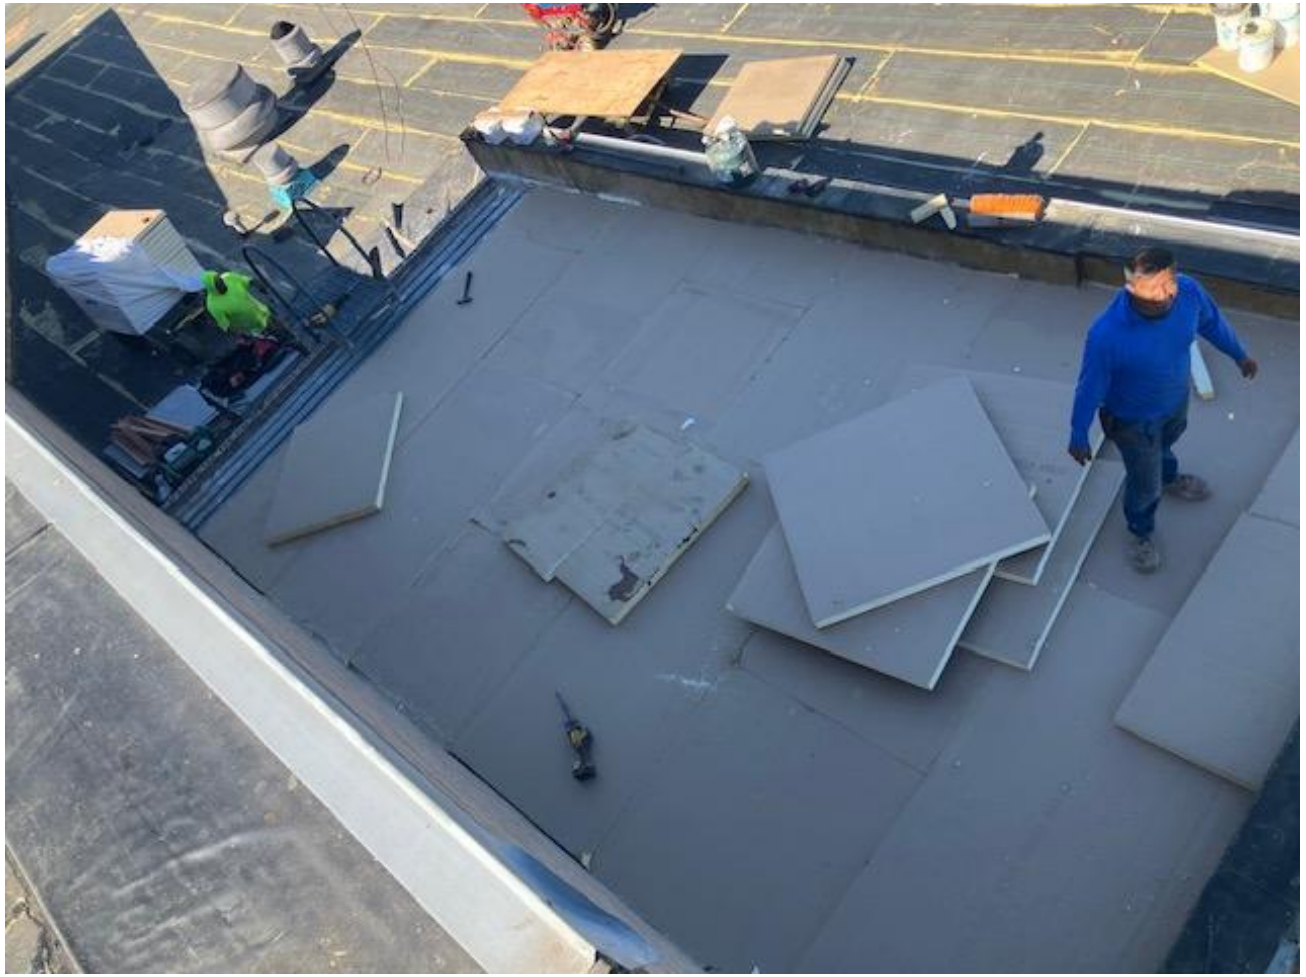

Paul Laurence Dunbar High School – Roof Replacement

Aluminization on mechanical flashings.



Paul Laurence Dunbar High School – Roof Replacement

Sheathing and weather barrier over mechanical penthouses.

