



Projects Update

February 22, 2021

Bond 2017 Project:
Leadership Support Center

Bond 2020 Projects:
ES North Classroom Addition
ES South Classroom Addition

Bond 2020 Projects:
Intermediate School North
Intermediate School South



PROJECT SCHEDULE

COMPLETE - Package 1: Demolition, Earthwork, Building Pad and Underground Utilities

- Demolition – Complete

January 15th – March 15th 2020

COMPLETE - Package 2: Foundation, Structural Steel Purchase and MEP Underslab

- Building Pad: Completed on Schedule:
- Drill & Pour Foundation Piers/Grade Beams Complete:
 - *PCI to give status update of project time line*

Package 3: Remaining Building Package

- Construction Documents Issue for Proposal: Complete April 6th 2020
- Issue for Permit: Complete April 9th 2020
- Develop GMP present to BOT for Approval/Award: Complete May 18th 2020
- Construction Start - Substantial Completion: May 19th 2020 - June 15th 2021
- Move – In: July 15th 2021



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



LSC – Hall of History

BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER



BOND 2017 – LEADERSHIP SUPPORT CENTER




BOND 2017 – LEADERSHIP SUPPORT CENTER



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS

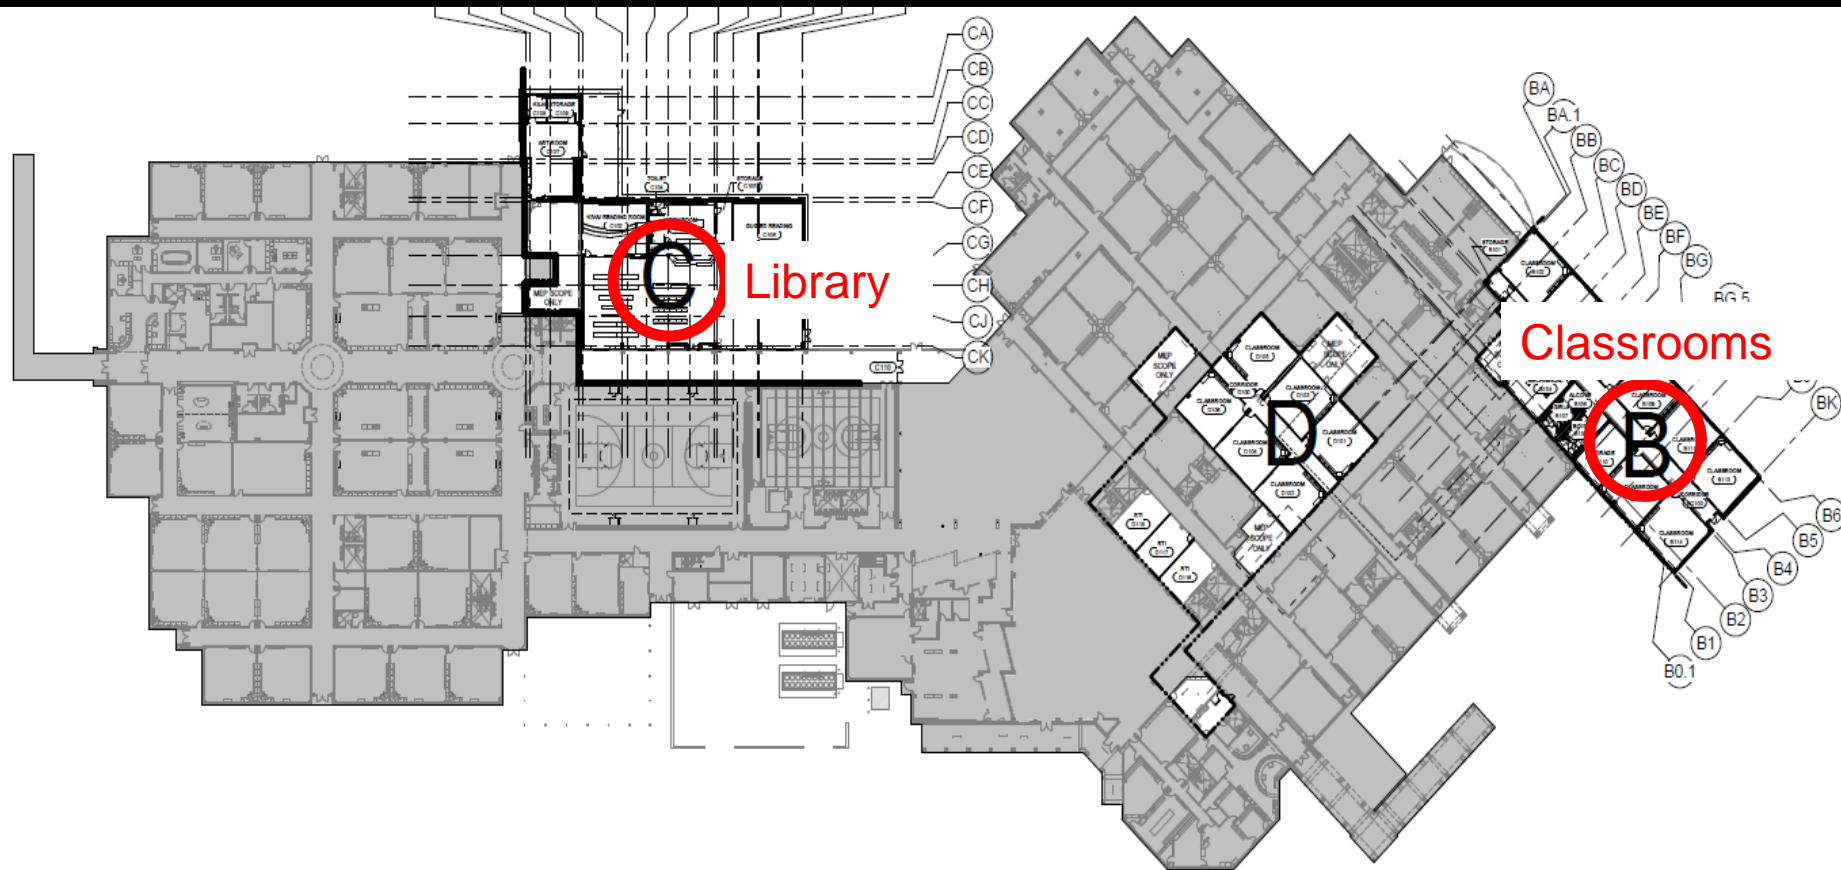

PHASING SCHEDULE

PHASE 1: AREA B & C
WORK TO BEGIN SUMMER 2020

PHASE 2: AREA D
WORK TO BEGIN SUMMER 2021

ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS




ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS



ELEMENTARY SCHOOL SOUTH CLASSROOM - LIBRARY ADDITIONS

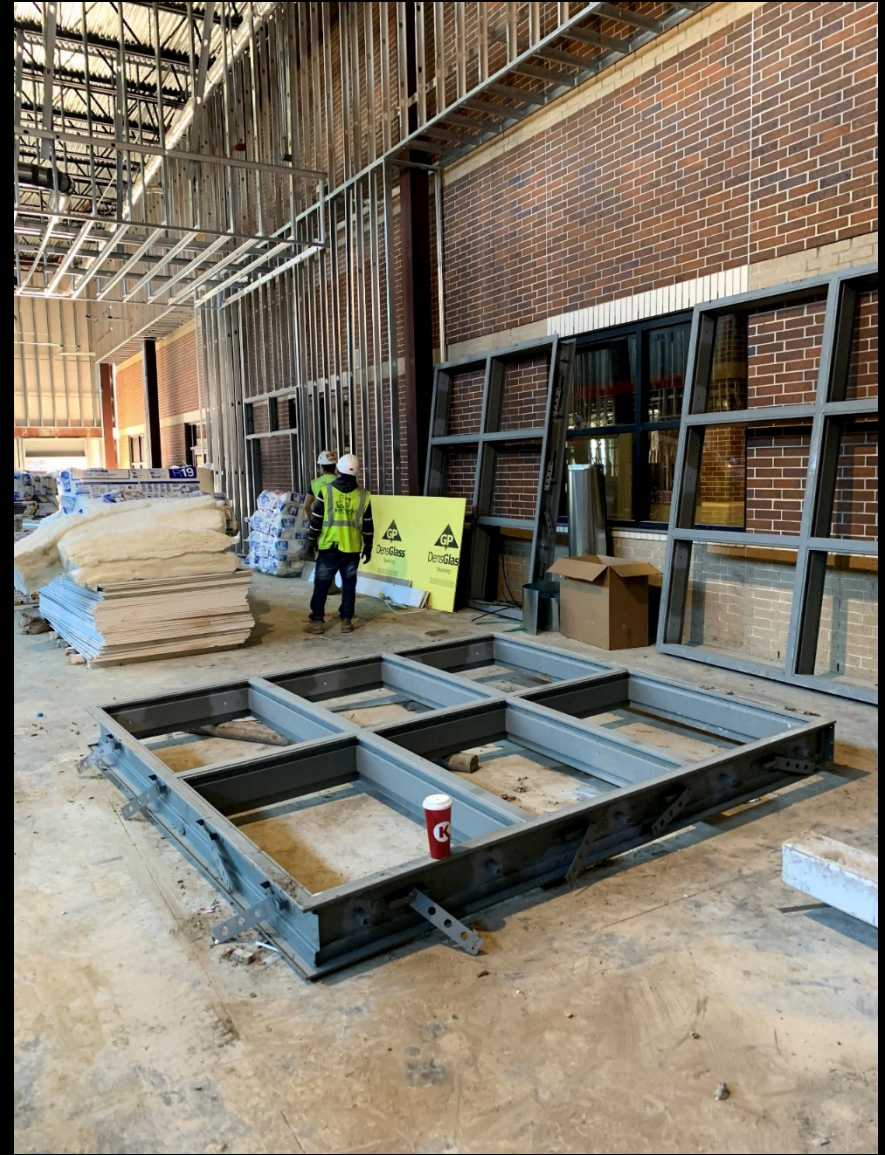


ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY NORTH ADDITIONS

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS

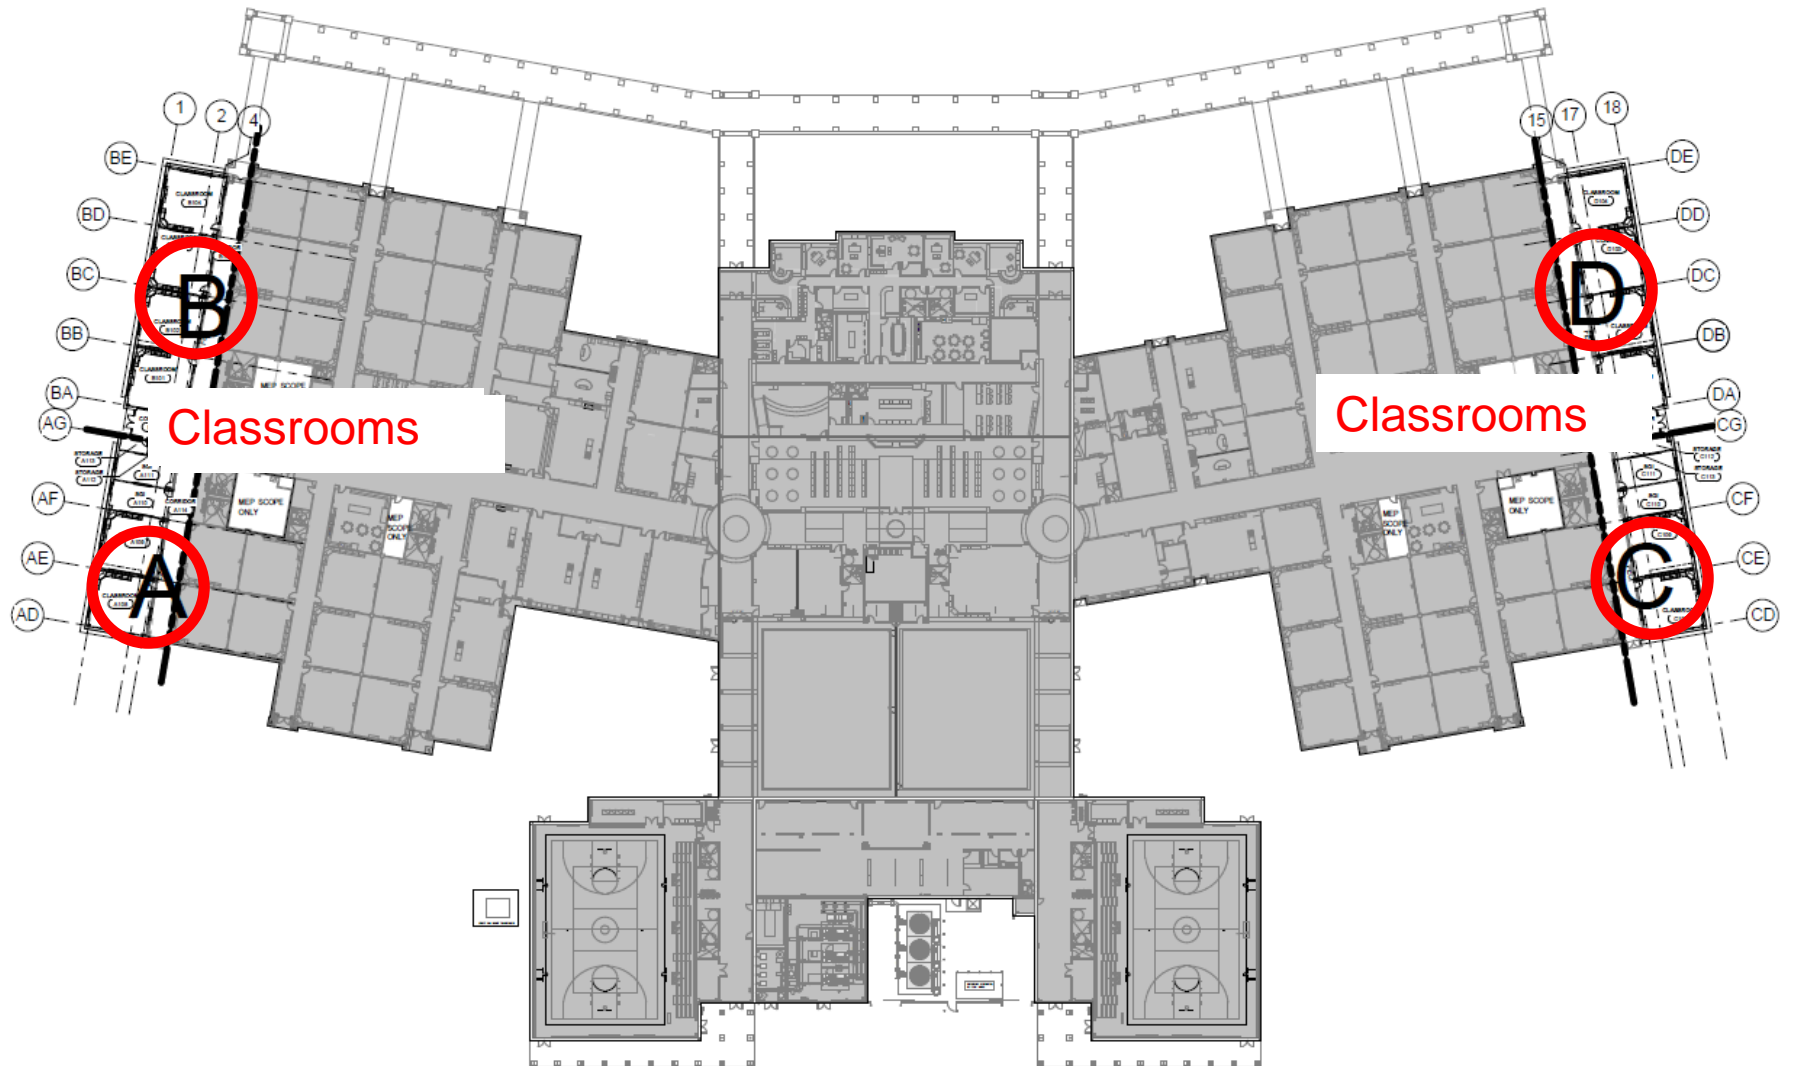

ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS




BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



INTERMEDIATE SCHOOL SOUTH



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN

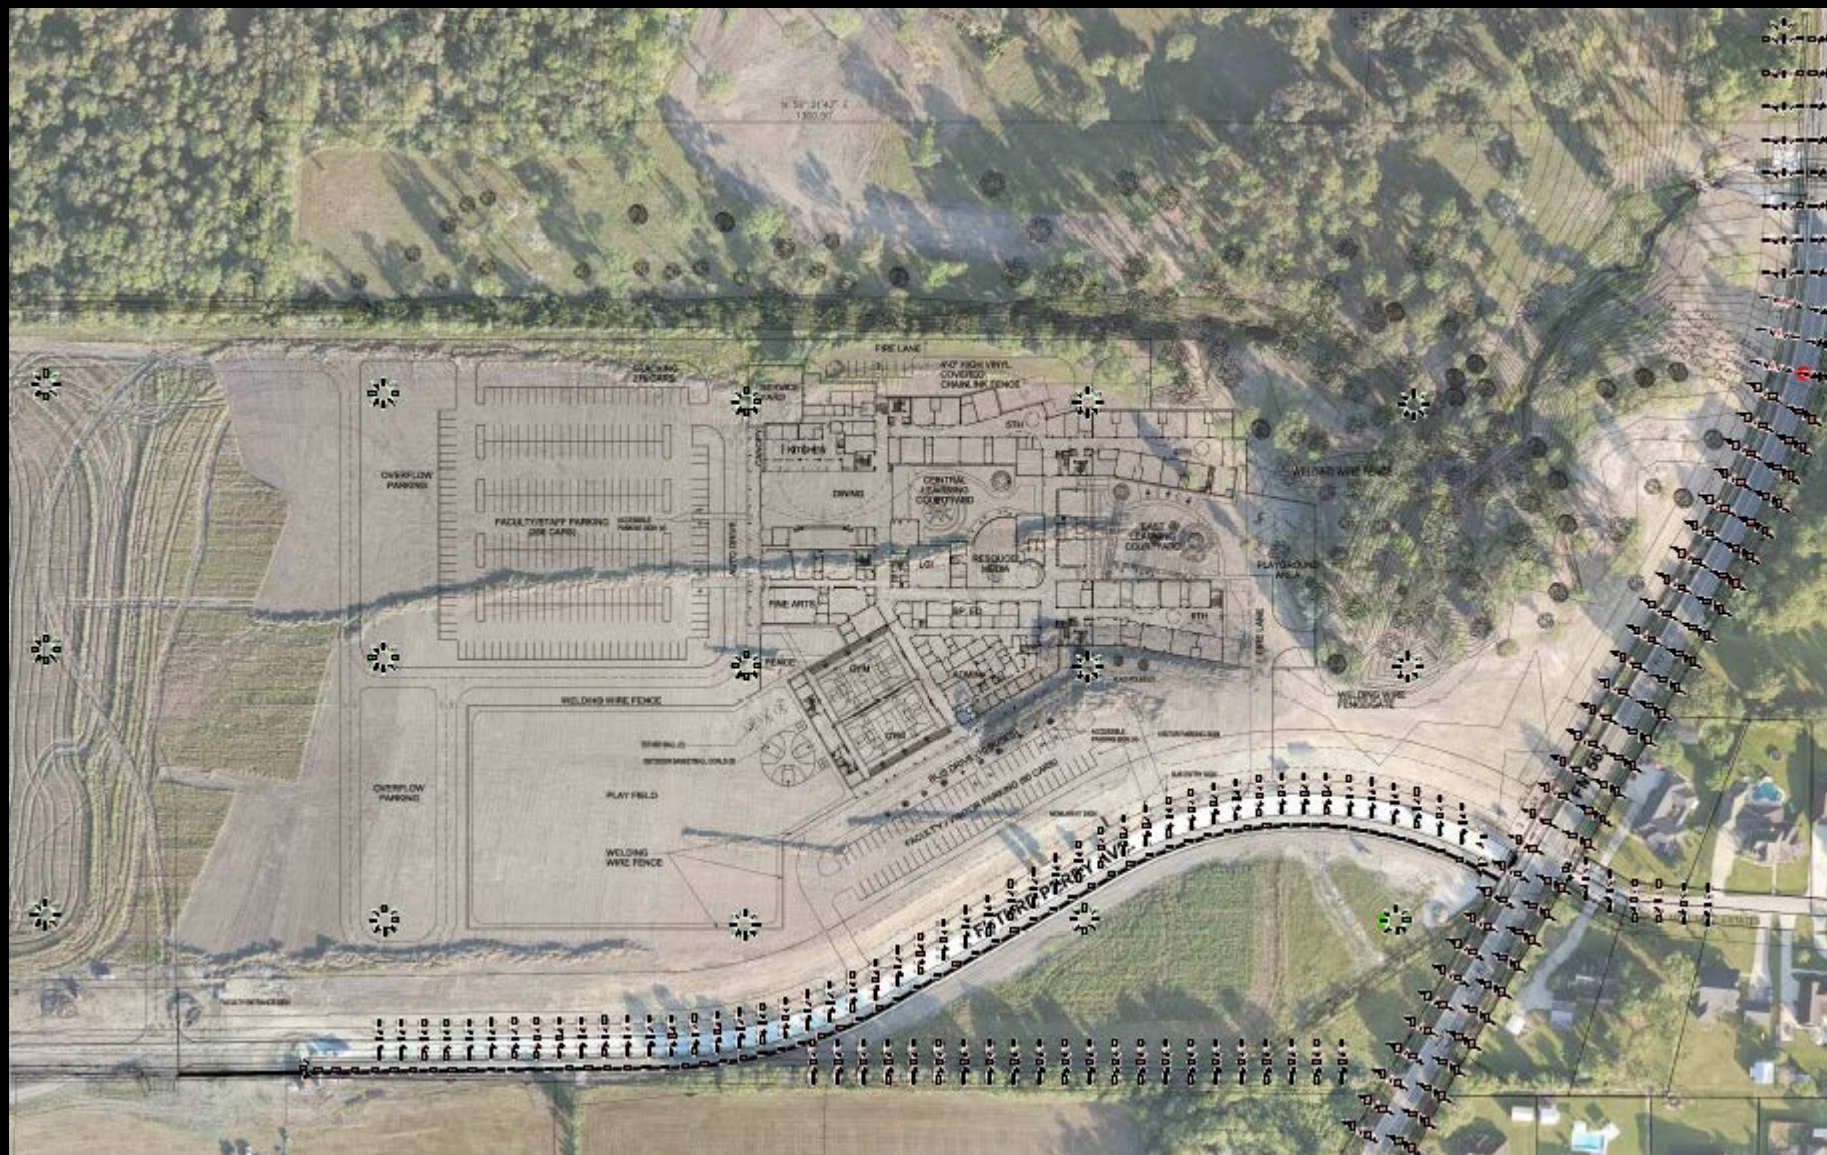

BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – ISS – ARBORIST TREE PRESERVATION



BOND 2020 – ISS – ARBORIST TREE PRESERVATION



BOND 2020 – INTERMEDIATE SCHOOL SOUTH - SITE PLAN



BOND 2020 – ISS – ARBORIST TREE PRESERVATION



BOND 2020 – ISS – ARBORIST TREE PRESERVATION




BOND 2020 – ISS – ARBORIST TREE PRESERVATION



BOND 2020 – INTERMEDIATE SCHOOL NORTH - SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN

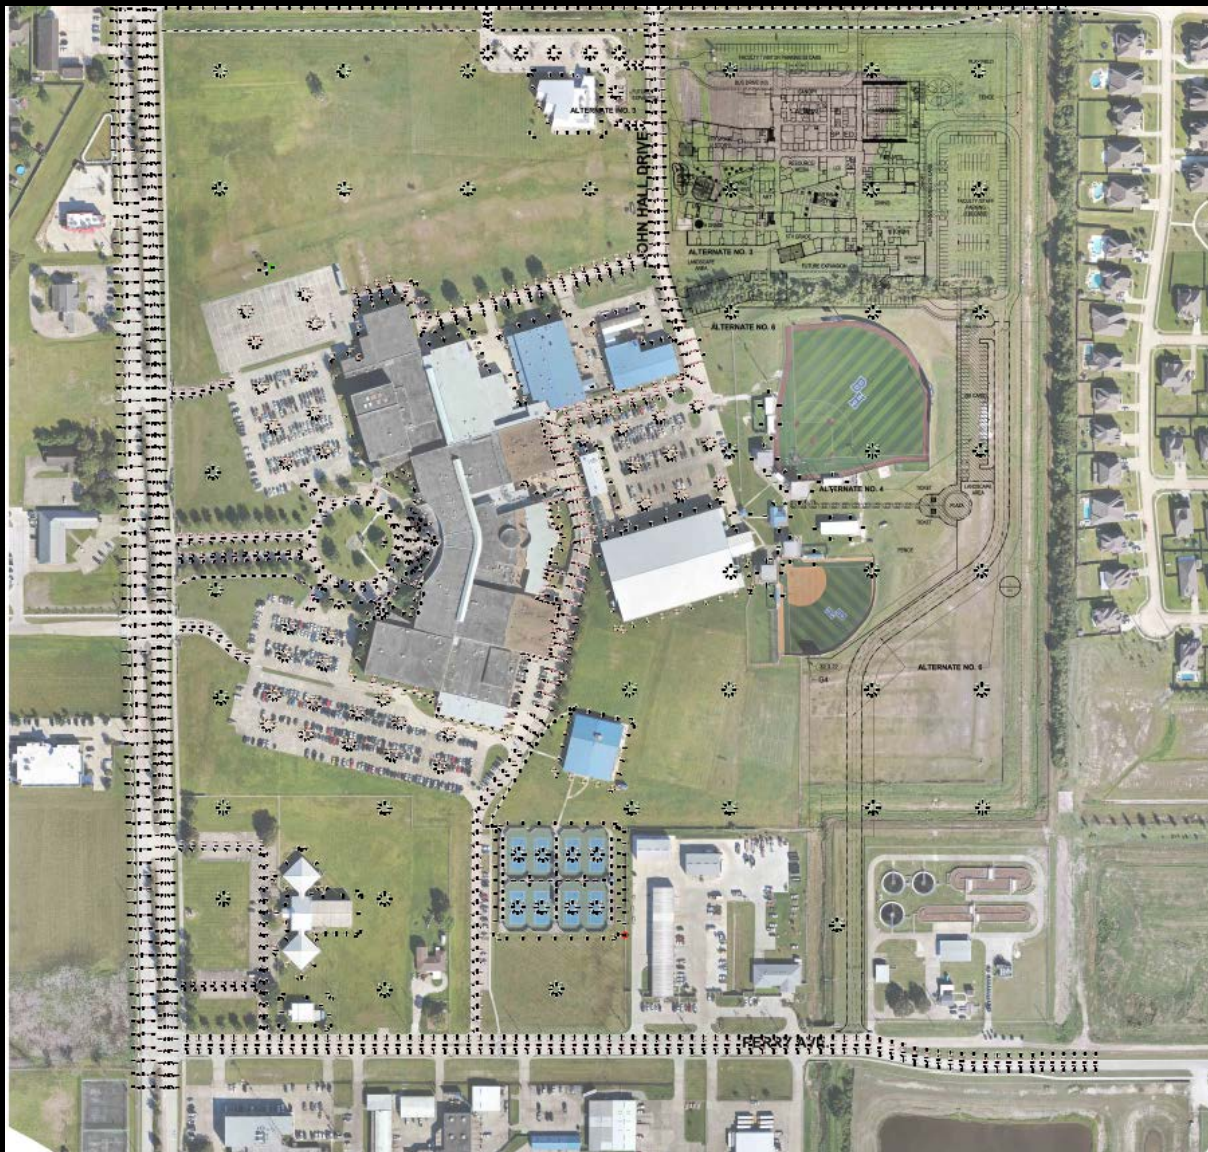

BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



Intermediate School North – Grade Beams and Underground Utilities



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN



BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN




BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN




BOND 2020 – INTERMEDIATE SCHOOL NORTH – SITE PLAN






ARTIFICIAL TURF REPLACEMENT EAGLE STADIUM

 **BOND 2020**
FACILITY PRESERVATION

ACTION ITEM - BOND 2020 – FACILITY PRESERVATION – REPLACEMENT OF ARTIFICIAL TURF AT EAGLE STADIUM – FIELD LAYOUT

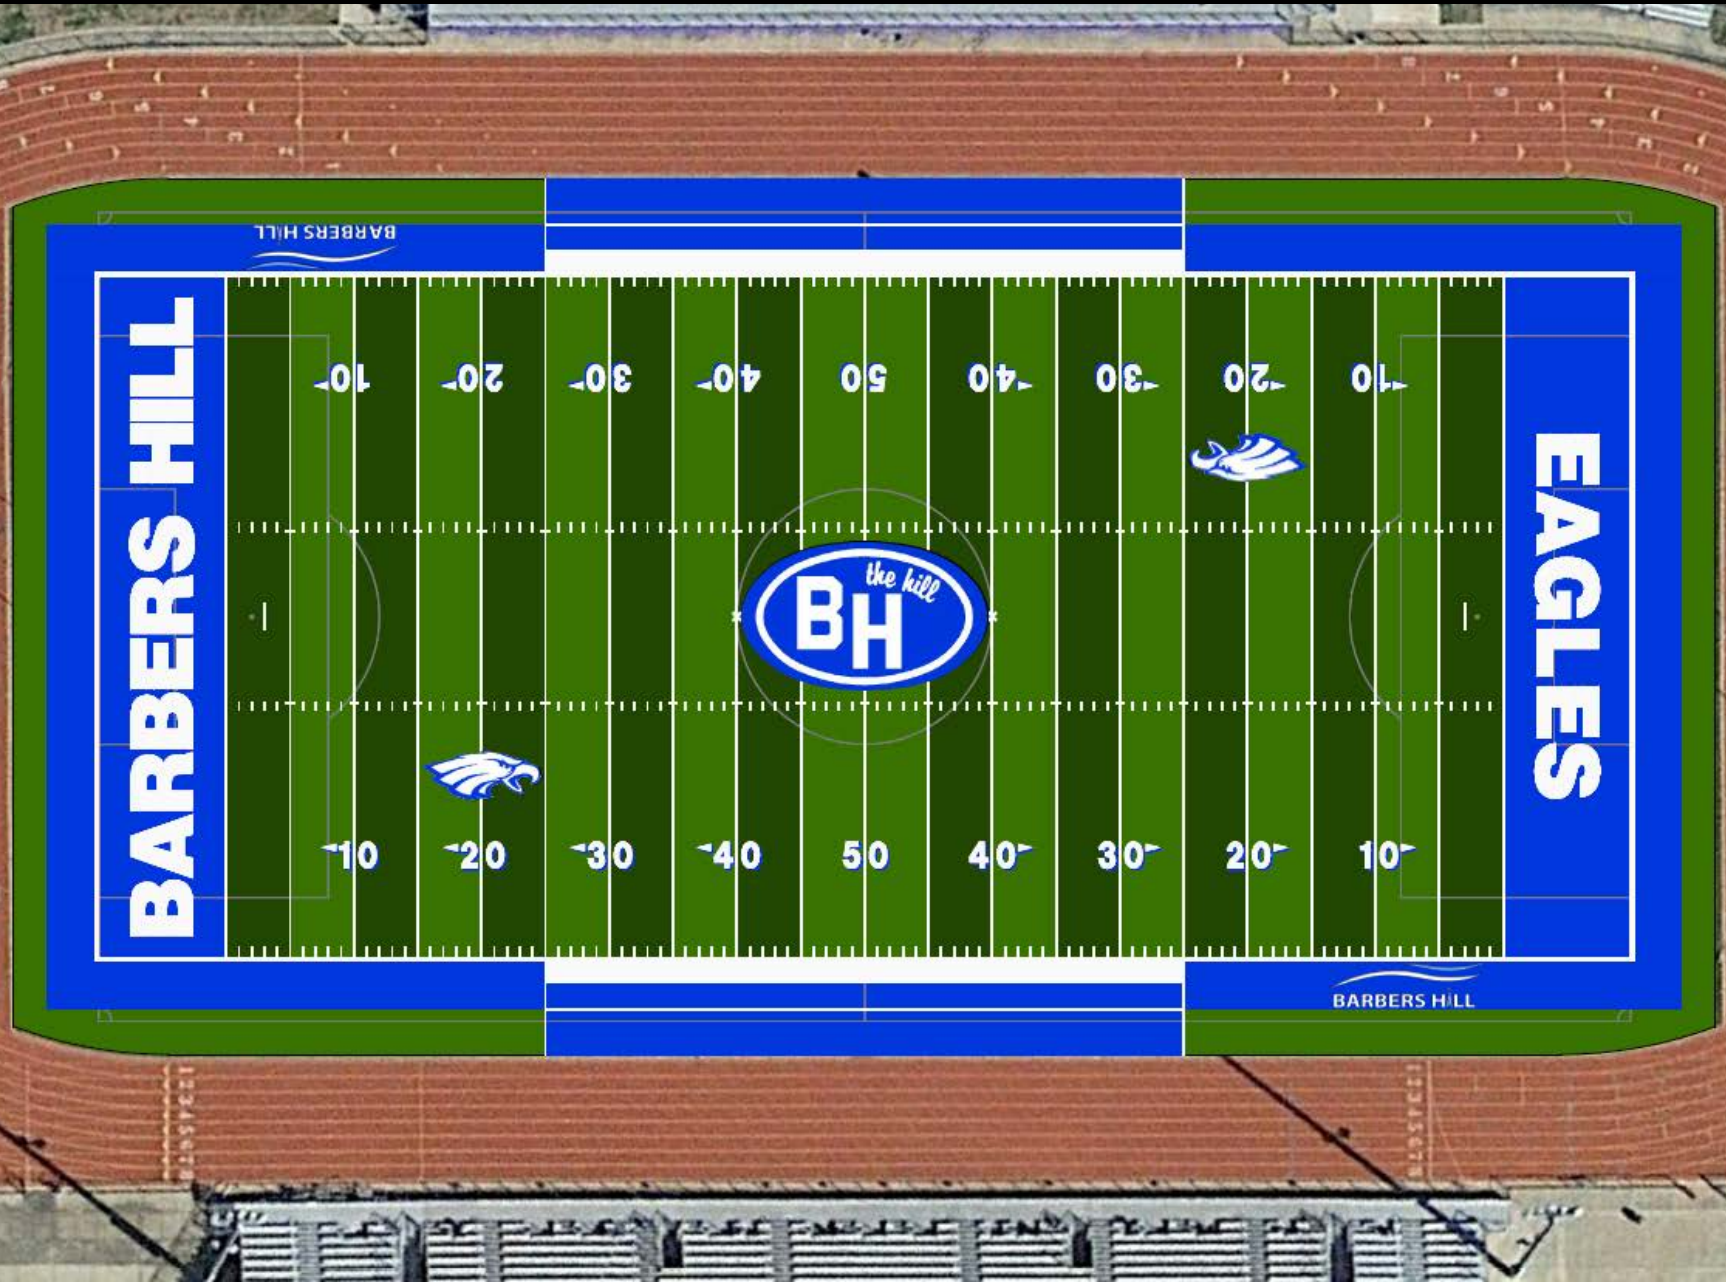



BARBERS HILL

Independent School District



PowerPro 65

QUIETECH
THIRD PARTY LOGO

AIRMAN

WINTER STORM DAMAGE WEEK OF 2-15-2021

WINTER STORM DAMAGE – WEEK OF 2-16-21




WINTER STORM DAMAGE – WEEK OF 2-16-21



WINTER STORM DAMAGE – WEEK OF 2-16-21 TECHNOLOGY/MAINTENANCE



WINTER STORM DAMAGE – WEEK OF 2-16-21 TECHNOLOGY/MAINTENANCE

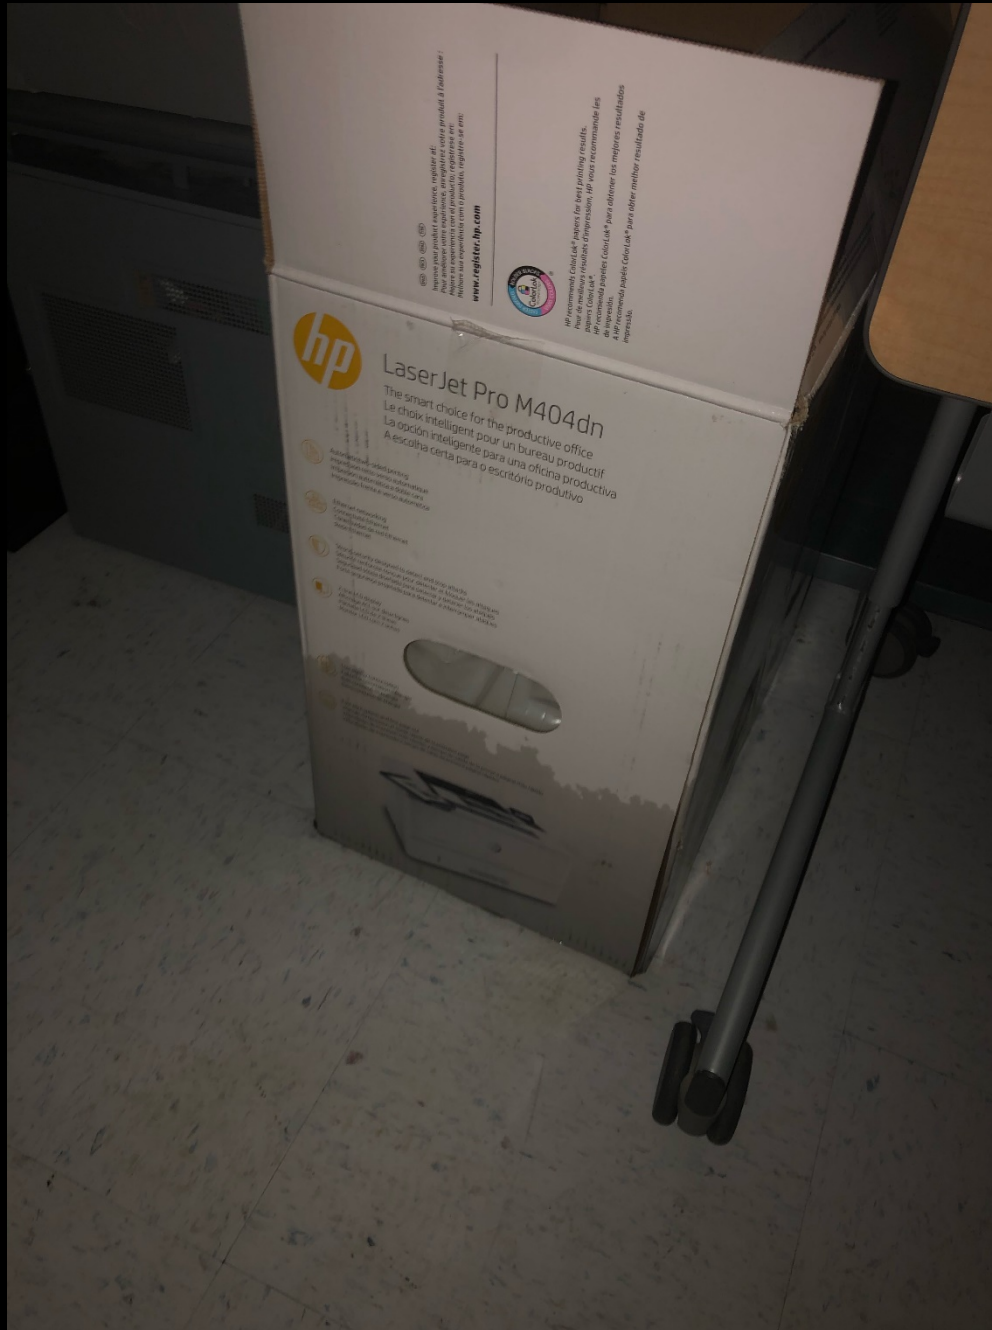


WINTER STORM DAMAGE – WEEK OF 2-16-21 TECHNOLOGY/MAINTENANCE



WINTER STORM DAMAGE – WEEK OF 2-16-21 TECHNOLOGY/MAINTENANCE



WINTER STORM DAMAGE – WEEK OF 2-16-21 TECHNOLOGY/MAINTENANCE

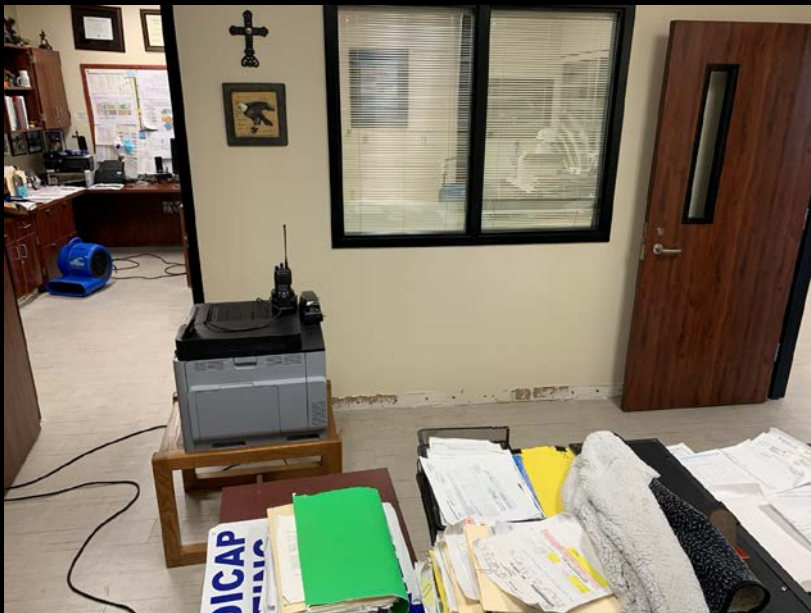

WINTER STORM DAMAGE – WEEK OF 2-16-21 TECHNOLOGY/MAINTENANCE




WINTER STORM DAMAGE – WEEK OF 2-16-21 MSS BAND ROOM




WINTER STORM DAMAGE – WEEK OF 2-16-21 MSS BAND ROOM




WINTER STORM DAMAGE – WEEK OF 2-16-21 MSN SCIENCE WING

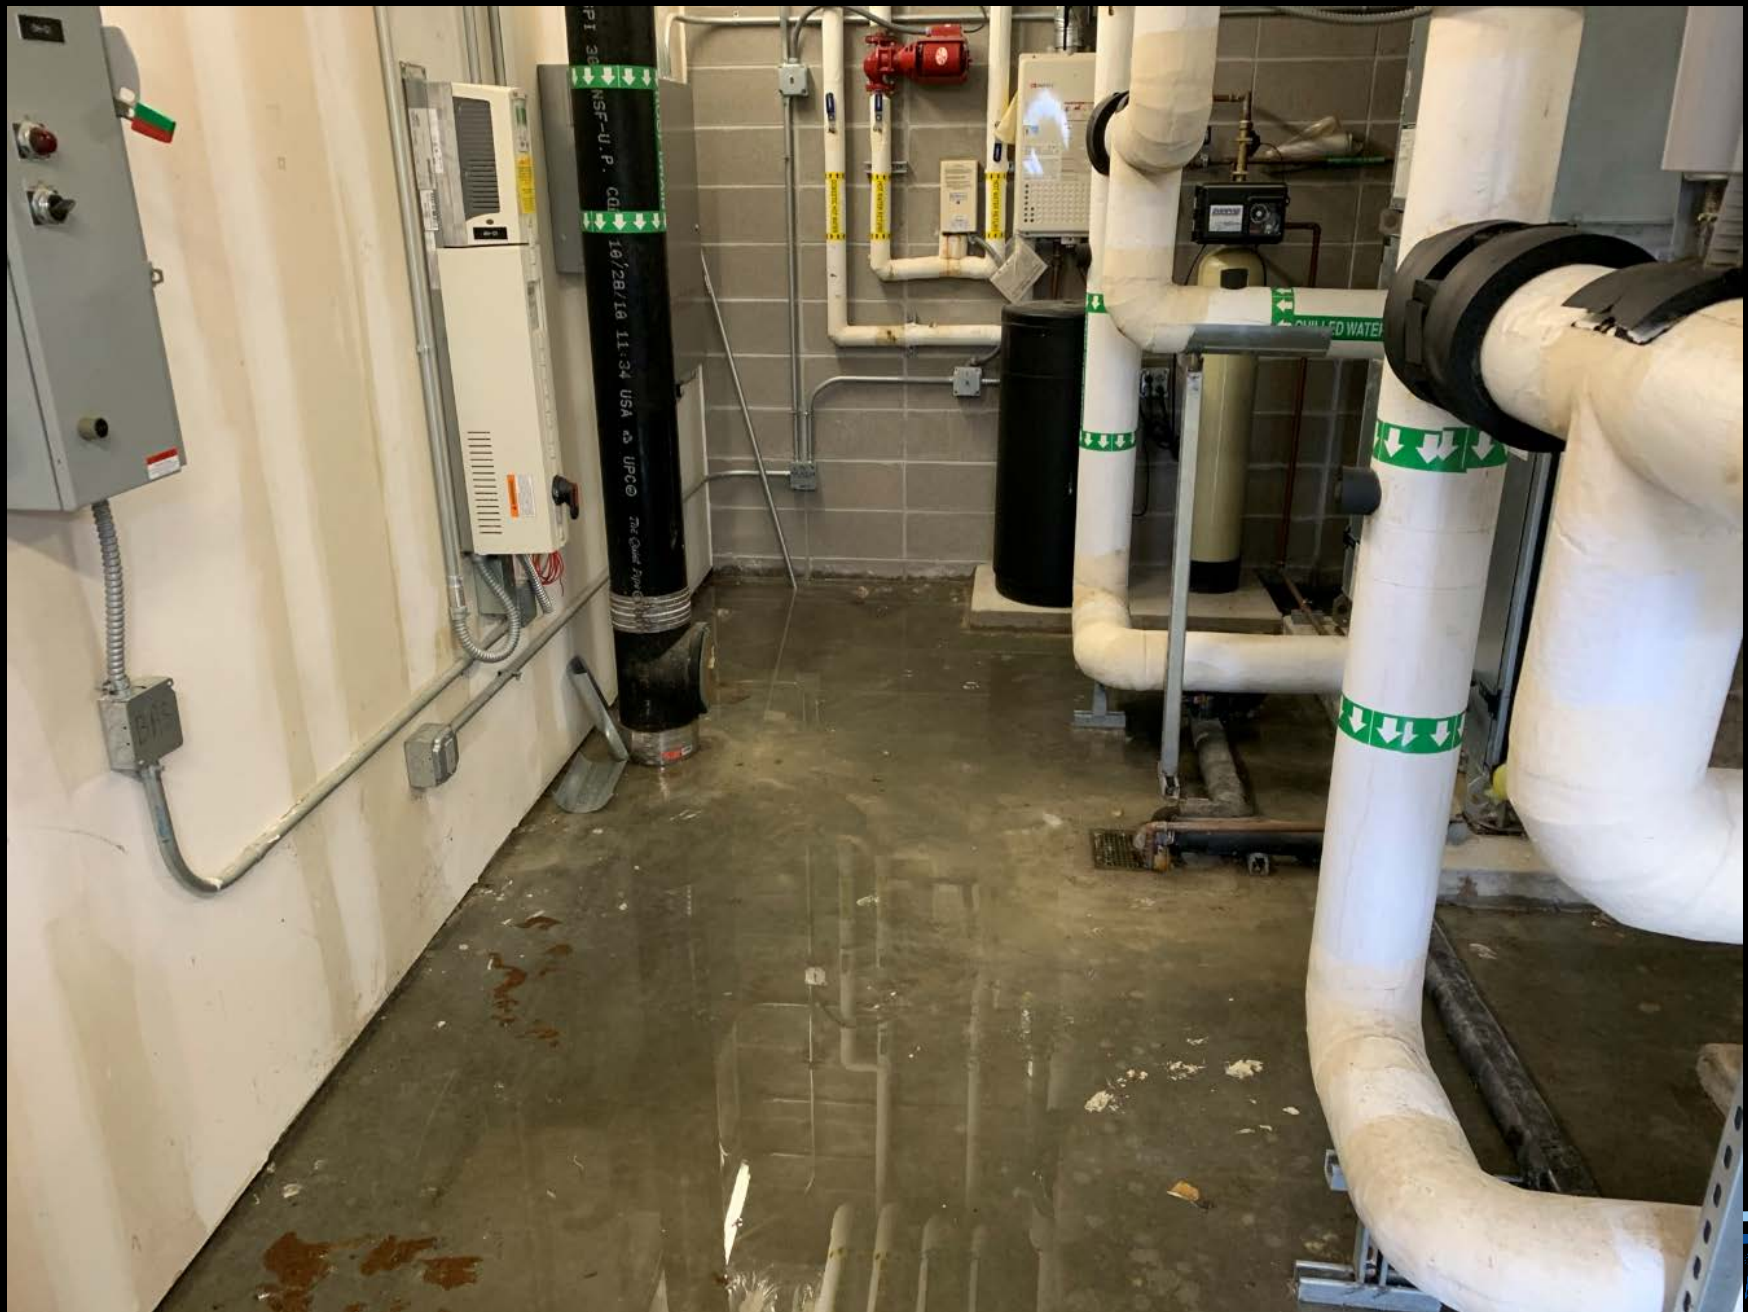


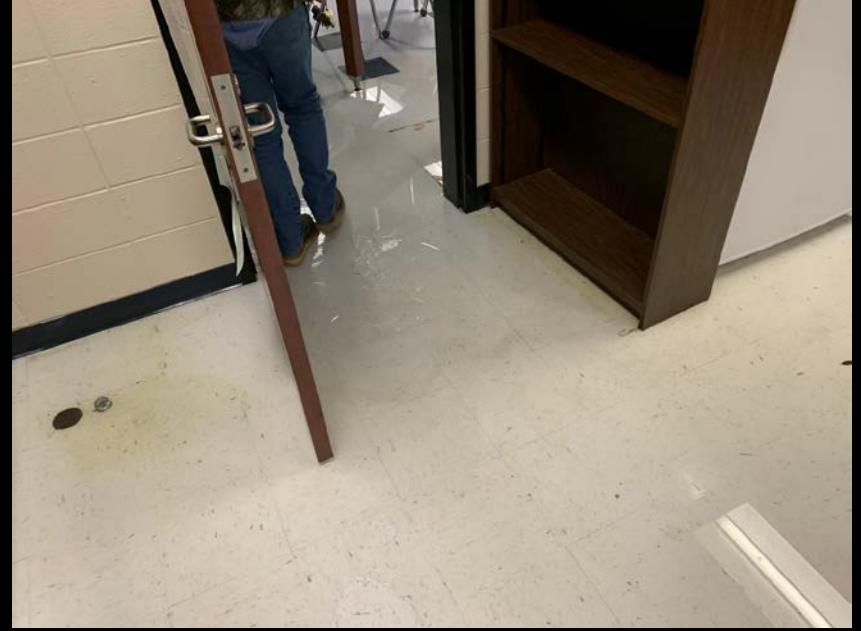

WINTER STORM DAMAGE – WEEK OF 2-16-21 MSN SCIENCE WING

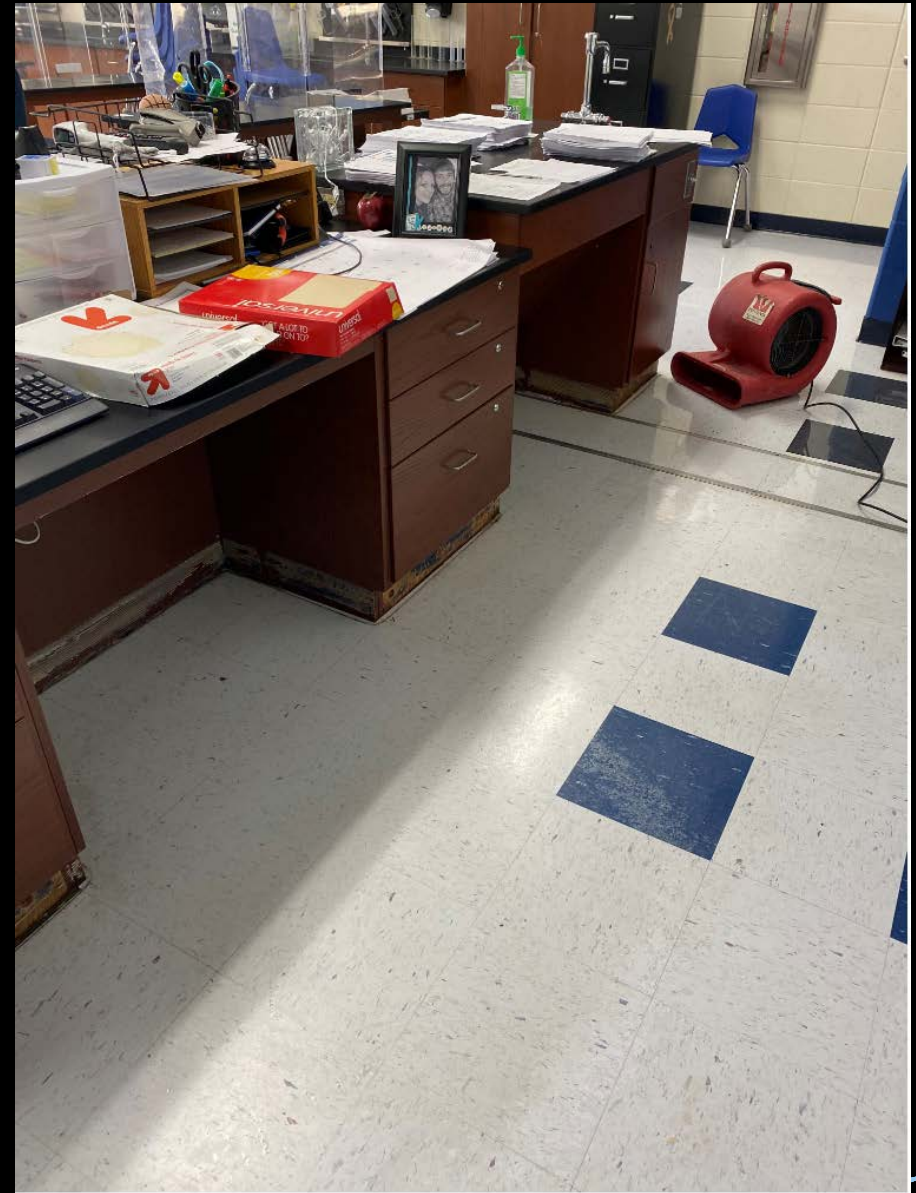

WINTER STORM DAMAGE – WEEK OF 2-16-21 MSN SCIENCE WING

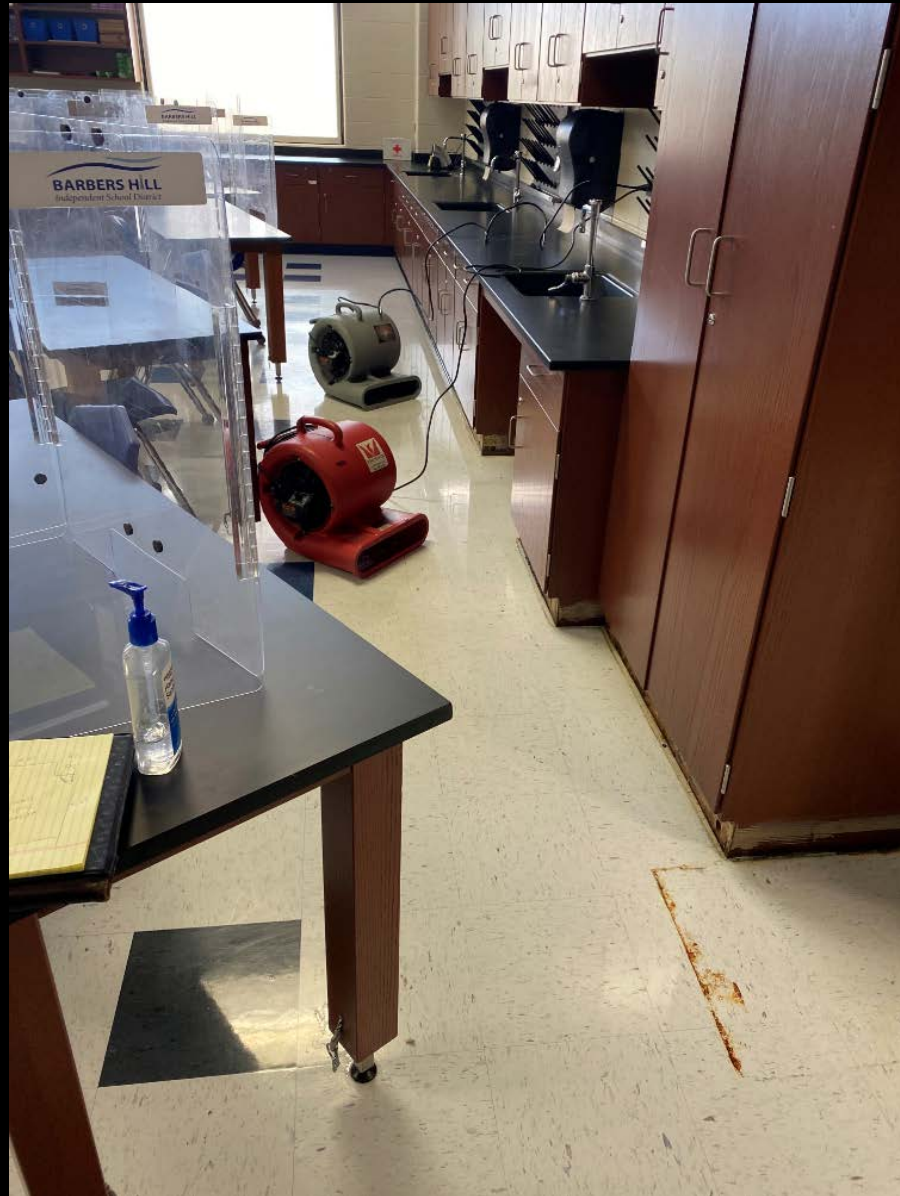

WINTER STORM DAMAGE – WEEK OF 2-16-21 CONCESSION STAND VISITORS RESTROOMS

EAGLE STADIUM NORTH



ALSO, AT BASEBALL/SOFTBALL CONCESSION STAND, CEILING WATER DAMAGE
TO WOMENS RESTROOM CEILING. ALL LEAKS REPAIRED.

An aerial photograph showing a large-scale construction project. A wide, light-colored road or embankment runs diagonally across the frame. To the left of this road is a large, dark, muddy area, possibly a construction site or a flooded field. To the right is a green field. In the background, there are several buildings, including a large one with a blue roof, and more construction activity. The sky is overcast.

THANK YOU!
