


ID	i	Task Mode	Task Name	Duration	Start	Finish	April															
							W	T	F	S	S	M	T	W	T	F	S	S				
1			Gilead Renovations	405 days	Fri 3/31/23	Thu 10/17/24																
2			Design	80 days	Fri 3/31/23	Thu 7/20/23																
3			Existing MEP system status investigation	10 days	Fri 3/31/23	Thu 4/13/23																
4			Kitchen re-design requirements	20 days	Fri 4/14/23	Thu 5/11/23																
5			A/E design	50 days	Fri 5/12/23	Thu 7/20/23																
6			Bid	30 days	Fri 7/21/23	Thu 8/31/23																
7			Award	20 days	Fri 9/1/23	Thu 9/28/23																
8			Procurement	250 days	Fri 9/29/23	Thu 9/12/24																
9			Elevator	180 days	Fri 9/29/23	Thu 6/6/24																
10			Technology Servers	250 days	Fri 9/29/23	Thu 9/12/24																
11			Electrical Switchgear	250 days	Fri 9/29/23	Thu 9/12/24																
12			Card Readers	140 days	Fri 9/29/23	Thu 4/11/24																
13			Kitchen Equipment	120 days	Fri 9/29/23	Thu 3/14/24																
14			Abatement	20 days	Fri 9/29/23	Thu 10/26/23																
15			Demolition	30 days	Fri 10/27/23	Thu 12/7/23																
16			New Construction	220 days	Fri 12/8/23	Thu 10/10/24																
17			Build out new classroom addition	30 days	Fri 12/8/23	Thu 1/18/24																
18			Build out new elevator addition	30 days	Fri 12/8/23	Thu 1/18/24																
19			Build out new interior elevator shaft	40 days	Fri 12/8/23	Thu 2/1/24																
20			Interior fit out - new walls, flooring, ceilings	80 days	Fri 2/2/24	Thu 5/23/24																
21			Install perimeter fencing	10 days	Fri 1/19/24	Thu 2/1/24																
22			Install elevator	20 days	Fri 9/13/24	Thu 10/10/24																
23			Install new security cameras, card access	20 days	Fri 9/13/24	Thu 10/10/24																

Project: WRESA Gilead Rough S Date: Thu 7/20/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	i	Task Mode	Task Name	Duration	Start	Finish	April																	
							W	T	F	S	S	M	T	W	T	F	S	S						
24		→	Final inspections	5 days	Fri 10/11/24	Thu 10/17/24																		
25		→	Building Occupancy	0 days	Thu 10/17/24	Thu 10/17/24																		

Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

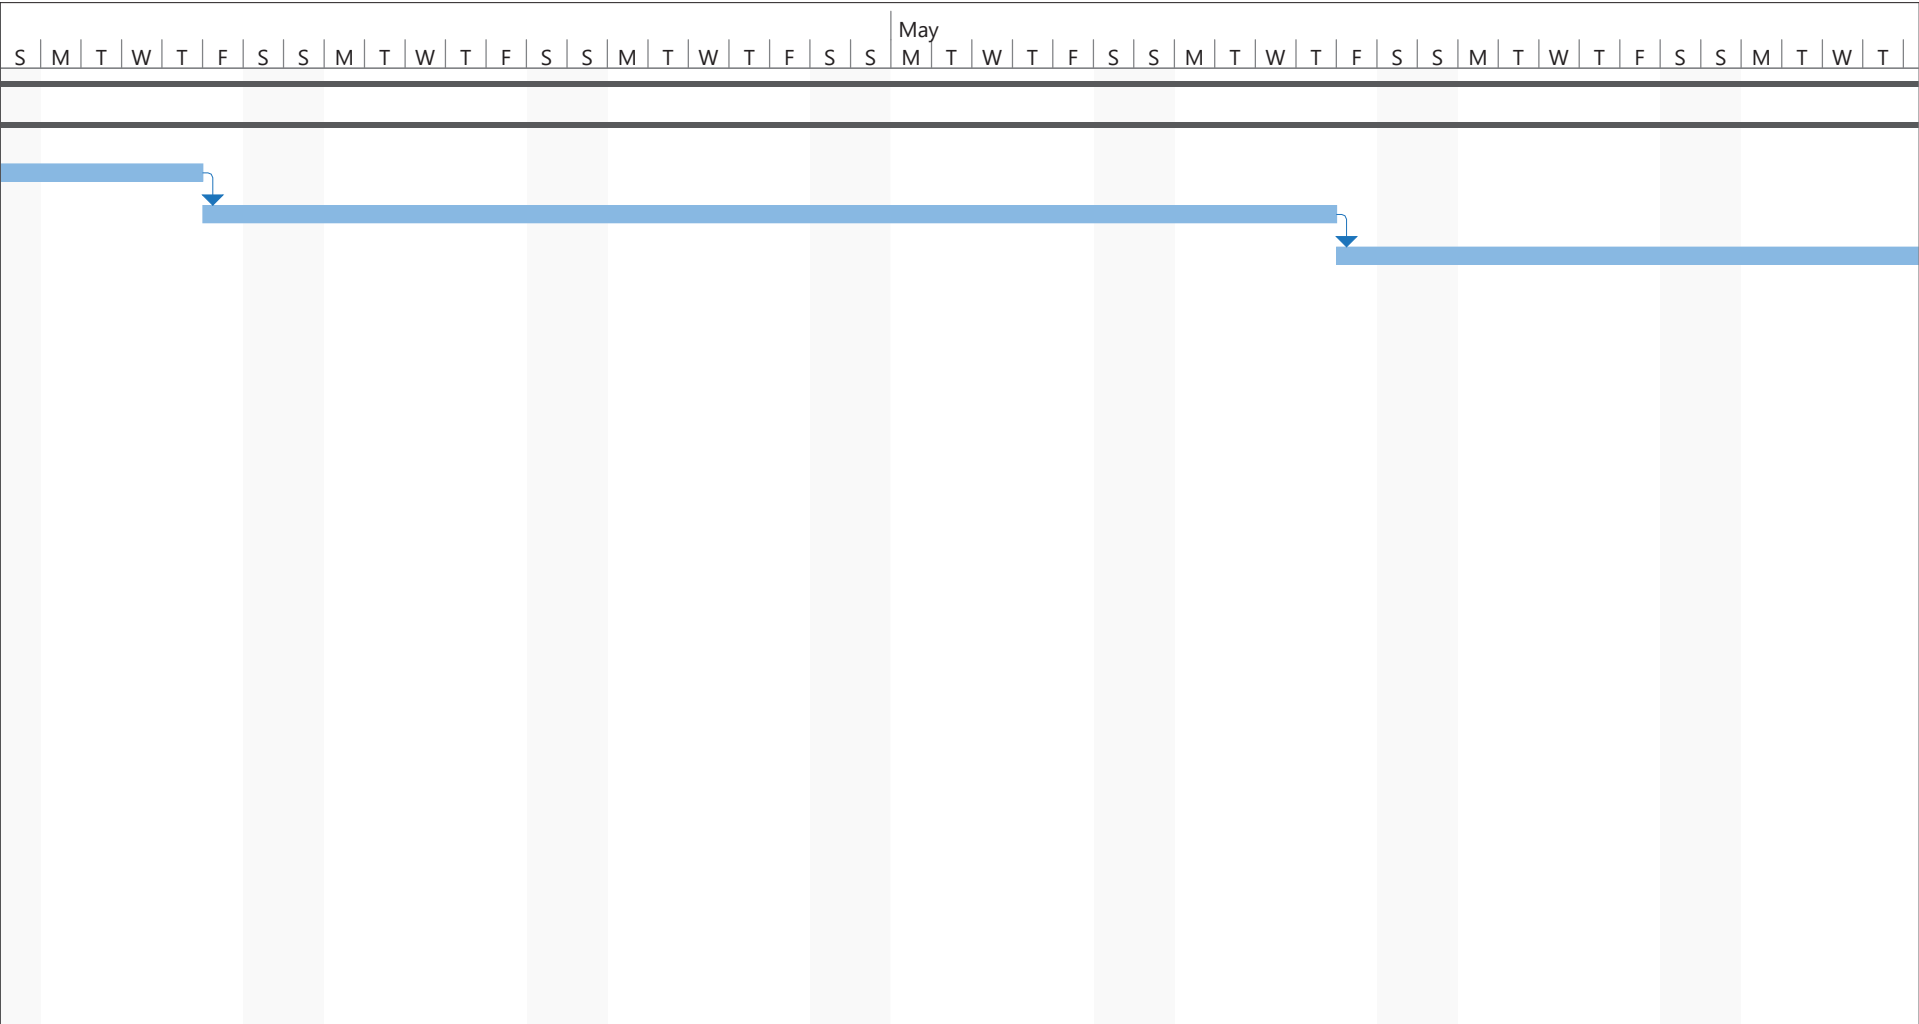

Project: WRESA Gilead Rough S
Date: Thu 7/20/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T




Project: WRESA Gilead Rough S
Date: Thu 7/20/23




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: WRESA Gilead Rough S Date: Thu 7/20/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

August

W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M

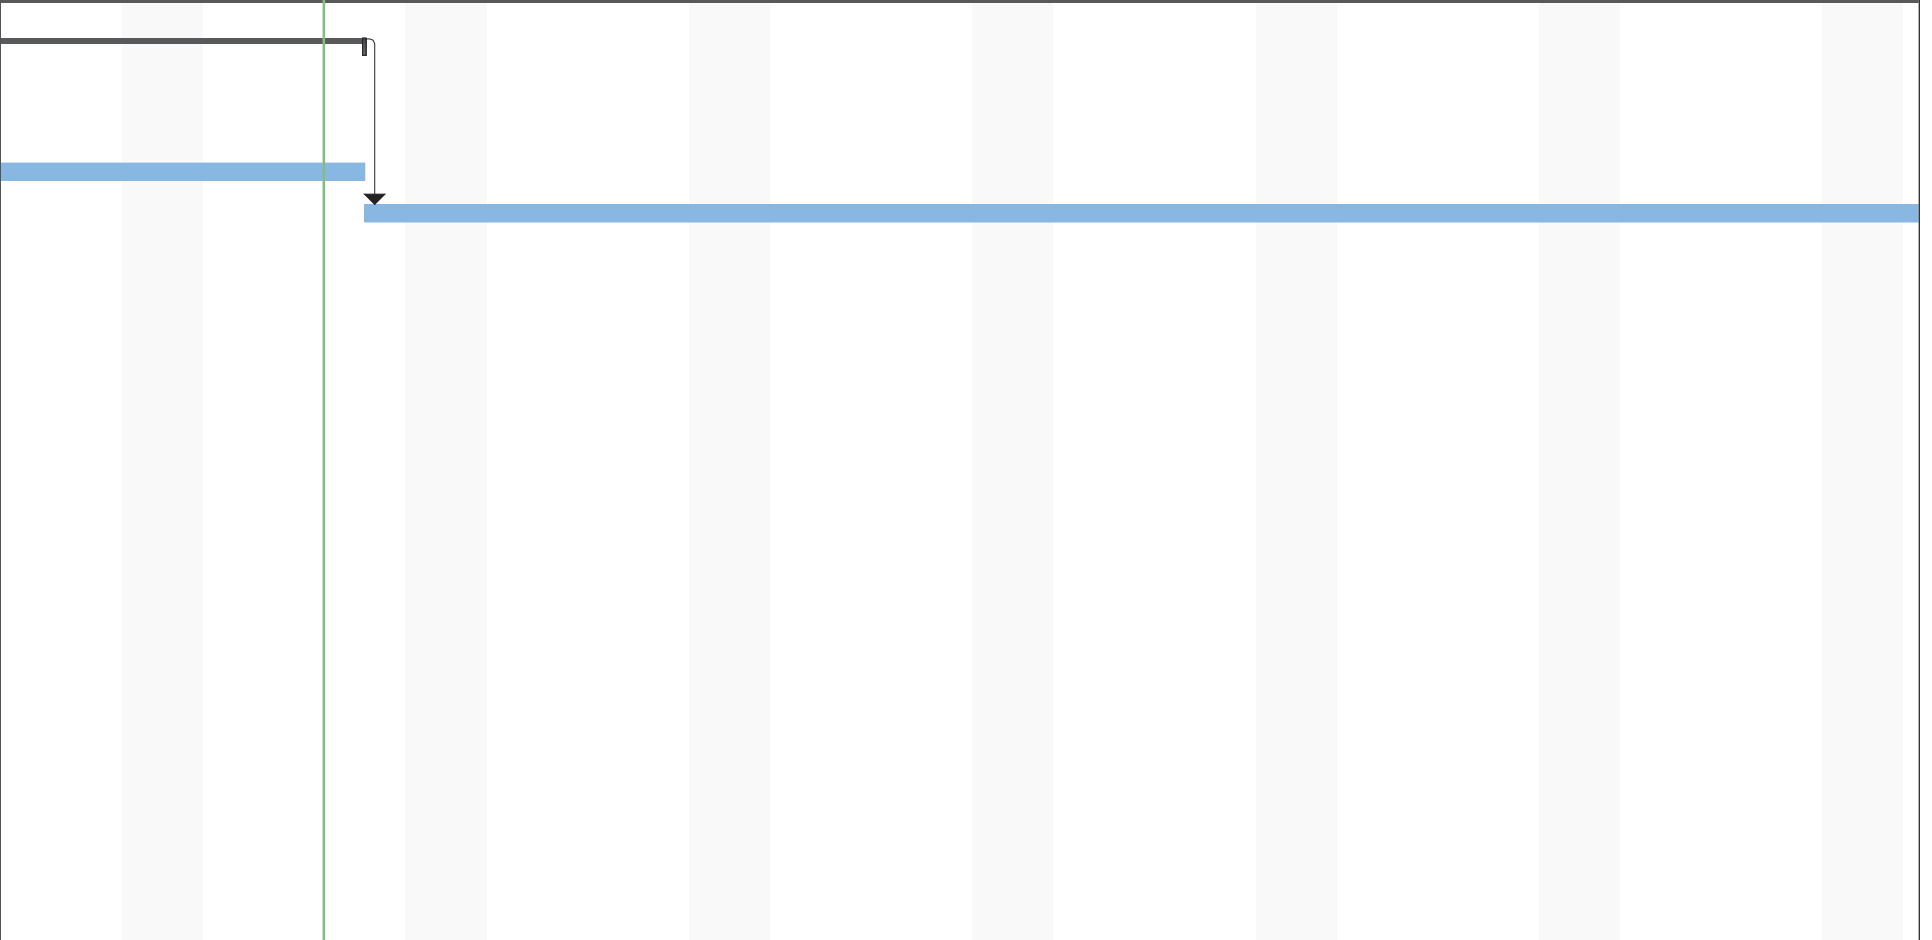


Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


August

W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M




Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

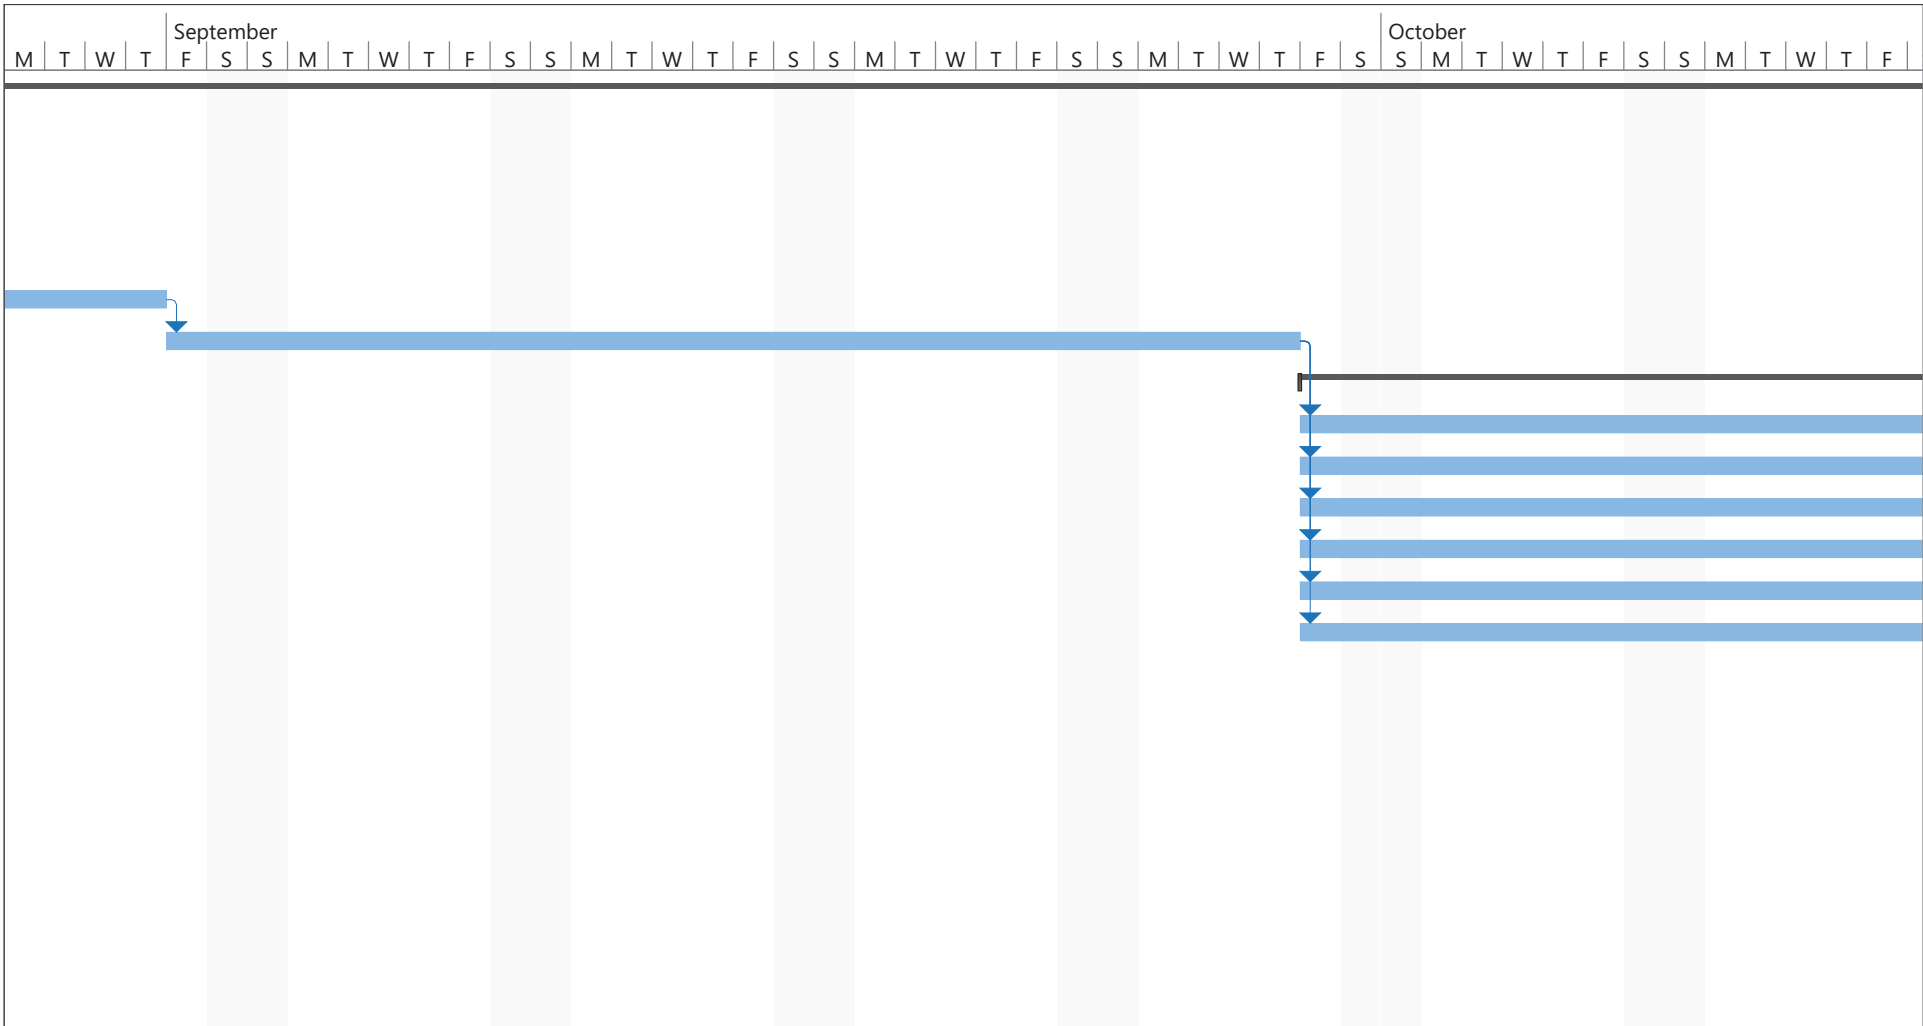


Project: WRESA Gilead Rough S
 Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

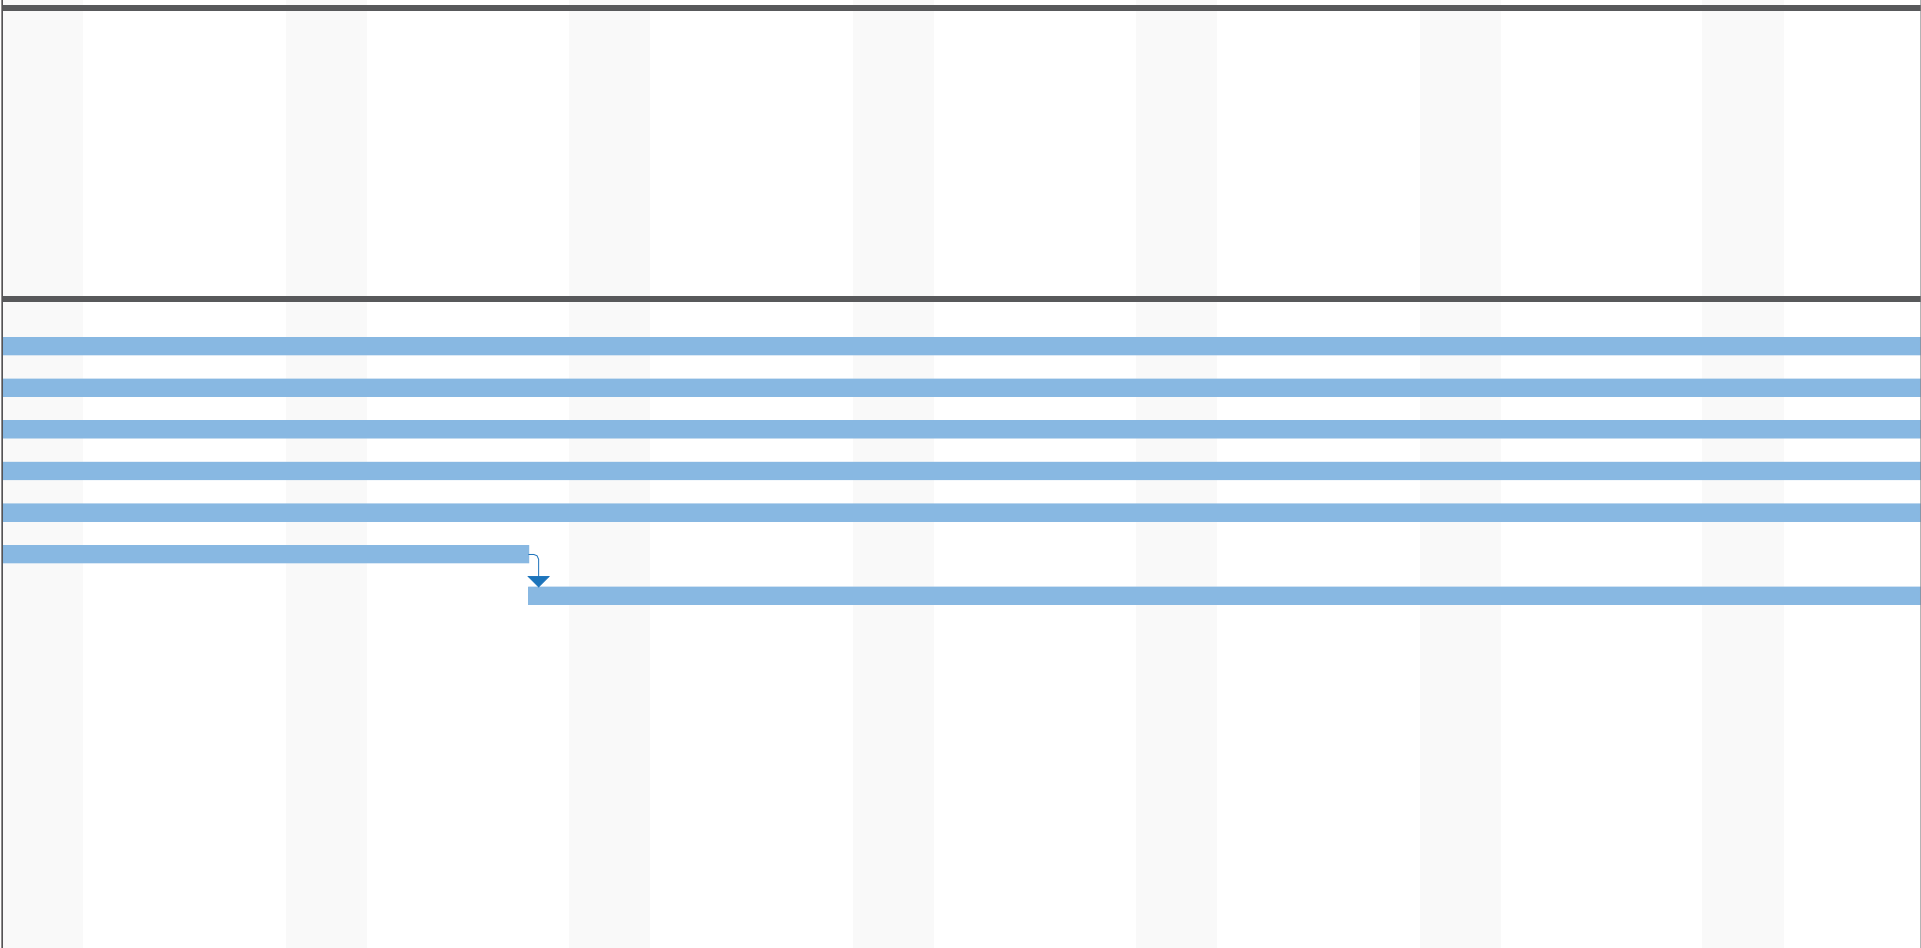

Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

December | January

T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M

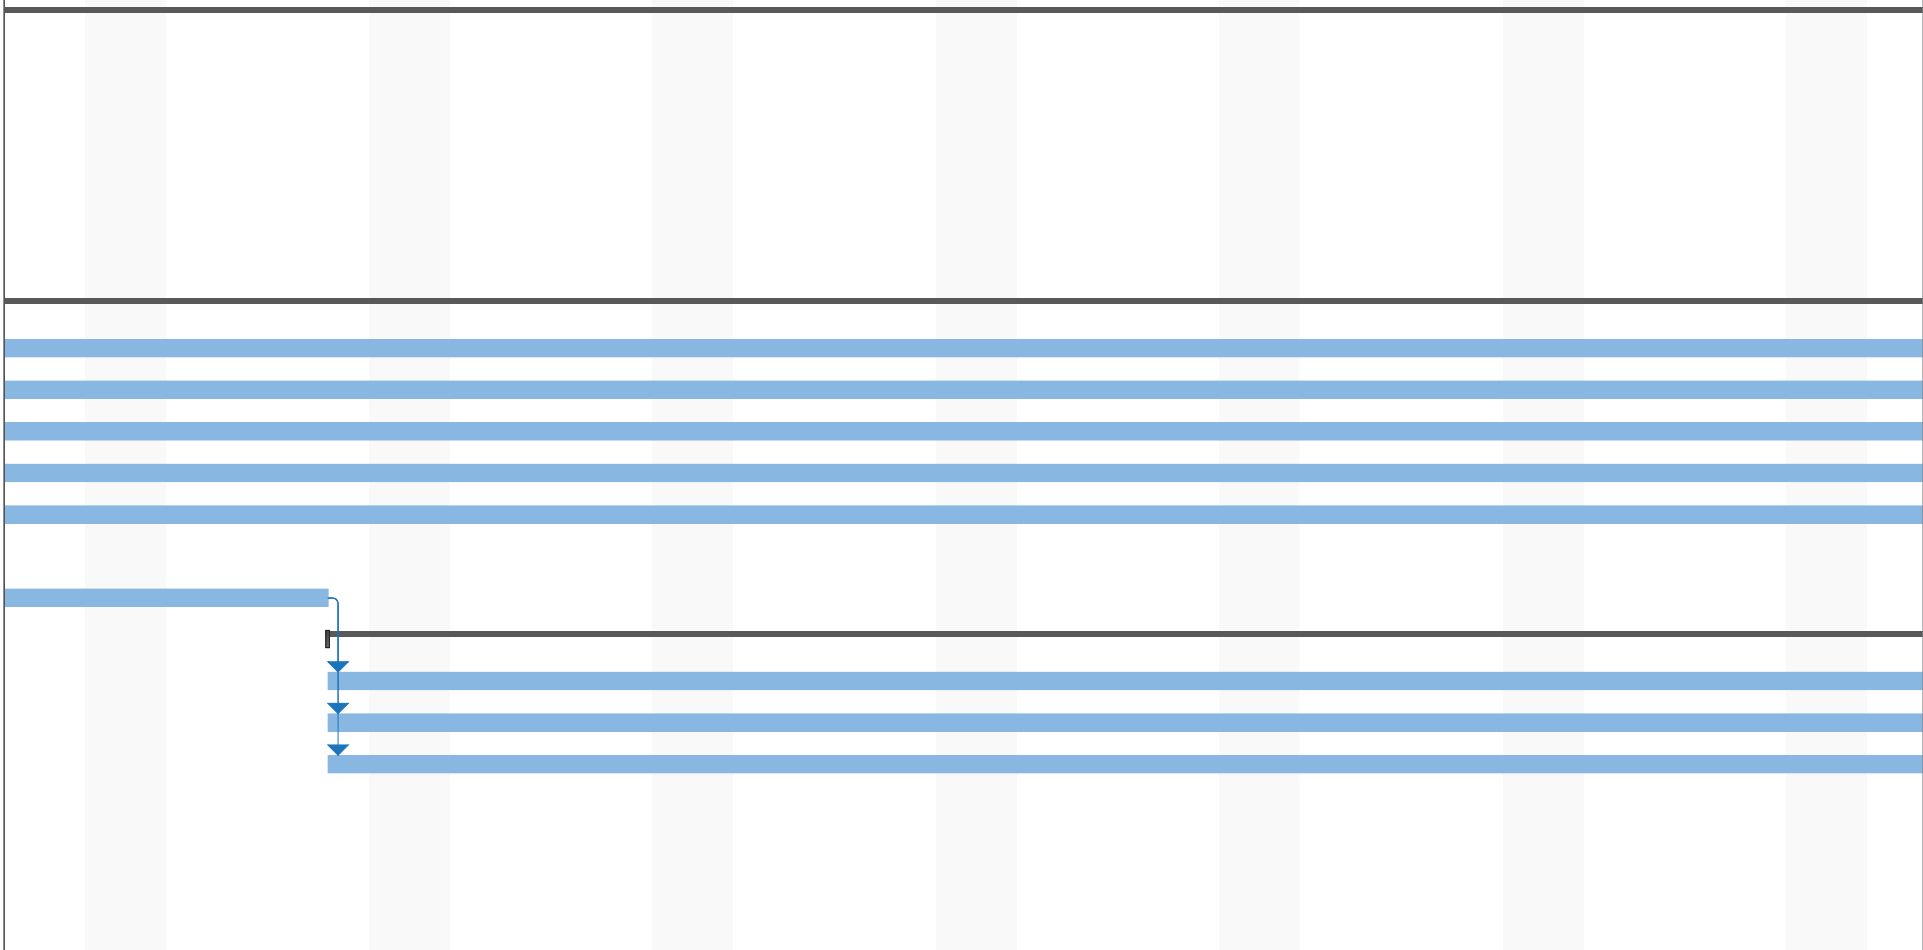


Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

December | January

T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M



Project: WRESA Gilead Rough S
Date: Thu 7/20/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

February																					March															
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S				



Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

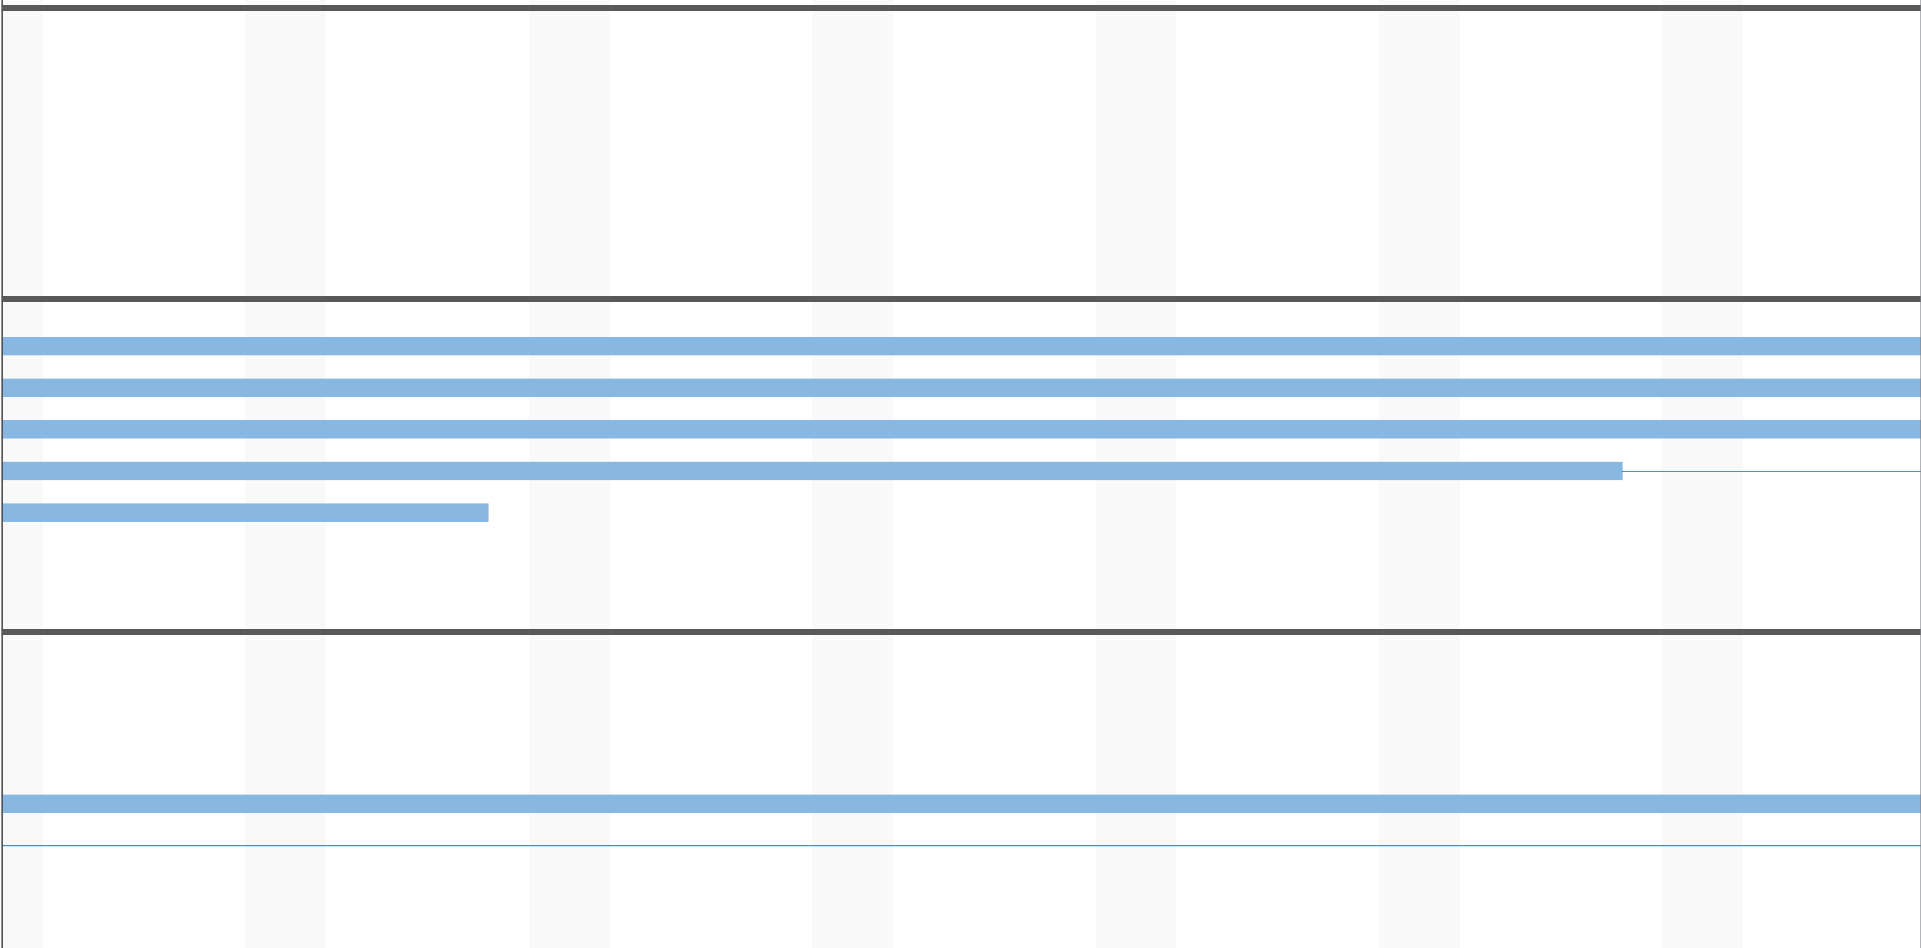


Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T


April



Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

F S S M T W T F S S M T **May** W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F **June** S S M T W

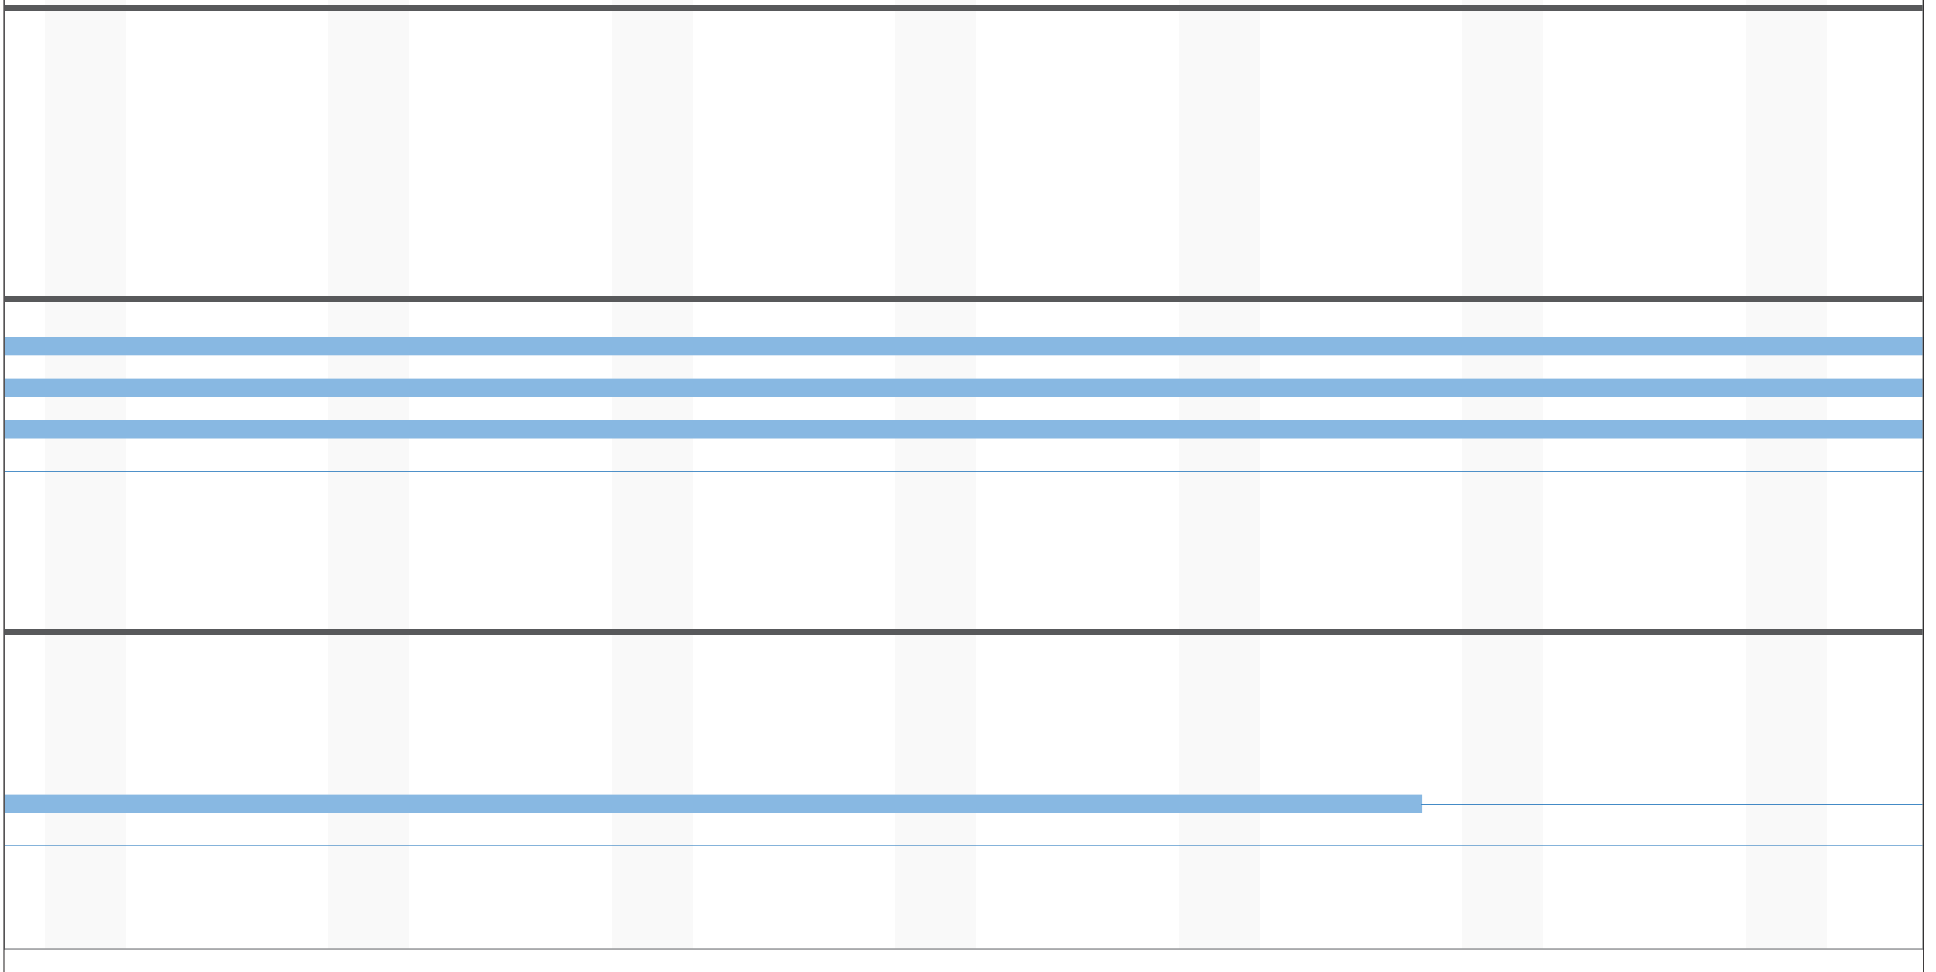


Project: WRESA Gilead Rough S Date: Thu 7/20/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: WRESA Gilead Rough S
Date: Thu 7/20/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

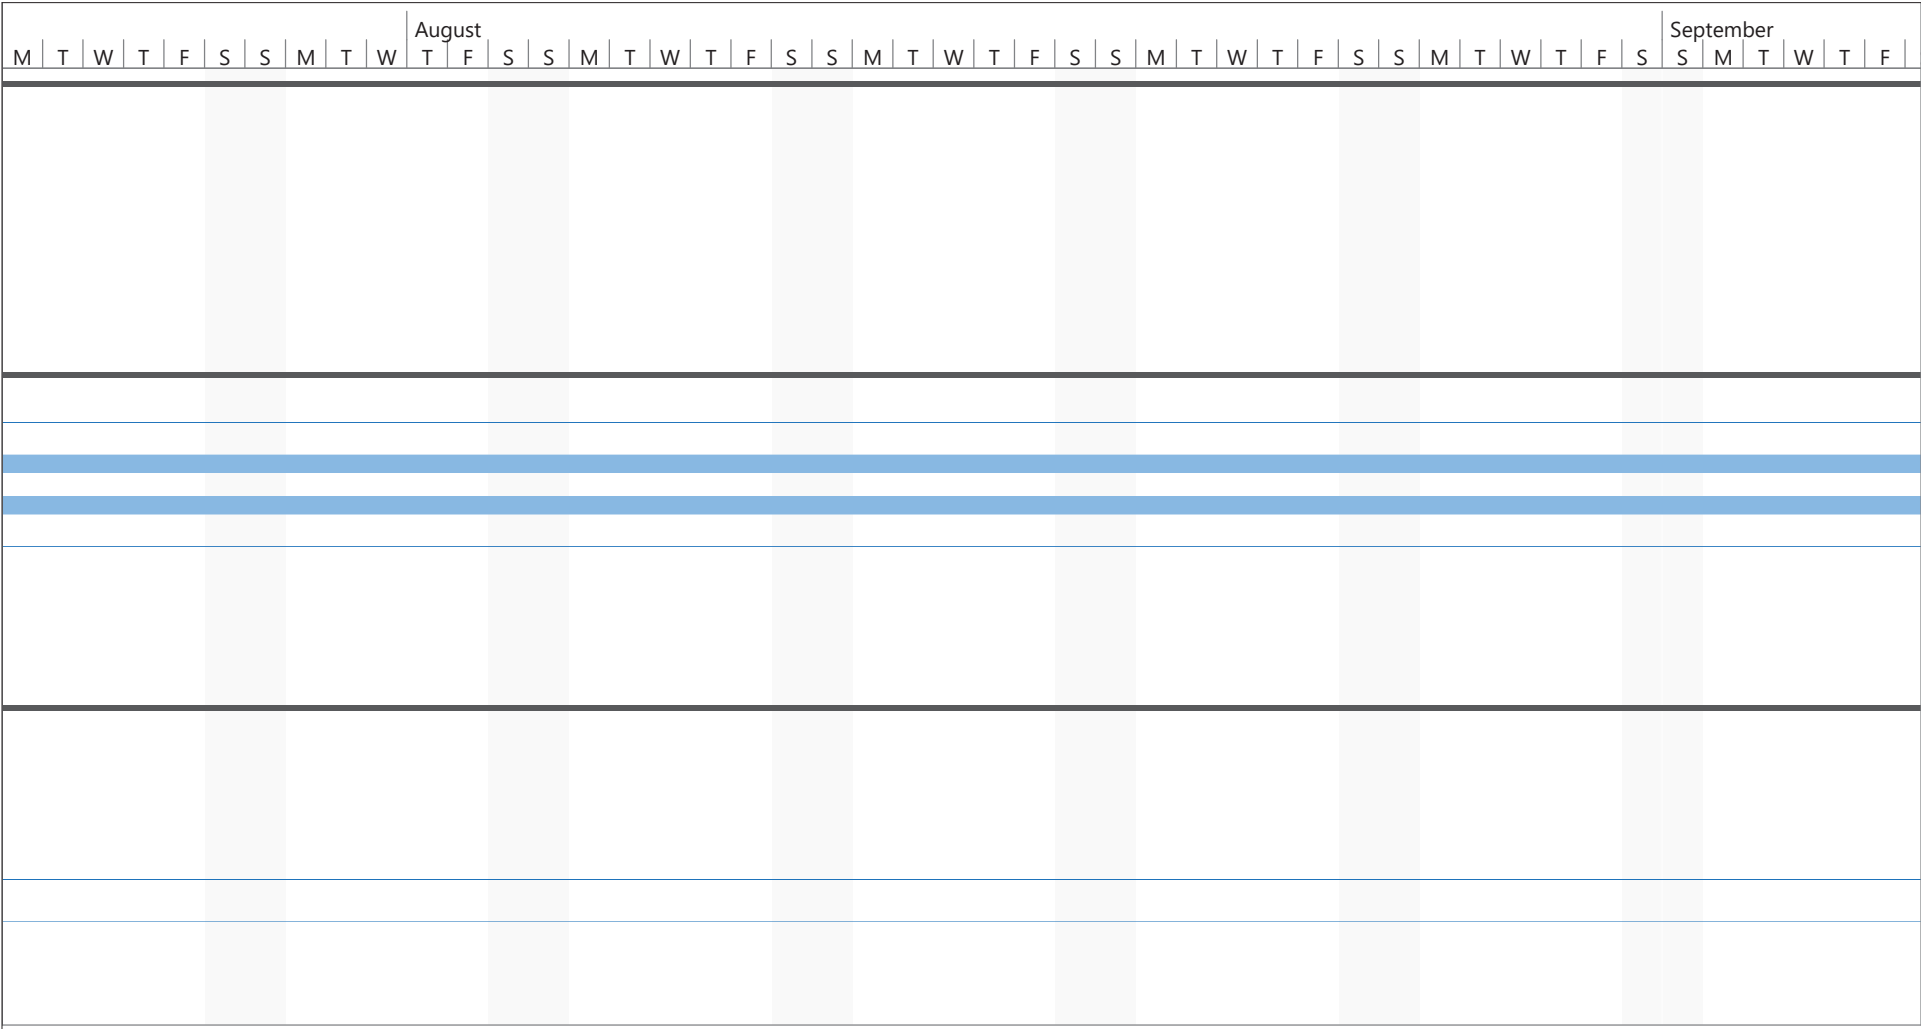

Project: WRESA Gilead Rough S
Date: Thu 7/20/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

														August							September																			
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S




Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

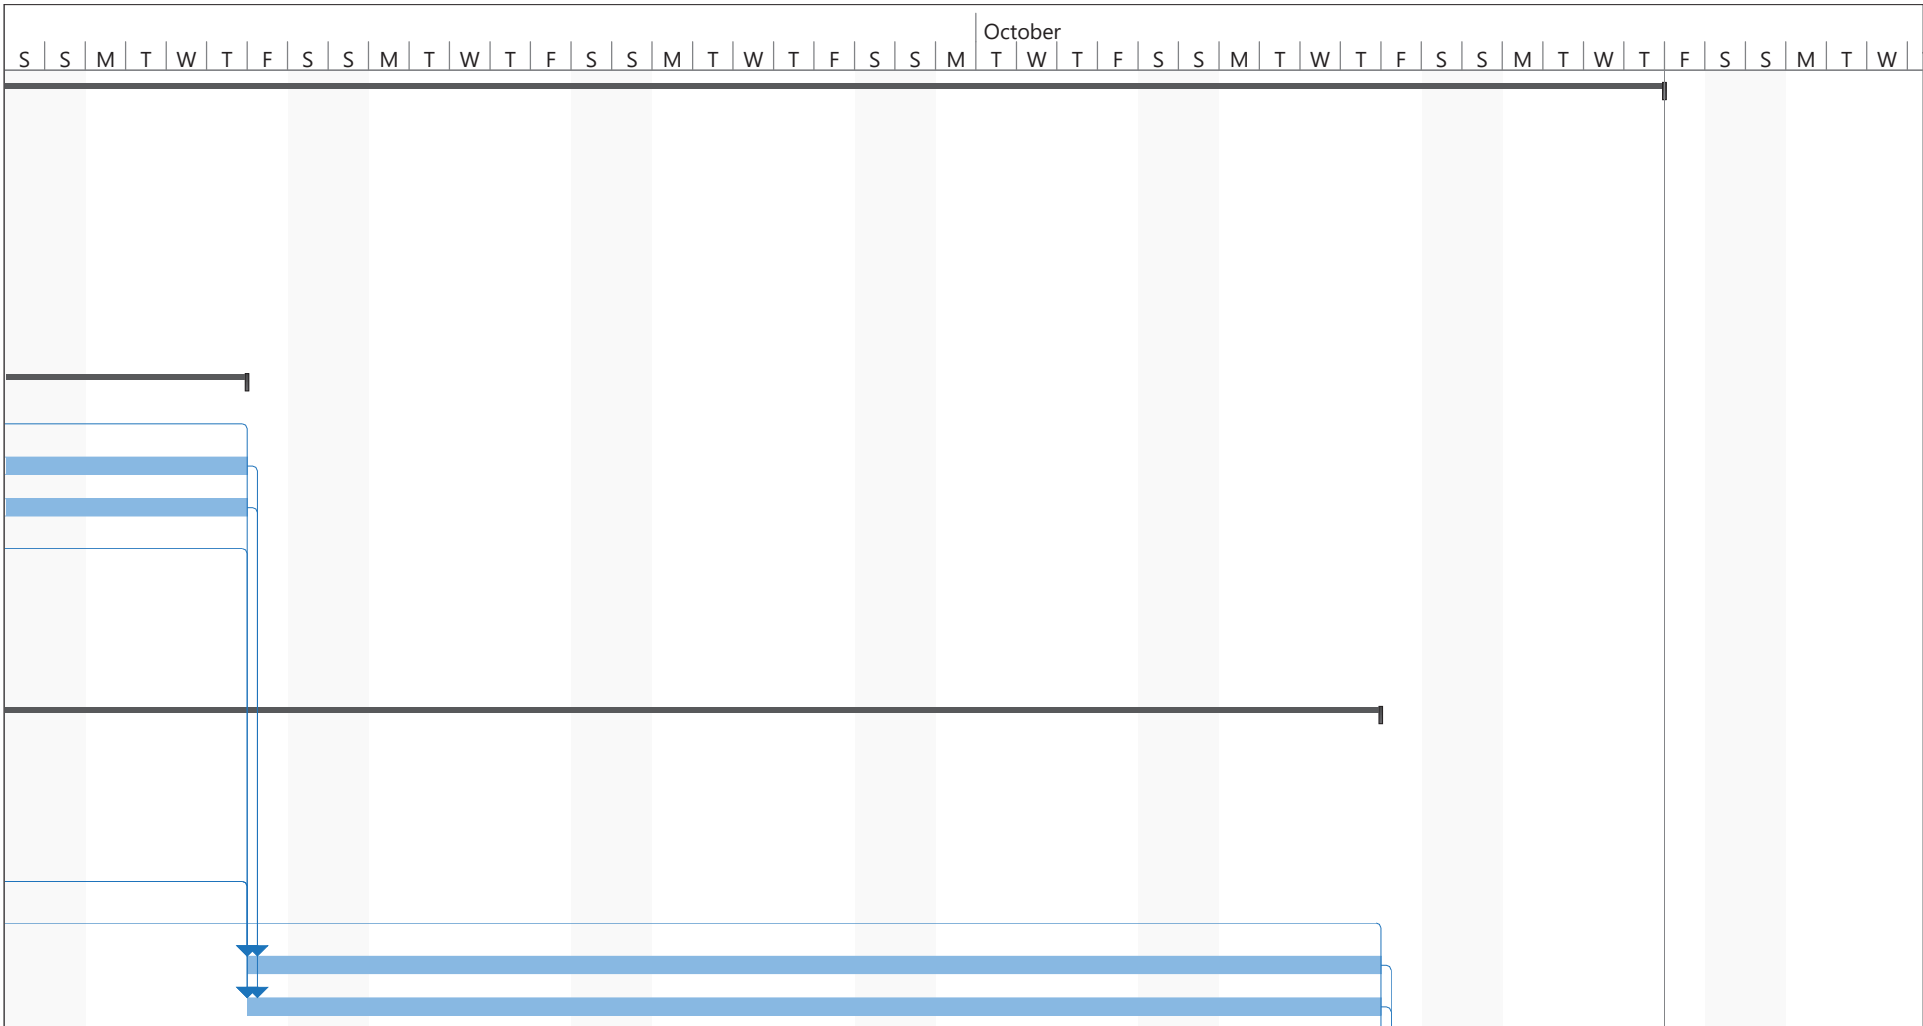

Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: WRESA Gilead Rough S
Date: Thu 7/20/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
