

Board of Trustees ED Report

June 1, 2023



AMSA

ADVANCED MATH & SCIENCE ACADEMY

INTEGRITY • EXCELLENCE • COMMUNITY

Report Overview

- MCAS
- Cummings Grant
- Senior Awards Night - Congratulations Seniors!
- Class of 2023 - Valedictorian & Salutatorian
- Construction Update
- Upcoming events

MCAS - Almost Complete



MCAS Biology Grade 9

Session 1 June 6

Session 2 June 7

2023 WINNER

We got it!

**\$30 MILLION
GRANT PROGRAM**

 **Cummings Foundation**

- **Prestigious non-profit grant**
 - **Great exposure for AMSA!!**
- **\$105,000 split over 3 yrs - \$35k/yr**
- **Summer STEM Program**
 - **Engineering**
 - **Expansion planned in future years (math/physics)**
- **Collaboration with UMass Lowell**
- **50 Students - 2 week program**

Senior Awards Night - May 18th

- Thanks to: Christie Jagielski, Matt Anderson, Lynn McCluskey and team!
- Department Awards - list will be published
- **Kia Kaha Award** - Shauna Sperou
- **Eagle Award** - Maddie Webster



Class of 2023 Valedictorian and Salutatorian



**Hannah Veracka,
Valedictorian**



**Vedant Roymoulik,
Salutatorian**

Construction Update

Construction Timeline - Next Steps

AMSA BIDDING AND FINAL GMP APPROVAL SCHEDULE UPDATE

	Notes	August 2022 Schedule		Current Schedule	
		No. of Weeks	Date Complete	No. of Weeks	Date Complete
Architect Completes Construction Drawings			6/21/23		6/21/23
Internal Quality Control Review by Team	1	0	-----	2	7/6/23
Bid Period for Subcontractors		4	7/19/23	4	8/4/23
Finalization of GMP by Construction Manager	2	2	8/2/23	3	8/26/23
Negotiation of Final GMP		2	8/16/23	2	9/9/23
Approve Final GMP	3	0	8/17/23	0	9/10/23

1. Decision to proof drawings by OPM and CM in order to reduce change orders, and week of July 4th would be lost week in bidding schedule.
2. WT Rich requested one extra week to assemble all bids and finalize GMP submission
3. Assuming GMP submission is reasonably acceptable, it should be ready for final approval within two weeks of submission.

Note: construction drawings are exactly on schedule from last summer, 6/21

Reasons for the Change in the Timeline to get to the GMP

(Comments provided by Bob Baldwin)

- Note: construction drawings are exactly on schedule from last summer, 6/21.

The final GMP moving from August to September is due to two specific tasks:

1. We added an internal review period; it should be well worth it.
2. The bidding period went from 6 weeks to 7 weeks, in order to accommodate WTR's request for three weeks instead of two to assemble the GMP. We could push them back to two weeks, but I don't know why we would. Our directive is to always favor quality and price over schedule.


ENLARGED SITE PLAN




The AMSA signage on the front window is a film adhered onto the glass that makes it appear to be etched.




The name of the school is written in stand alone letters along the ridge.

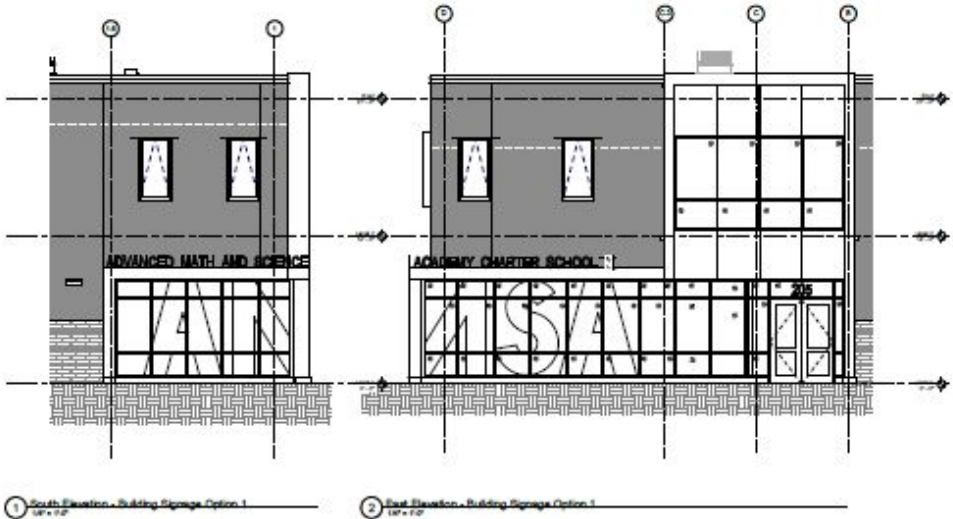


EXTERIOR ELEVATIONS

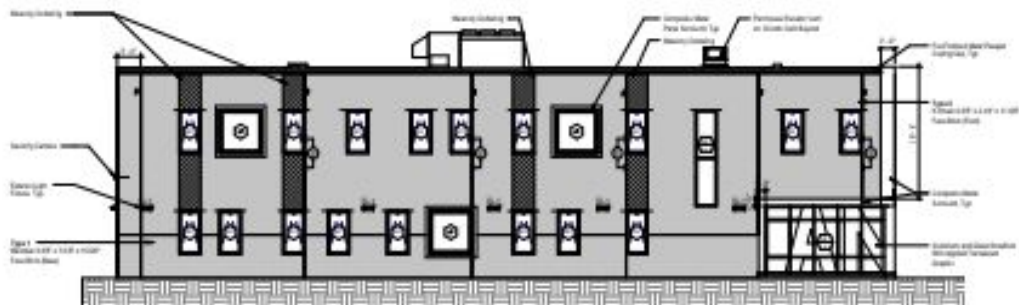


SOUTH ELEVATION

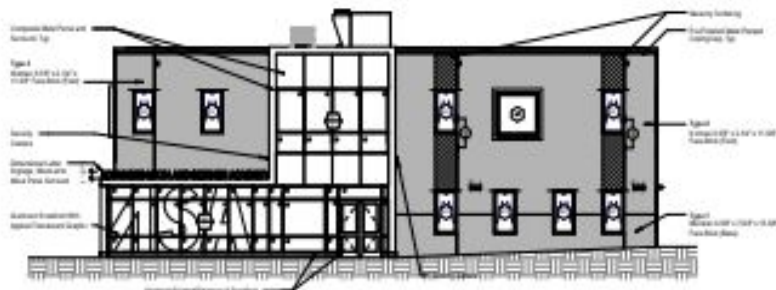

EAST ELEVATION

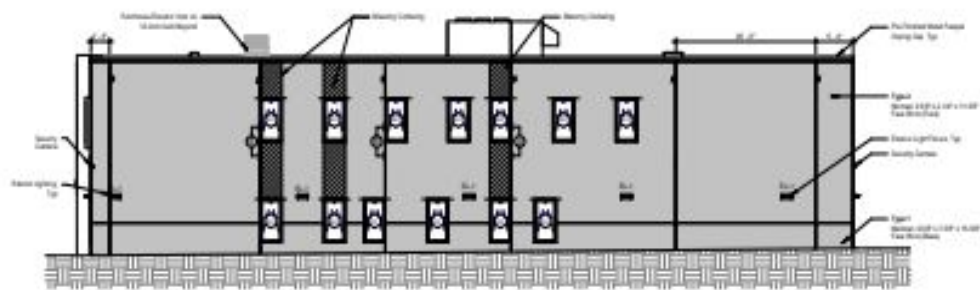

NORTH ELEVATION

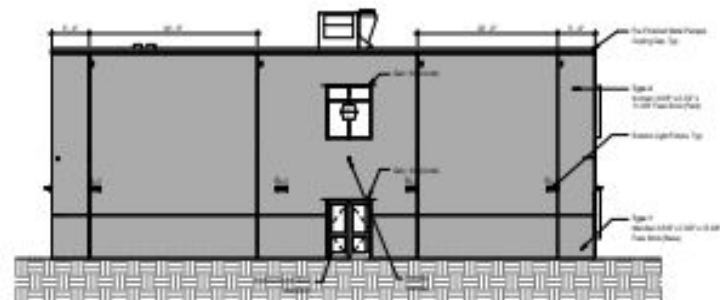

WEST ELEVATION

EXTERIOR MATERIALS



3D VIEW



BRICK TEXTURE



FIELD BRICK



METAL PANEL SURROUND



BASE BRICK



Thanks to our departing Board Members

Nick Poirier - served for 3 years on the Finance Committee and Facilities Task Force



Zak Prescott - served on the Education Committee for 2 years as our Faculty Representative



Upcoming Events

- **Graduation:** June 9th @ 6:00 pm, ForeKicks
- **June 21st:** Last day of school!! (half day)
- **Annual Faculty and Staff BBQ:** June 21st, Hudson Elks
- **Golf Tournament:** August 14th

So long, Board of Trustees, past and present!

