Witter Field
Completion Schedule

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Witter Field Completion Schedule**				
2	**Track and Field**	**82 days**	**Tue 9/12/23**	**Mon 1/8/24**	
3	Storm Drainage	15 days	Tue 9/12/23	Mon 10/2/23	
4	Field Sub-Drainage	10 days	Fri 9/22/23	Thu 10/5/23	3FS-7 days
5	Electrical Underground	10 days	Tue 9/19/23	Mon 10/2/23	3FF
6	Track Drains				4
7	D-Zone Curbs	5 days	Fri 10/13/23	Thu 10/19/23	6FF
8	Sports Equipment Foundations	5 days	Fri 10/13/23	Thu 10/19/23	7FF
9	Composite Turf Base System	14 days	Fri 10/20/23	Wed 11/8/23	6
10	Synthetic Turf	20 days	Thu 11/9/23	Fri 12/8/23	9
11	AC Demo and Repair at Track Failure	5 days	Fri 10/20/23	Thu 10/26/23	9SS
12	AC Paving at Track Failure	1 day	Fri 10/27/23	Fri 10/27/23	11
13	AC Cure	28 edays	Fri 10/27/23	Fri 11/24/23	12
14	Remove Track Surfacing	4 days	Thu 11/9/23	Tue 11/14/23	9
15	Track Surfacing	20 days	Mon 12/11/23	Mon 1/8/24	10,13
16	Track Striping	3 days	Thu 1/4/24	Mon 1/8/24	15FF

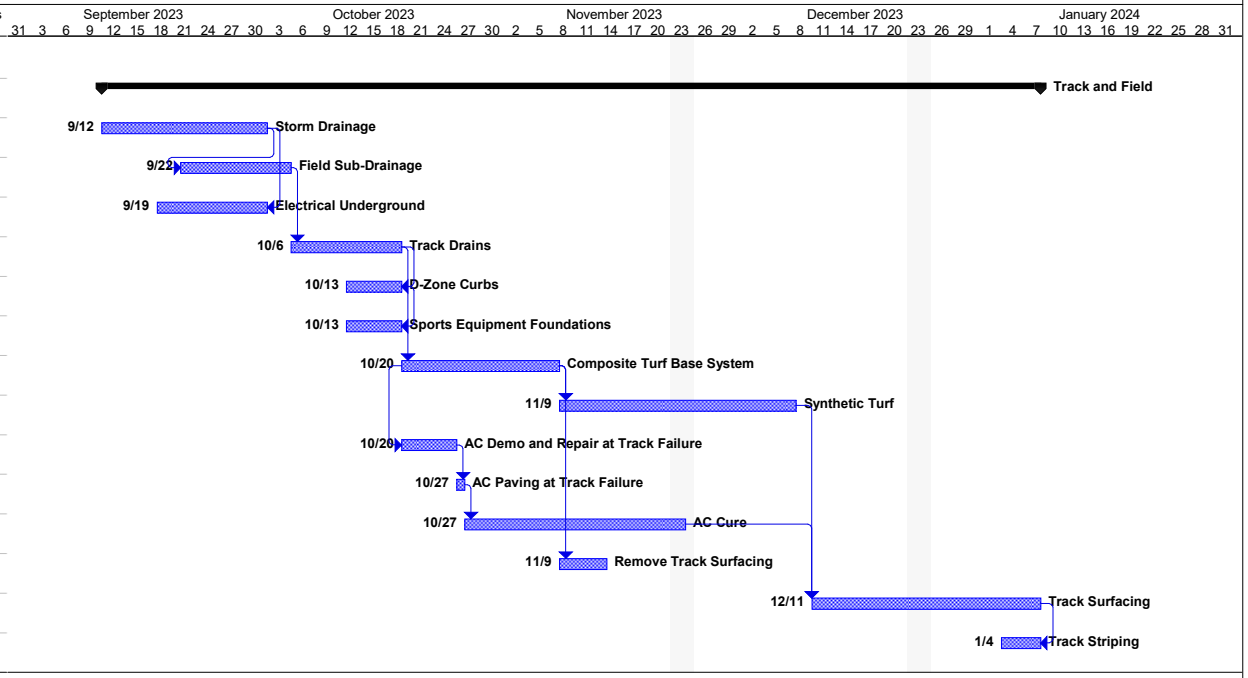

Robert A. Bothman, Inc.
2690 Scott Boulevard, Santa Clara, CA 95050
