

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Bidding**	**95 days**	**Mon 1/19/26**	**Fri 5/29/26**	
2		TMP to issues CD's	0 days	Tue 3/3/26	Tue 3/3/26	
3		Submit to State for Plan Review/Permitting	64 days	Tue 3/3/26	Fri 5/29/26	2
4		Bid/Review/Recommend	3 wks	Wed 3/11/26	Tue 3/31/26	2
5		Interview & Award	1 wk	Wed 4/1/26	Tue 4/7/26	4
6		Submit Recommendation for Board Approval	0 days	Mon 1/19/26	Mon 1/19/26	
7		**Construction**	**315 days**	**Wed 6/10/26**	**Tue 8/24/27**	
8		Last day of School	0 days	Wed 6/10/26	Wed 6/10/26	
9		Mobilize Soil Erosion Control Measures	5 days	Wed 6/10/26	Tue 6/16/26	8
10		Demo Landscape, Hardscape, Bleachers and Equipment	10 days	Wed 6/17/26	Tue 6/30/26	9
11		Rough Grading	10 days	Wed 7/1/26	Tue 7/14/26	10
12		Install Soccer Posts and Netting	8 days	Wed 7/15/26	Fri 7/24/26	11
13		Install Backstop Posts	7 days	Wed 7/8/26	Thu 7/16/26	11SS+5 days
14		Baseball Concrete Foundations and Hardscape	7 days	Fri 7/17/26	Mon 7/27/26	11,13
15		Softball Concrete Foundations and Hardscape	7 days	Wed 7/22/26	Thu 7/30/26	11,13,14SS+3 day
16		Fine grade Walkways	5 days	Fri 7/31/26	Thu 8/6/26	14,15
17		Asphalt Paving	5 days	Fri 8/7/26	Thu 8/13/26	16
18		**Summer 2027 Construction**	**52 days**	**Mon 6/14/27**	**Tue 8/24/27**	
19		Demo Existing Fencing	5 days	Mon 6/14/27	Fri 6/18/27	17
20		Grade Entry Plaza	10 days	Mon 6/21/27	Fri 7/2/27	19
21		Install Ornimental Fencing	7 days	Mon 7/5/27	Tue 7/13/27	20
22		Entry Plaza Hardscape	10 days	Wed 7/14/27	Tue 7/27/27	21
23		Install New Chain Link Fencing	10 days	Wed 7/28/27	Tue 8/10/27	22
24		Landscaping	10 days	Wed 8/11/27	Tue 8/24/27	23,17SS+5 days
25		Complete	0 days	Tue 8/24/27	Tue 8/24/27	12,24

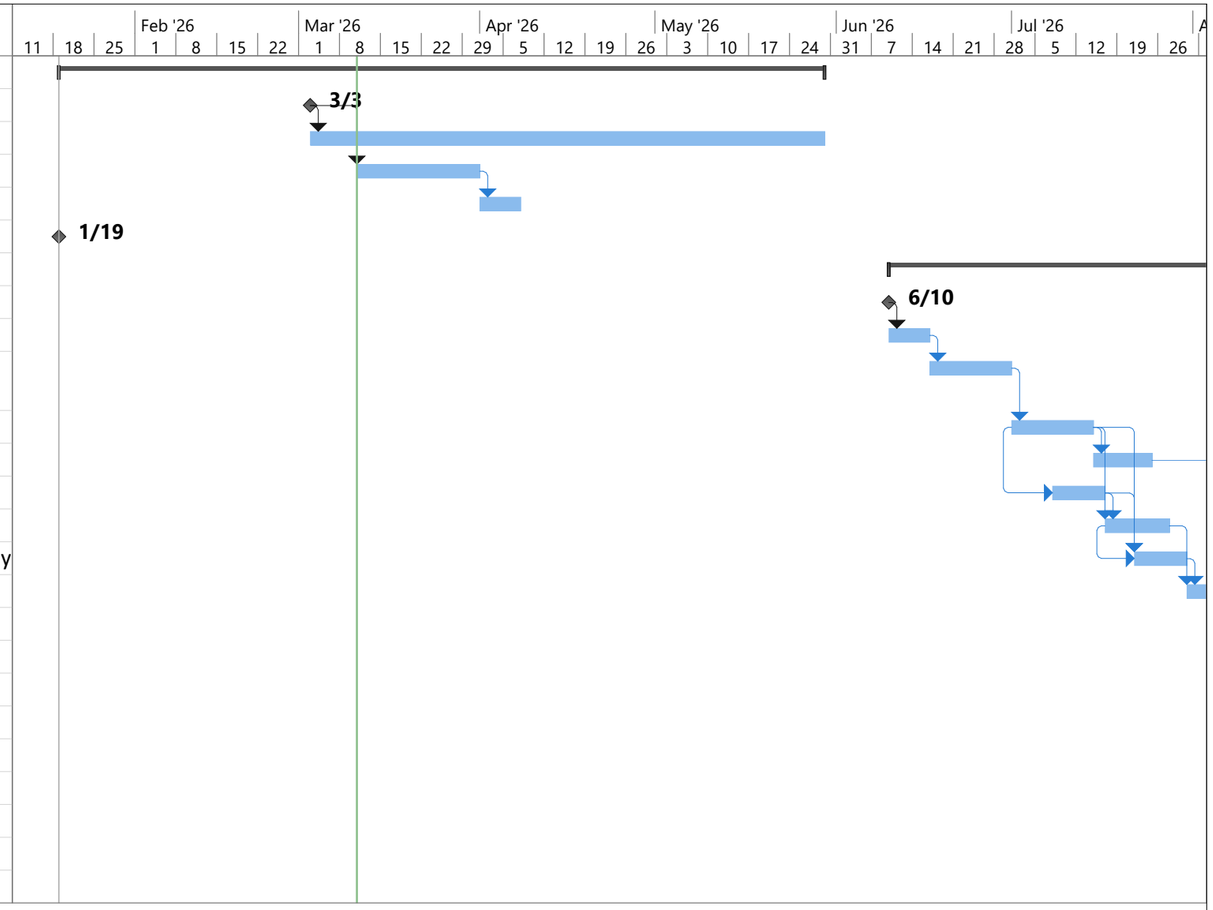

Project: Wylie Bidding Schedule
Date: Wed 3/11/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

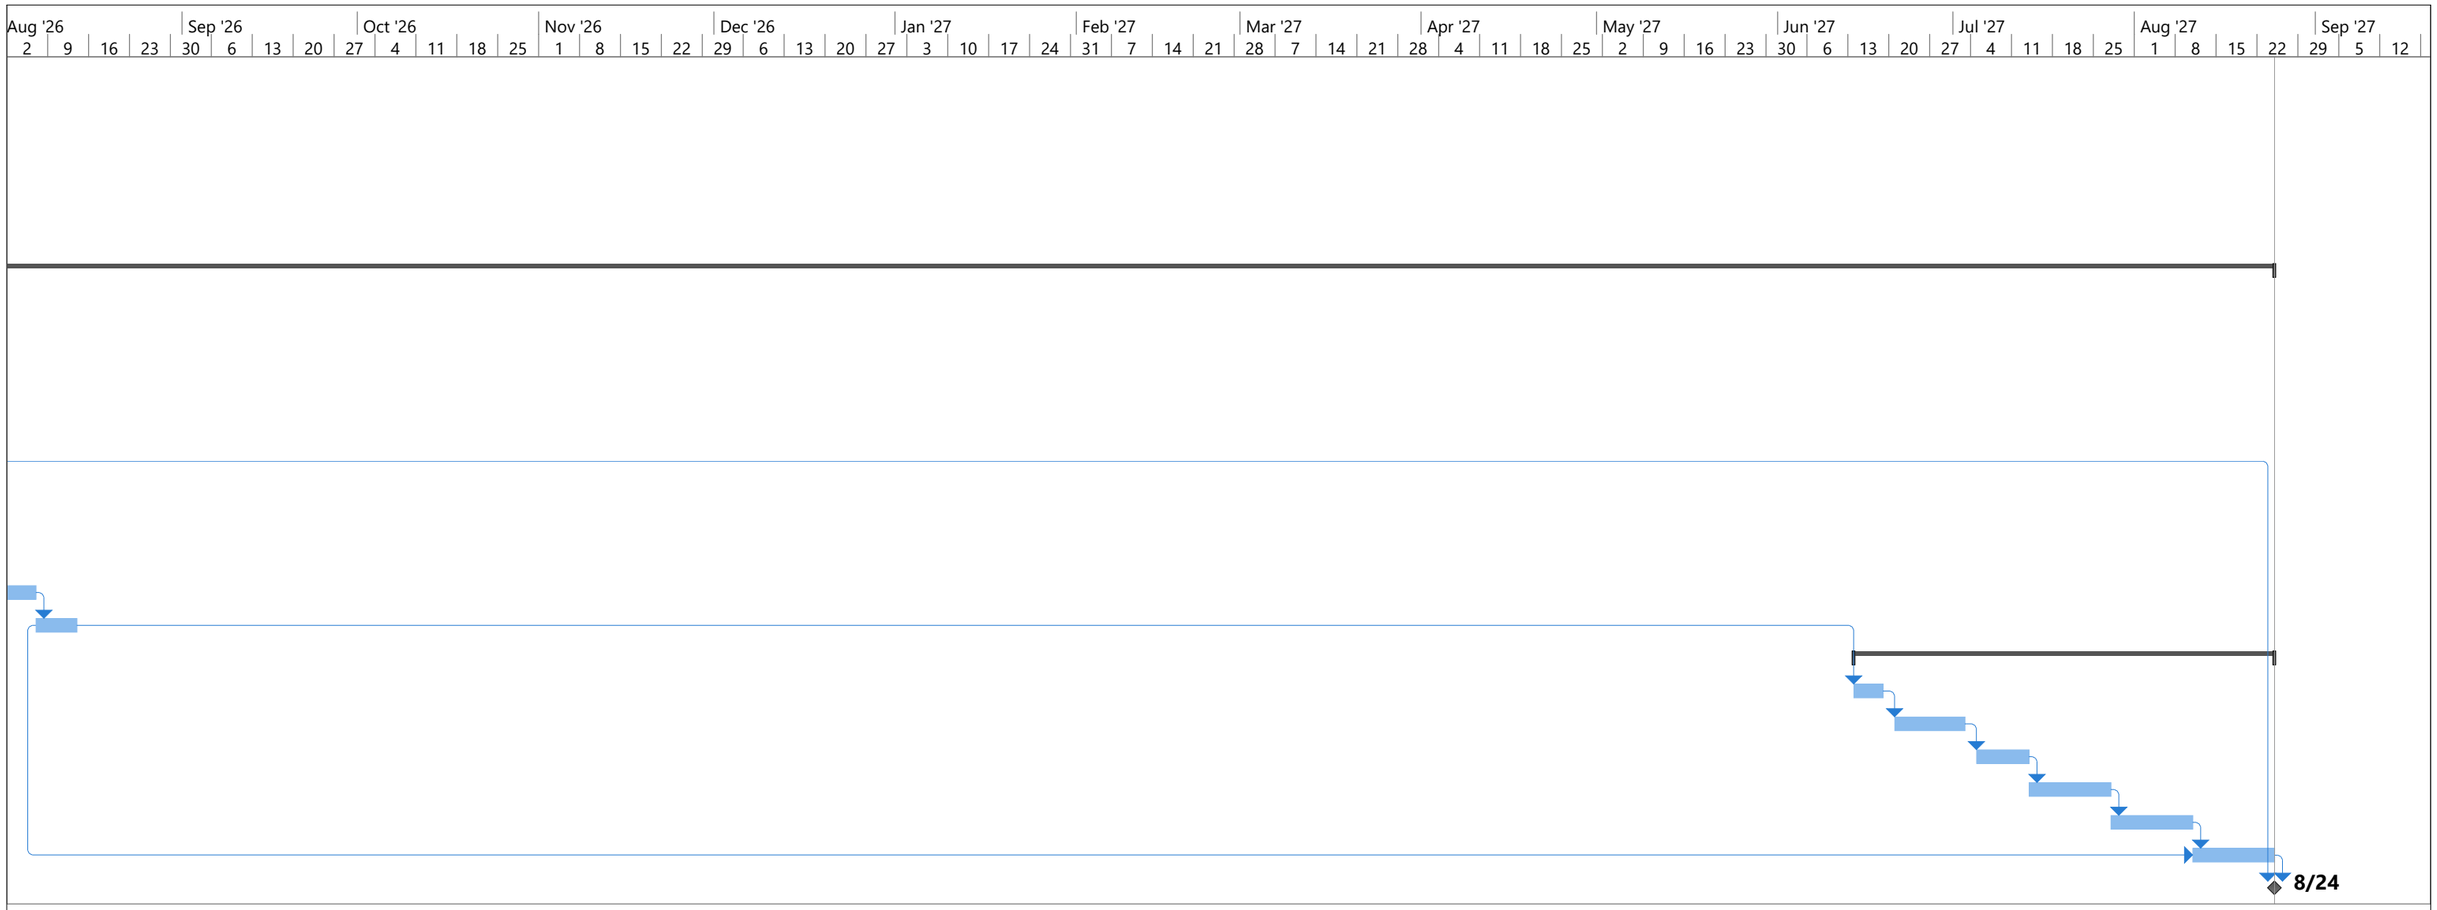

Project: Wylie Bidding Schedule
Date: Wed 3/11/26

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
