



Spring Branch ISD
**Career & Technical
Education**



CTE Long Range Facility Planning LRFP Committee | Meeting #4

July 8, 2021



Agenda: LRFP Committee Meeting #4

05 Minutes

- CTE LRFP Committee Charge
- CTE LRFP Mtg#3 Recap

1

30 Minutes

- CTE LRFP Mtg#3 Results – 12 Table Consensus
- CTE LRFP Mtg#3 Results – 4 Group Consensus

2

40 Minutes

- LRFP Committee Engagement: “CTE LRFP Recommendation”
Tier Strategy + LRFP Timeline Consensus
 - Review/Finalize Recommendation = Group Discussion
 - Formalize Recommendation = Individual Consensus Poll
 - LRFP Committee Feedback Form

3

15 Minutes

- Discuss Presentation to SBISD Board: July 19, 2021
 - Presentation Outline
 - Identify 2 LRFP Committee Volunteers (Student, Adult)
- Closing Remarks

CTE Long Range Facility Plan Committee - Charge

- The SBISD Board of Trustees will appoint a **Career and Technical Education (CTE) Long Range Facilities Committee (The Committee)** comprised of parents, students, staff, community members, business representatives, and administrators to participate in the development of the SBISD CTE Long Range Facilities Plan.
- **The Committee will function in an advisory capacity** to the SBISD Board of Trustees, Superintendent and Senior Staff. The Committee will consider the District's vision for the future of CTE, the conditions and capacities of its existing classrooms, labs, and facilities, and future CTE-related facility needs.
- **The Committee will present recommendations to the Board of Trustees** by _____.
The Board of Trustees will receive and review the Committee's recommendations.
The Board of Trustees will be responsible for final approval of a CTE Long Range Facilities Plan and its execution.

CTE Long Range Facility Plan Committee – Scope of Work

- **Develop and present to the Board of Trustees a CTE Long-Range Facilities Plan to serve the district as a baseline for the next 10 years.** The Plan should include recommendations related to upgrades, renovations, and/or expansions to existing classrooms, labs, and facilities to align with the CTE Program of Studies, and where appropriate, identify facilities to be replaced or added to the portfolio.

CTE Long Range Facility Plan Committee – Refrain from

- **Recommendations regarding specific design** of schools or district facilities, **location(s)** of schools or district facilities or **boundaries** of district facilities,
- **Recommendations regarding instructional arrangements** and/or **educational pedagogy** and **district policy** as the CTE Long Range Facilities Plan is developed

<div> <div>1</div> <div>Meeting Objective</div> </div>		<div> <div>LRFP #3</div> <div>June 24th (SFMS)</div> </div>
<div> <div>2</div> <div>Topics Discussed</div> </div>		<div> <div>DEVELOP Plan:</div> <div>Long Range Plan</div> <div>Confirm Tier Strategy</div> <div>Create LRFP Timeline</div> </div>
<div> <div>3</div> <div>Informed Direction</div> </div>		<div> <div>CTE LRFP:</div> <div>(Develop Options)</div> <div>12 Tables → 4 Tables</div> <div>Improvement Strategy</div> <div>(Tier 1 + Tier 2 + Tier 3)</div> <div>Timeline Order Priority</div> <div>(Building Type)</div> </div>
<div>FOCUS:</div>		<div> <div>Small + Medium Group</div> <div>INPUT / FEEDBACK:</div> <div>CAMPUS TIER STRATEGY</div> <div>+</div> <div>BLDG TIMELINE</div> <div>DEVELOP</div> </div>

LRFP Committee Mtg #3 Recap: Reminder of what we covered....

<div> <div>CTE Long Range Facilities Planning LRFP Committee Meeting #3</div> </div>		<div> <div>Agenda: LRFP Committee Meeting #3</div> </div>
<div> <div>05 Minutes</div> </div>		<div> <div>CTE LRFP Committee Charge</div> <div>CTE LRFP Mtg#2 Recap</div> </div>
<div> <div>1</div> <div>10 Minutes</div> </div>		<div> <div>CTE LRFP Mtg#2 Results</div> <div>– Individual Voting Results</div> <div>New Information</div> <div>– Current Project Costs + Project Timelines</div> </div>
<div> <div>2</div> <div>35 Minutes</div> </div>		<div> <div>LRFP Committee Engagement: “LRFP Strategy + Timeline”</div> <div>– 05 min = Set-up (Objective, Tools + Rules of Game)</div> <div>– 30 min = LRFP 12 Table Consensus (Strategy + Timeline)</div> </div>
<div> <div>40 Minutes</div> </div>		<div> <div>– 05 min = Set-up (Objective, Tools + Rules of Game)</div> <div>– 30 min = LRFP 4 Table Consensus (Strategy + Timeline)</div> <div>– 05 min = Review Results of 4 Tables</div> </div>
<div> <div>3</div> <div>5 Minutes</div> </div>		<div> <div>What to Expect at LRFP Mtg#4</div> <div>Closing Remarks</div> </div>

LRFP Committee Mtg #3 Recap:

Mtg #2 Engagement.... Tier Strategy

Individual Input Results

LRFP Mtg#2 Follow-up | Individual Results: Campus Sort

55 Voting Participants

LRFP Member	MIDDLE SCHOOLS						HIGH SCHOOLS				SPECIALTY		CENTRAL	
	MMS	NMS	SBMS	SFMS	SOMS	SWMS	MHS	NHS	SWHS	SHS	SBEC	WAIS	AG	Guthrie
1	1	1	1	1	1	1	2	2	2	2	1	1	2	2
2	1	1	1	1	1	1	2	2	2	2	1	1	2	2
3	1	1	1	1	1	1	2	2	2	2	1	1	2	2
4	2	2	2	2	2	2	3	3	3	3	2	2	3	3
5	2	2	2	2	2	2	3	3	3	3	2	2	3	3
6	2	2	2	2	2	2	3	3	3	3	2	2	3	3
7	2	2	2	2	2	2	3	3	3	3	2	2	3	3
8	2	2	2	2	2	2	3	3	3	3	2	2	3	3
9	2	2	2	2	2	2	3	3	3	3	2	2	3	3
10	2	2	2	2	2	2	3	3	3	3	2	2	3	3
11	2	2	2	2	2	2	3	3	3	3	2	2	3	3
12	2	2	2	2	2	2	3	3	3	3	2	2	3	3
13	2	2	2	2	2	2	3	3	3	3	2	2	3	3
14	2	2	2	2	2	2	3	3	3	3	2	2	3	3
15	2	2	2	2	2	2	3	3	3	3	2	2	3	3
16	2	2	2	2	2	2	3	3	3	3	2	2	3	3
17	2	2	2	2	2	2	3	3	3	3	2	2	3	3
18	2	2	2	2	2	2	3	3	3	3	2	2	3	3
19	2	2	2	2	2	2	3	3	3	3	2	2	3	3
20	2	2	2	2	2	2	3	3	3	3	2	2	3	3
21	2	2	2	2	2	2	3	3	3	3	2	2	3	3
22	2	2	2	2	2	2	3	3	3	3	2	2	3	3
23	2	2	2	2	2	2	3	3	3	3	2	2	3	3
24	2	2	2	2	2	2	3	3	3	3	2	2	3	3
25	2	2	2	2	2	2	3	3	3	3	2	2	3	3
26	2	2	2	2	2	2	3	3	3	3	2	2	3	3
27	2	2	2	2	2	2	3	3	3	3	2	2	3	3
28	2	2	2	2	2	2	3	3	3	3	2	2	3	3
29	2	2	2	2	2	2	3	3	3	3	2	2	3	3
30	2	2	2	2	2	2	3	3	3	3	2	2	3	3
31	2	2	2	2	2	2	3	3	3	3	2	2	3	3
32	2	2	2	2	2	2	3	3	3	3	2	2	3	3
33	2	2	2	2	2	2	3	3	3	3	2	2	3	3
34	2	2	2	2	2	2	3	3	3	3	2	2	3	3
35	2	2	2	2	2	2	3	3	3	3	2	2	3	3
36	2	2	2	2	2	2	3	3	3	3	2	2	3	3
37	2	2	2	2	2	2	3	3	3	3	2	2	3	3
38	2	2	2	2	2	2	3	3	3	3	2	2	3	3
39	2	2	2	2	2	2	3	3	3	3	2	2	3	3
40	2	2	2	2	2	2	3	3	3	3	2	2	3	3
41	2	2	2	2	2	2	3	3	3	3	2	2	3	3
42	2	2	2	2	2	2	3	3	3	3	2	2	3	3
43	2	2	2	2	2	2	3	3	3	3	2	2	3	3
44	2	2	2	2	2	2	3	3	3	3	2	2	3	3
45	2	2	2	2	2	2	3	3	3	3	2	2	3	3
46	2	2	2	2	2	2	3	3	3	3	2	2	3	3
47	2	2	2	2	2	2	3	3	3	3	2	2	3	3
48	2	2	2	2	2	2	3	3	3	3	2	2	3	3
49	2	2	2	2	2	2	3	3	3	3	2	2	3	3
50	2	2	2	2	2	2	3	3	3	3	2	2	3	3
51	2	2	2	2	2	2	3	3	3	3	2	2	3	3
52	2	2	2	2	2	2	3	3	3	3	2	2	3	3
53	2	2	2	2	2	2	3	3	3	3	2	2	3	3
54	2	2	2	2	2	2	3	3	3	3	2	2	3	3
55	2	2	2	2	2	2	3	3	3	3	2	2	3	3

MIDDLE SCHOOLS
4 Campuses split: Tier1 / Tier 2
2 Campuses split: Tier2 / Tier3

HIGH SCHOOLS
4 Campuses split: Tier2 / Tier 3
Isolated votes: Tier1

SPECIALTY MS/HS
SBEC / WAIS trending: Tier 1

CENTRAL FACILITIES
Ag Farm split: Tier2 / Tier3
Guthrie clear: Tier3

LRFP Mtg#2 Follow-up | Individual Results: Tier Strategy Sort

55 Voting Participants

	MIDDLE SCHOOLS						HIGH SCHOOLS				SPECIALTY		CENTRAL	
	MMS	NMS	SBMS	SFMS	SOMS	SWMS	MHS	NHS	SWHS	SHS	SBEC	WAIS	AG	Guthrie
TIER 1	14	6	25	41	8	8	5	5	12	5	30	27	2	2
TIER 2	36	21	27	11	39	24	17	27	23	19	20	21	23	5
TIER 3	2	26	1	1	6	21	31	21	18	29	3	4	30	48
"Blank"	3	2	2	2	2	2	2	2	2	2	2	3	0	0
Total Votes Cast	55	55	55	55	55	55	55	55	55	55	55	55	55	55

TIER 1

VOTES	Ranking
41	SFMS
30	SBEC
27	WAIS
25	SBMS
14	MMS
12	SWHS
8	SOMS
8	SWMS
6	NMS
5	MHS
5	NHS
5	SHS
2	AG
2	Guthrie

TIER 2

VOTES	Ranking
39	SOMS
36	MMS
27	SBMS
27	NHS
24	SWMS
23	SWHS
23	AG
21	NMS
21	WAIS
20	SBEC
19	SHS
17	MHS
11	SFMS
5	Guthrie

TIER 3

VOTES	Ranking
48	Guthrie
31	MHS
30	AG
29	SHS
26	NMS
21	SWMS
21	NHS
18	SWHS
6	SOMS
4	WAIS
3	SBEC
2	MMS
1	SBMS
1	SFMS

CAMPUS SORT
55 Committee Member's Input
Tier Strategy Assigned for Each Campus

TIER STRATEGY SORT
55 Committee Member's Input
Campus Ranking under each Tier Strategy

LRFP Committee Mtg #3 Recap: Facilities Assessment Findings....


Project Cost Data

LRFP Mtg#3 New Information | Project Cost Assumptions

COST ANALYSIS

The CTE Facilities Assessment Cost Analysis will include the following Total **PROJECT COST** components:

- **Estimated Hard Costs**
Demolition Costs
Renovation Costs
Equipment Costs
Contingency Allocation
- **Estimated Soft Costs**
Professional Services Fees
Permits, Regulatory Review
Furniture & Equipment
Technology Capacity
Contingency Allocation
- **Estimated Future Cost Projection**
Current Cost – Year 2021
Escalation Rate – adjusting % rate per year over future planning timeline



LRFP Mtg#3 New Information | Project Cost Summary Data

	T1	T2	T3	
	TIER 1	TIER 2	TIER 3	
MIDDLE SCHOOLS				6 MIDDLE SCHOOLS
MEMORIAL	\$3,185,396	\$4,896,253	\$7,717,098	
NORTHBROOK	\$2,637,880	\$4,806,561	\$5,940,438	
SPRING BRANCH	\$3,364,139	\$5,629,381	\$5,259,548	
SPRING FOREST	\$3,011,283	\$4,825,170	\$6,119,572	
SPRING OAKS	\$3,519,157	\$6,706,315	\$6,548,219	
SPRING WOODS	\$3,100,345	\$6,161,640	\$6,015,863	
ROLLING TOTALS	\$18,818,200	\$33,025,320	\$37,600,738	
HIGH SCHOOLS				4 HIGH SCHOOLS
MEMORIAL	\$2,852,619	\$13,667,238	\$14,581,304	
NORTHBROOK	\$4,636,594	\$16,795,737	\$17,975,257	
SPRING WOODS	\$4,807,278	\$15,025,144	\$22,374,224	
STRATFORD	\$4,654,025	\$17,426,609	\$20,180,110	
ROLLING TOTALS	\$16,950,516	\$62,914,728	\$75,110,895	
SPECIALTY SCHOOLS				2 SPECIALTY MS/HS 2 CENTRAL CAMPUS
SBEC	\$1,879,834	\$3,197,184	\$5,811,690	
WAIS	\$2,493,462	\$5,218,069	\$5,809,887	
CENTRAL - AG FARM	\$6,050,701	\$12,954,872	\$25,609,662	
CENTRAL - GUTHRIE	\$10,161,672	\$65,714,172	\$89,166,697	
ROLLING TOTALS	\$20,585,669	\$87,084,297	\$126,397,936	
PROJECT TIER TOTALS	\$56,354,385	\$183,024,345	\$239,109,569	DISTRICT TOTAL
	TIER 1 IN PLACE, AS IS	TIER 2 ADD MISSING + IMPROVE ADJACENCIES	TIER 3 MEET CTE ED SPECIFICATIONS	

- Key Planning Factors:**
- Project Cost Data is based on current costs (Year 2021).
 - Future Cost Data will need to be adjusted based on escalation at appropriate time.

COST ASSUMPTIONS

Soft Cost + Hard Cost = **TOTAL Project Cost**
Current Cost = **\$\$ Yr2021**

SUMMARY TOTALS

Tier Strategy = Tier 1, Tier 2, Tier 3
Building Type = MS, HS, MS/HS, Central

LRFP Committee Mtg #3 Recap: Mtg #3 Engagement Activity....

Achieving “Table” Consensus

CTE LRFP Committee Mtg #2 | LRFP Committee Engagement Activity

“Tools” for the LRFP Table Consensus

CTE Ed Spec Comparison Data
Reference Information

SBISD LRFP Engagement: **TIER STRATEGY** (CTE Ed Spec Comparison)
LRFP Meeting #3

Tier Strategy Gameboard
Agree on Campus Tier

SBISD LRFP Engagement: **TIER STRATEGY** (LRFP Mtg#2 Results)
LRFP Meeting #3

LRFP Timeline Gameboard
Prioritize Project Timing

SBISD LRFP Engagement: **TIMELINE STRATEGY** (Game Board)
LRFP Meeting #3

LRFP Mtg#3 Engagement | Project Timeline Parameters

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
Tier 1 Strategy	TIER 1 12 months	TIER 1 12 months	TIER 1 12 months	TIER 1 12 months	TIER 1 12 months	TIER 1 12 months
Tier 2 Strategy		TIER 2 18 months				
			TIER 2 18 months			
				TIER 2 18 months		
					TIER 2 18 months	
Tier 3 Strategy			TIER 3 24 months			
				TIER 3 24 months		
					TIER 3 24 months	
						TIER 3 24 months

3 6 7 7 6 3

Key Planning Information:

- “**Mid-year completion**” is ideal time to for a project to allow for typical school start (August school start)
- “**Tier Strategy timeline duration**” are proposed construction time frames (12 months, 18 months, 24 months)

LRFP Planning Guidelines

- “**Prioritize**” LRFP Projects on Timeline
Higher Priority: Closer to Year 1
Lower Priority: Closer to Year 6
- **Maximum Limits / Single Year**
3 Middle Schools / Year
2 High Schools / Year
7 Total Projects / Year
- **Helpful Planning Tips**
“Tier 3” projects = Spread across timeline (longest duration)
“Tier 1” projects = Location might be driven by maximum limit / single year

2 STEP PROCESS: Tier → Timeline

Step1 = Achieve Consensus on Tier Strategy

Step2 = Develop Timeline using Guidelines

LRFP TIMELINE PARAMETERS

Timeline: 5 Year Total, Mid-Year Completion

Max Limits/Year: 7 Projects, 3 MS, 2 HS

LRFP Committee Mtg #3 Recap: Mtg #3 Engagement Activity....

Part 1 12 Table | Consensus



LRFP Committee Mtg #3 Recap: Mtg #3 Engagement Activity....

Part 2 4 Group | Consensus



Item

1

LRFP Mtg#3 RESULTS
Tier Strategy + Timeline





LRFP Mtg #3

Results

Seek Consensus:

Part 1

12 Tables

LRFP Committee Mtg #3 RESULTS: Mtg #3 Engagement Activity....

TABLE Consensus



Table 1



Table 2/4/9



Table 3



Table 5



Table 6



Table 7



Table 8



Table 10



Table 11



Table 12

TABLE Results: Tier Strategy

SBISD LRFP
Engagement:

TABLE INPUT: TIER STRATEGY

LRFP Table	MIDDLE SCHOOLS					
	MMS	NMS	SBMS	SFMS	SOMS	SWMS
1	2	2	2	1	2	2
2/4/9	2	3	2	2	2	2
3	2	3	2	1	2	3
5	2	3	2	1	2	2
6	2	3	2	1	2	2
7	2	3	2	1	3	3
8	2	3	3	1	3	2
10	2	3	1	1	2	2
11	2	3	1	1	2	2
12	2	3	3	1	3	3

	MIDDLE SCHOOLS					
	MMS	NMS	SBMS	SFMS	SOMS	SWMS
TIER 1	0	0	2	9	0	0
TIER 2	10	1	6	1	7	7
TIER 3	0	9	2	0	3	3

MIDDLE SCHOOLS

Clear **CONSENSUS** achieved

- **(1) Tier 1 Strategy**
Spring Forest MS
- **(4) Tier 2 Strategy**
Memorial MS
Spring Branch MS
Spring Oaks MS
Spring Woods MS
- **(1) Tier 3 Strategy**
Northbrook MS



TABLE Results: Tier Strategy

SBISD LRFP
Engagement:

TABLE INPUT: TIER STRATEGY

LRFP Table	HIGH SCHOOLS			
	MHS	NHS	SWHS	SHS
1	2	2	2	2
2/4/9	3	3	2	3
3	3	2	2	3
5	3	3	2	3
6	3	2	2	3
7	3	3	3	3
8	3	3	3	3
10	3	2	2	3
11	3	2	2	3
12	3	3	3	2

	HIGH SCHOOLS			
	MHS	NHS	SWHS	SHS
TIER 1	0	0	0	0
TIER 2	1	5	7	2
TIER 3	9	5	3	8

HIGH SCHOOLS

Clear **CONSENSUS** achieved at every campus except one

- **(1) Tier 2 Strategy**
Spring Woods HS
- **(1) Split Strategy Tier2/Tier3**
Northbrook HS
- **(2) Tier 3 Strategy**
Memorial HS
Stratford HS



TABLE Results: Tier Strategy

SBISD LRFP
Engagement:

TABLE INPUT: TIER STRATEGY

LRFP Table	SPECIALTY		CENTRAL	
	SBEC	WAIS	AG	Guthrie
1	1	1	2	3
2/4/9	1	1	3	3
3	1	1	3	3
5	1	1	3	3
6	1	2	2	3
7	1	1	3	3
8	1	1	3	3
10	1	1	3	3
11	1	1	3	3
12	1	1	3	3

	SPECIALTY		CENTRAL	
	SBEC	WAIS	AG	Guthrie
TIER 1	10	9	0	0
TIER 2	0	1	2	0
TIER 3	0	0	8	10

SPECIALTY SCHOOLS

Clear **CONSENSUS** achieved

- **(2) Tier 1 Strategy**
SBEC
WAIS

CENTRAL CAMPUS

Clear **CONSENSUS** achieved

- **(2) Tier 3 Strategy**
Ag Farm
Guthrie Center



TABLE Results: Preliminary LRFP Timeline

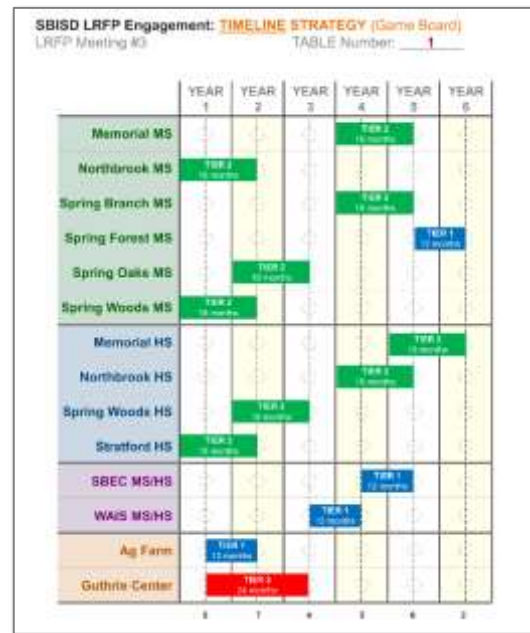


Table 1

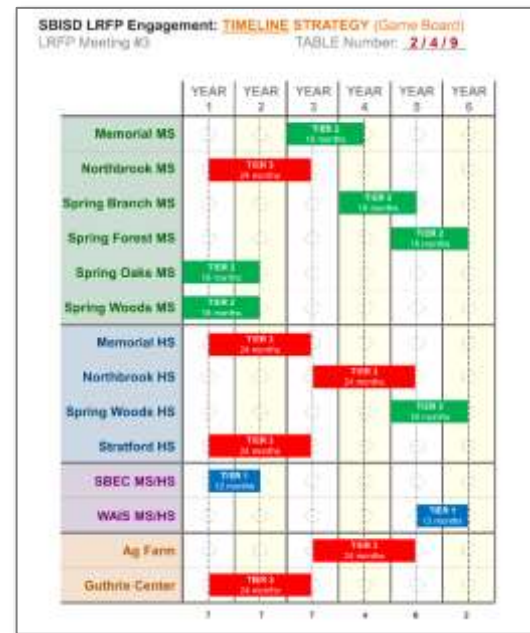


Table 2/4/9



Table 3



Table 5

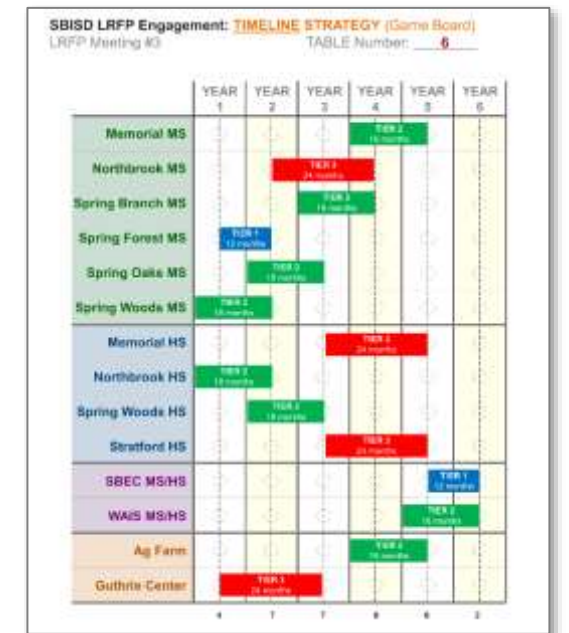


Table 6



Table 7

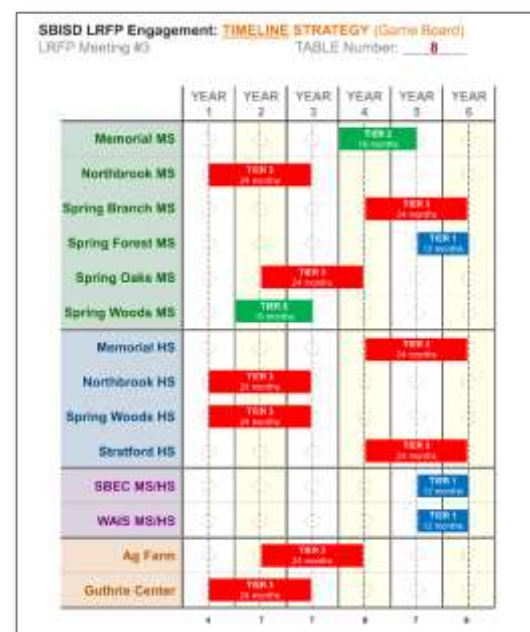


Table 8

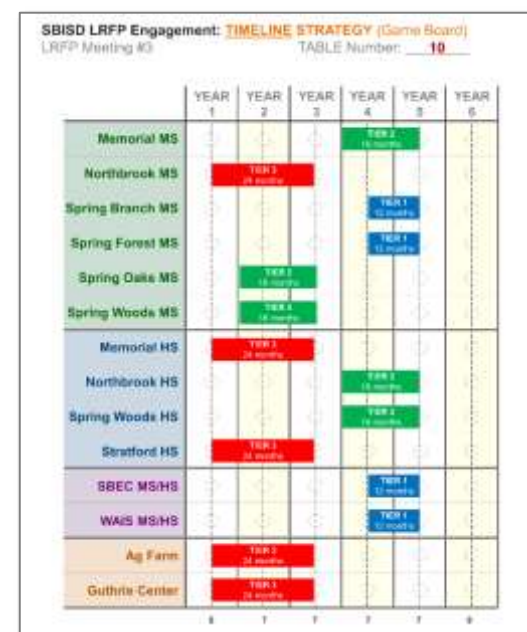


Table 10



Table 11



Table 12



LRFP Mtg #3

Results



Seek Consensus:

Part 2

4 Groups

LRFP Committee Mtg #3 RESULTS: Mtg #3 Engagement Activity....

GROUP Consensus

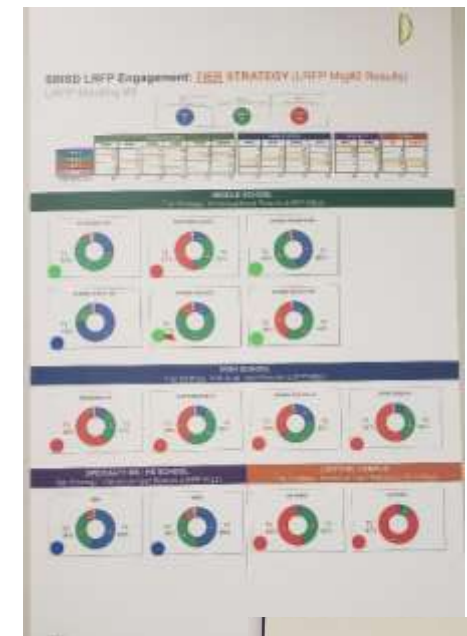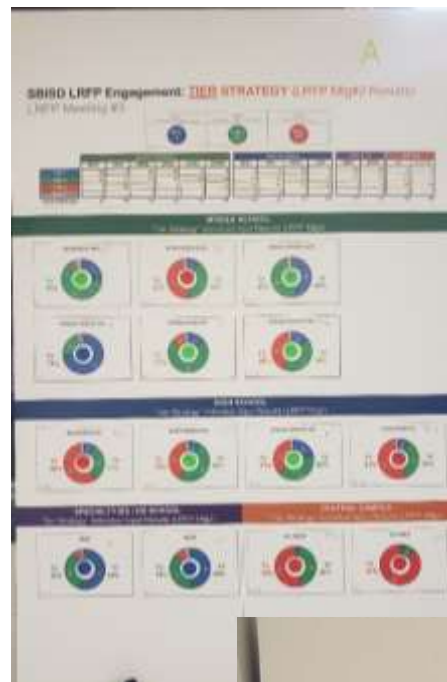

Group A
Tables 1, 3, 5

Group B
Tables 2, 4/9, 6

Group C
Tables 7, 11

Group D
Tables 8, 10, 12

GROUP Results: Tier Strategy

SBISD LRFP
Engagement:

GROUP INPUT: TIER STRATEGY

LRFP Table	MIDDLE SCHOOLS					
	MMS	NMS	SBMS	SFMS	SOMS	SWMS
A	2	3	2	1	2	2
B	2	3	2	1	2	2
C	2	3	1	1	3	3
D	2	3	2	1	2	2

	MIDDLE SCHOOLS					
	MMS	NMS	SBMS	SFMS	SOMS	SWMS
TIER 1	0	0	1	4	0	0
TIER 2	4	0	3	0	3	3
TIER 3	0	4	0	0	1	1

MIDDLE SCHOOLS

Clear **CONSENSUS** achieved

- **(1) Tier 1 Strategy**
Spring Forest MS
- **(4) Tier 2 Strategy**
Memorial MS
Spring Branch MS
Spring Oaks MS
Spring Woods MS
- **(1) Tier 3 Strategy**
Northbrook MS



SAME Tier Strategy Pattern as 12 Tables

GROUP Results: Tier Strategy

SBISD LRFP
Engagement:

GROUP INPUT: TIER STRATEGY

LRFP Table	HIGH SCHOOLS			
	MHS	NHS	SWHS	SHS
A	3	2	2	3
B	3	3	2	3
C	3	3	2	3
D	3	3	3	3

	HIGH SCHOOLS			
	MHS	NHS	SWHS	SHS
TIER 1	0	0	0	0
TIER 2	0	1	3	0
TIER 3	4	3	1	4

HIGH SCHOOLS

Clear **CONSENSUS** achieved

- **(1) Tier 2 Strategy**
Spring Woods HS
- **(3) Tier 3 Strategy**
Memorial HS
Northbrook HS
Stratford HS



*SAME Tier Strategy Pattern as 12 Tables
Tie broken at NHS*

GROUP Results: Tier Strategy

SBISD LRFP
Engagement:

GROUP INPUT: TIER STRATEGY

LRFP Table	SPECIALTY		CENTRAL	
	SBEC	WAIS	AG	Guthrie
A	1	1	3	3
B	1	2	2	3
C	1	1	3	3
D	1	1	3	3

	SPECIALTY		CENTRAL	
	SBEC	WAIS	AG	Guthrie
TIER 1	4	3	0	0
TIER 2	0	1	1	0
TIER 3	0	0	3	4

SPECIALTY SCHOOLS

Clear **CONSENSUS** achieved

- **(2) Tier 1 Strategy**

SBEC

WAIS

CENTRAL CAMPUS

Clear **CONSENSUS** achieved

- **(2) Tier 3 Strategy**


Ag Farm

Guthrie Center




SAME Tier Strategy Pattern as 12 Tables


GROUP Results: LRFP Timeline

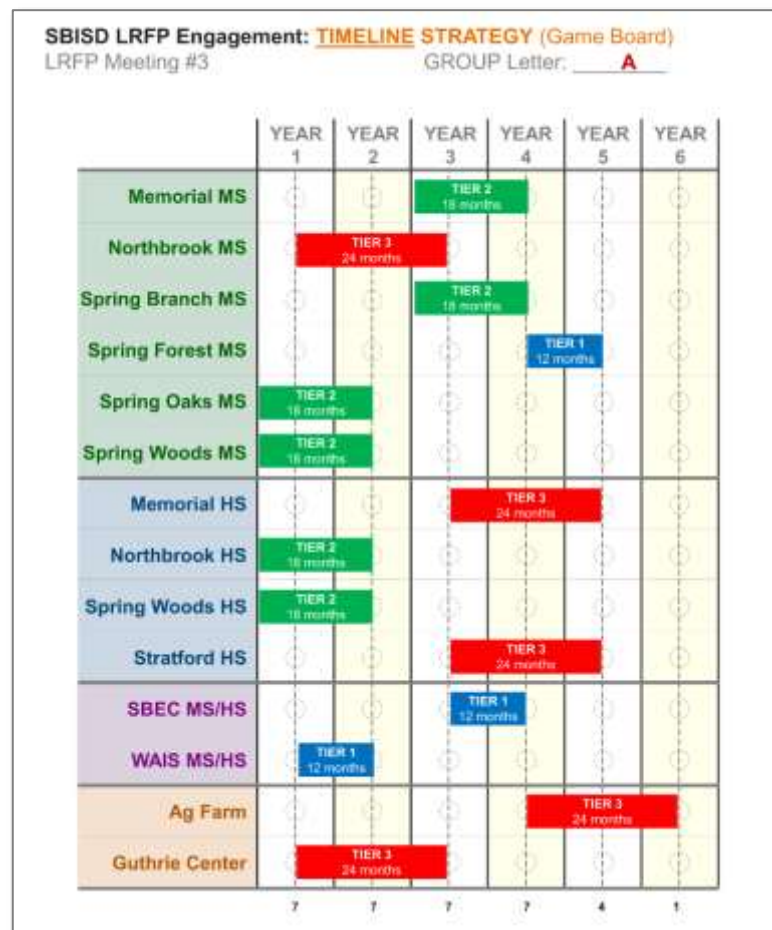


Group A
Tables 1, 3, 5

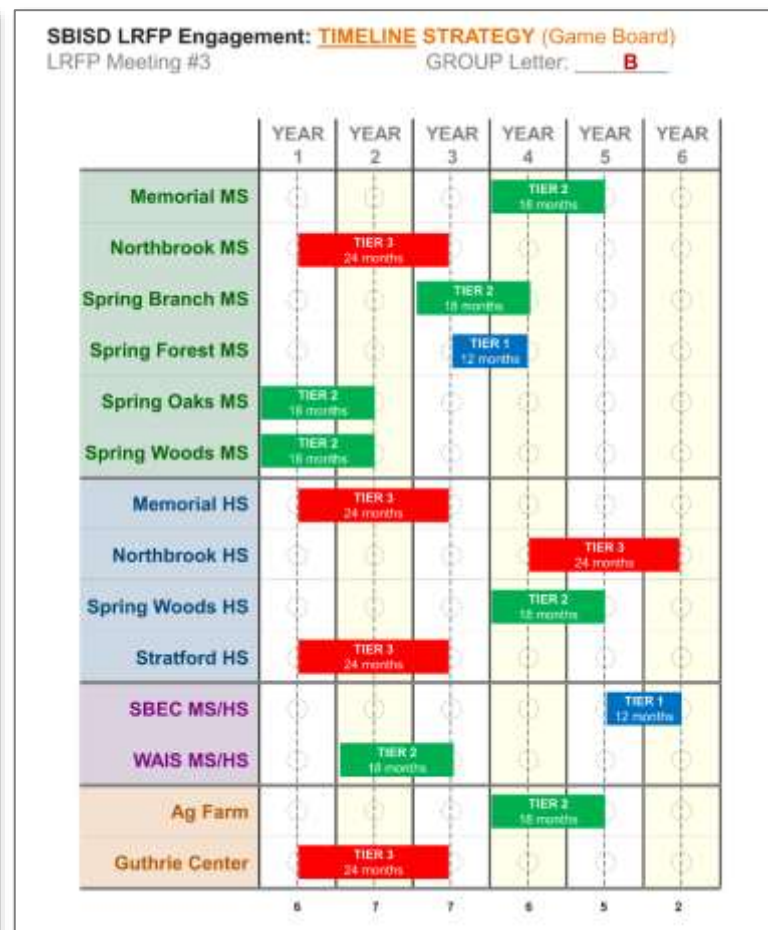

Group B
Tables 2, 4/9, 6

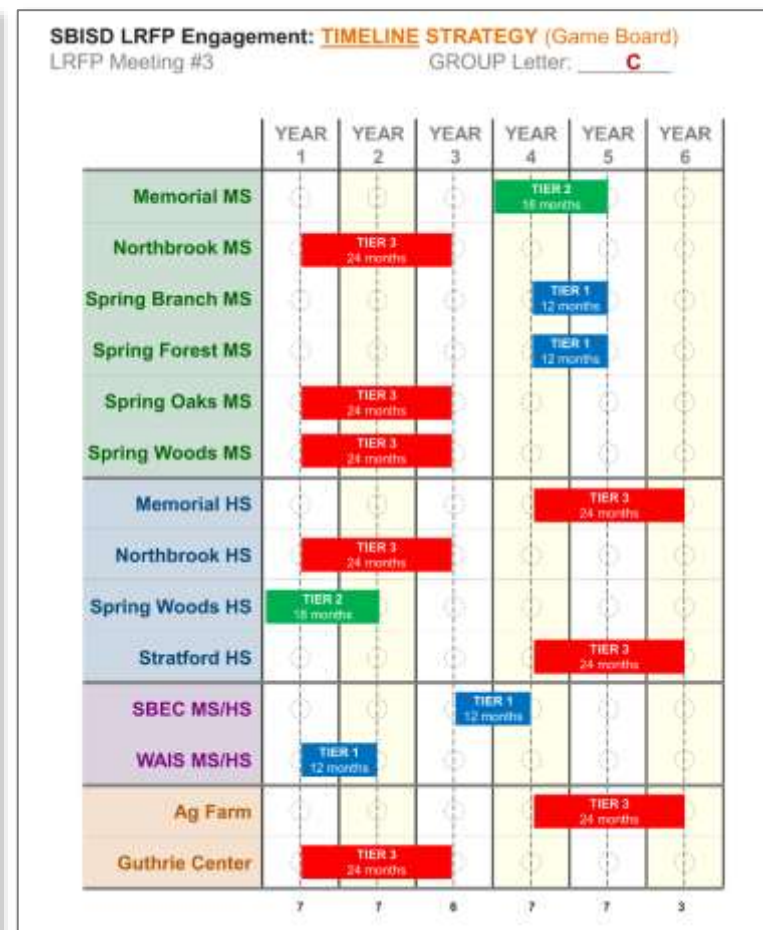

Group C
Tables 7, 11

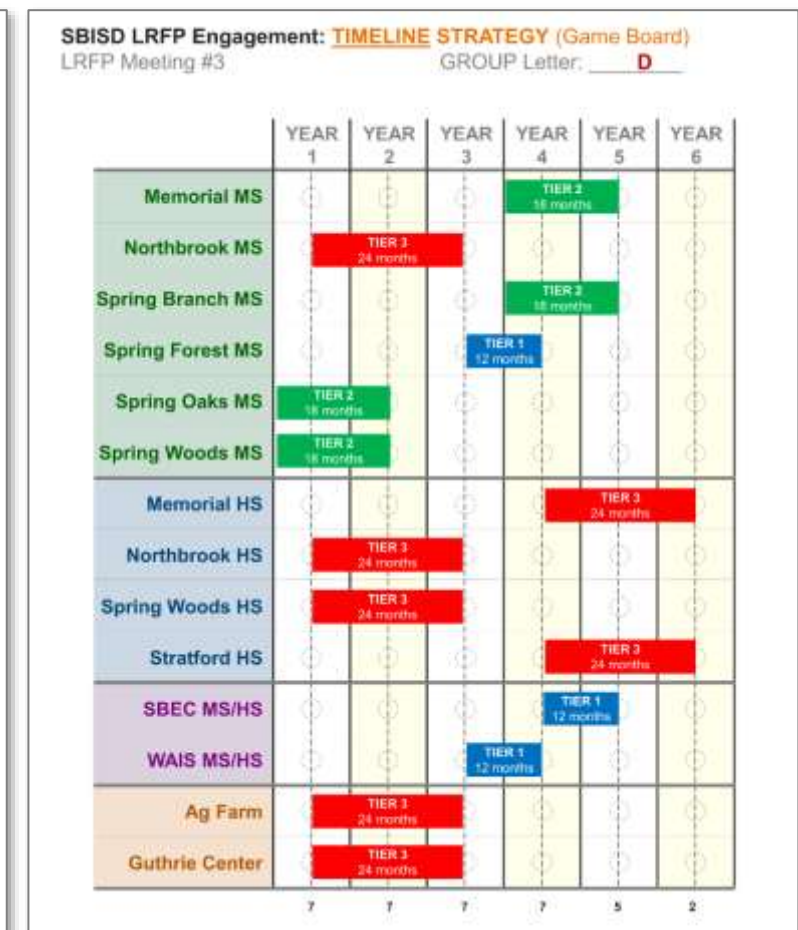

Group D
Tables 8, 10, 12

A photograph showing several hands raised against a green chalkboard background. The hands are of various skin tones and are positioned at different heights, suggesting a group of people participating in a discussion or asking questions. The lighting is soft, and the overall tone is educational and collaborative.

Questions?

Item

2

**LRFP Committee Mtg #4
Engagement Exercise:**



**REVIEW “DRAFT” RECOMMENDATION
Committee Discuss → Consensus Vote**


“Finalize” CTE LRFP Recommendation

REVIEW/DISCUSS “CTE LRFP Recommendation”
Built from LRFP Mtg#3 CONSENSUS Agreement!

- ➔ **1** ➔ **REVIEW Recommendation – Facilitated Committee Discussion**
 - “Tier Strategy” for each campus
 - “Proposed LRFP Timeline” for 14 projects
- 2** ➔ **FORMALIZE Recommendation - Individual Input**
 - “Consensus Vote” for Final CTE Recommendation
 - “Feedback” on the LRFP Process

CTE LRFP Recommendation: Tier Strategy + Timeline

Based on “Consensus” established from Individual and Group Input

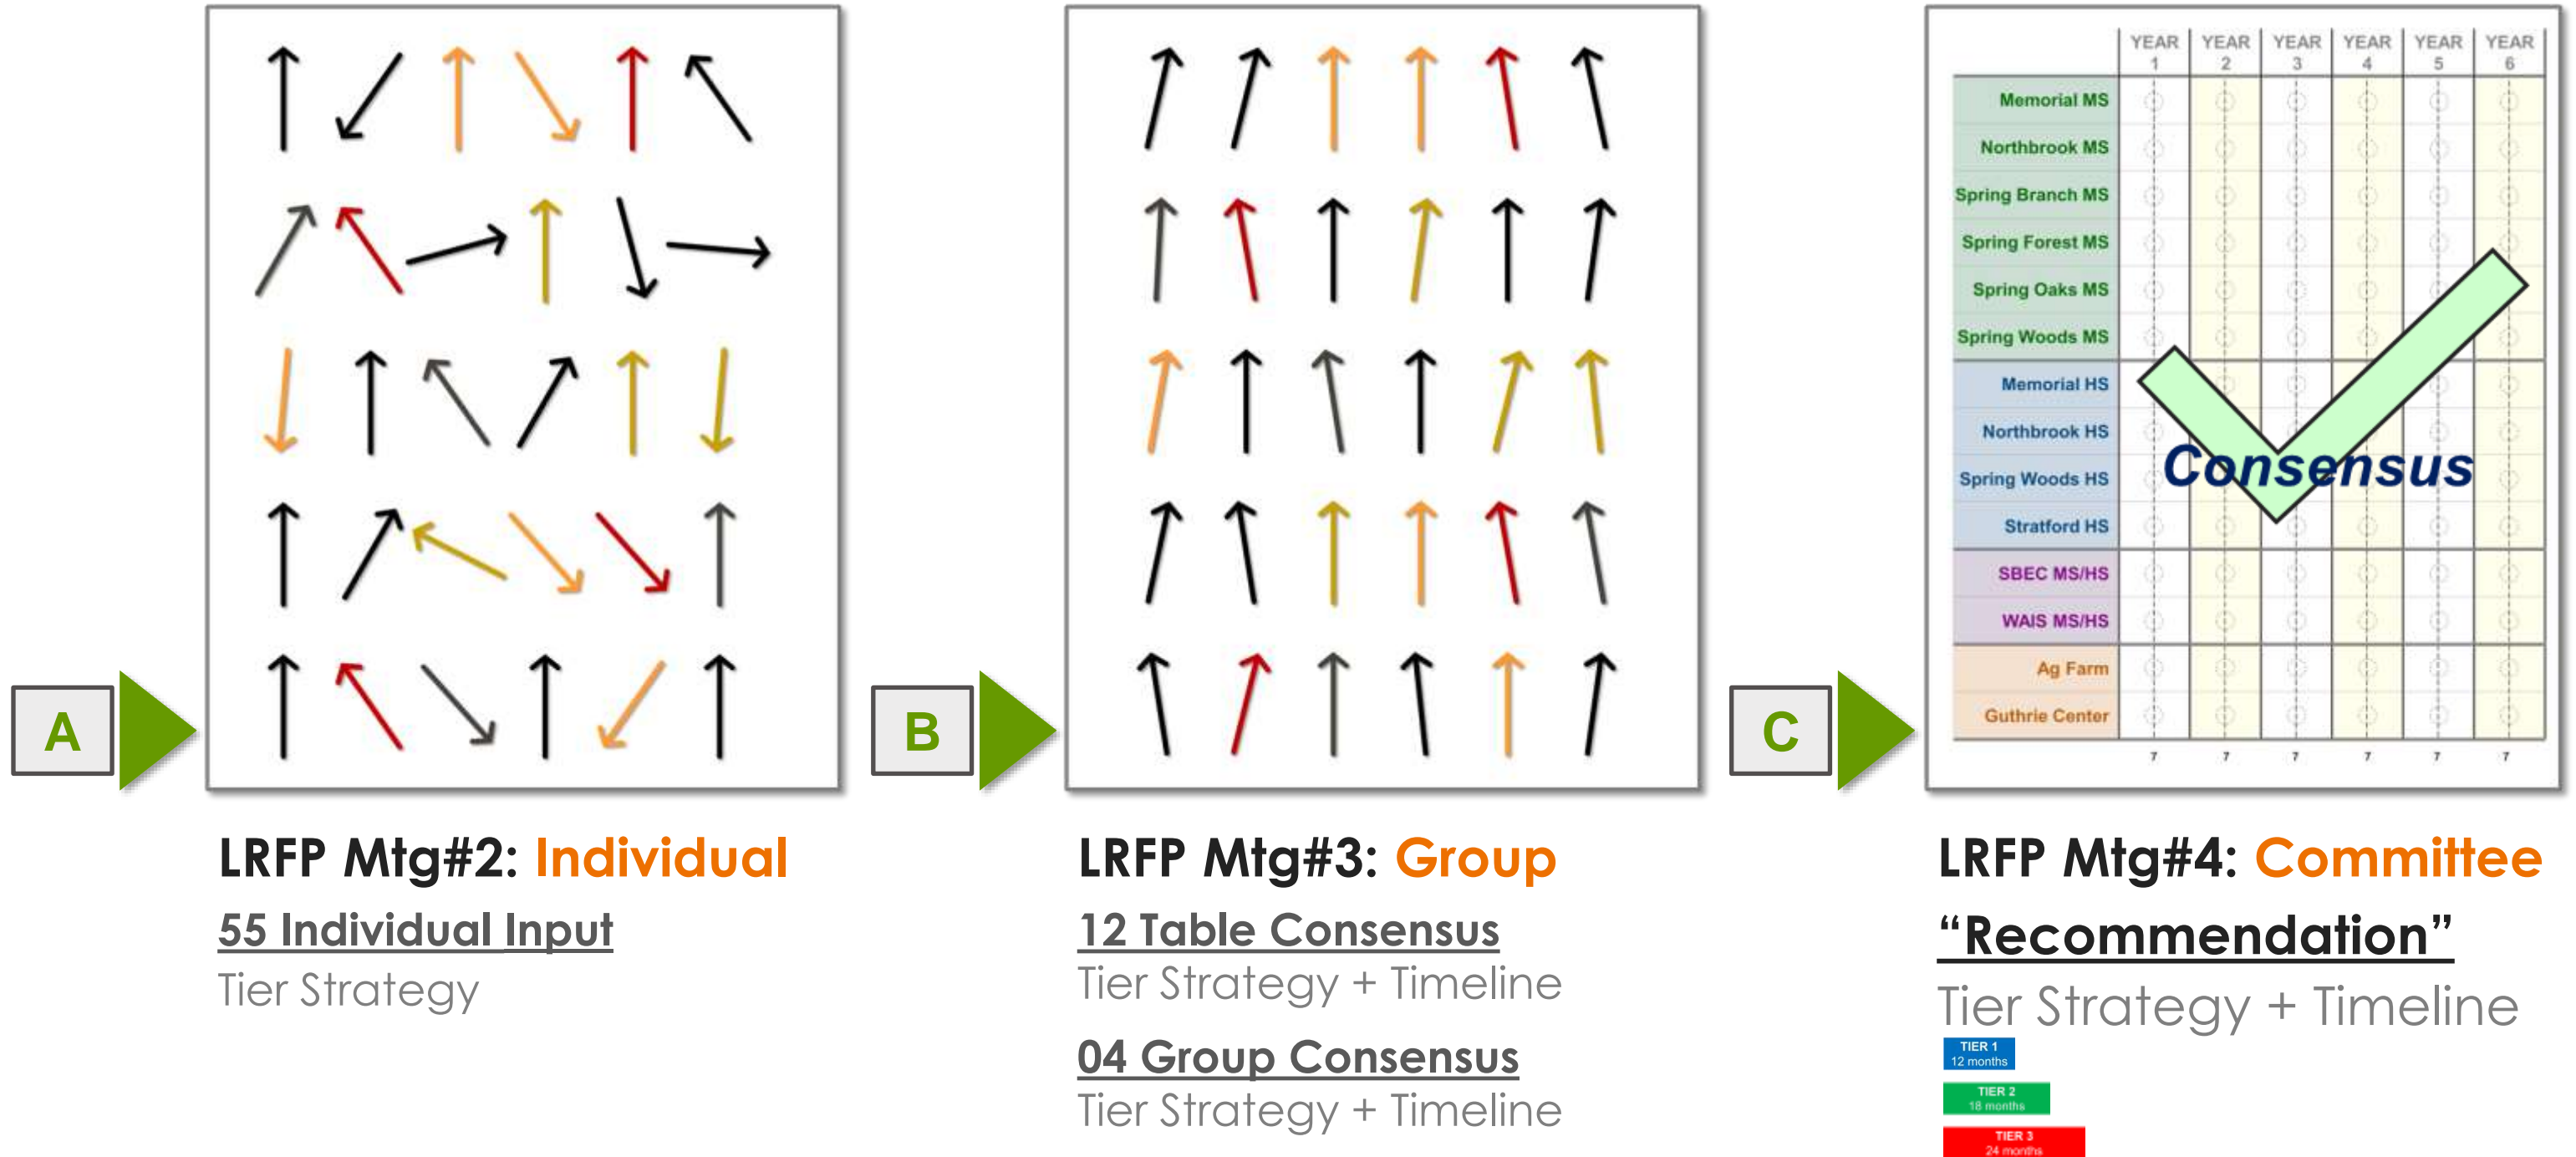

REVIEW: CTE LRFP Recommendation


Tier Strategy + Timeline



LRFP Committee Mtg #3 RESULTS:

Mtg #3 Engagement Activity....

GROUP Consensus

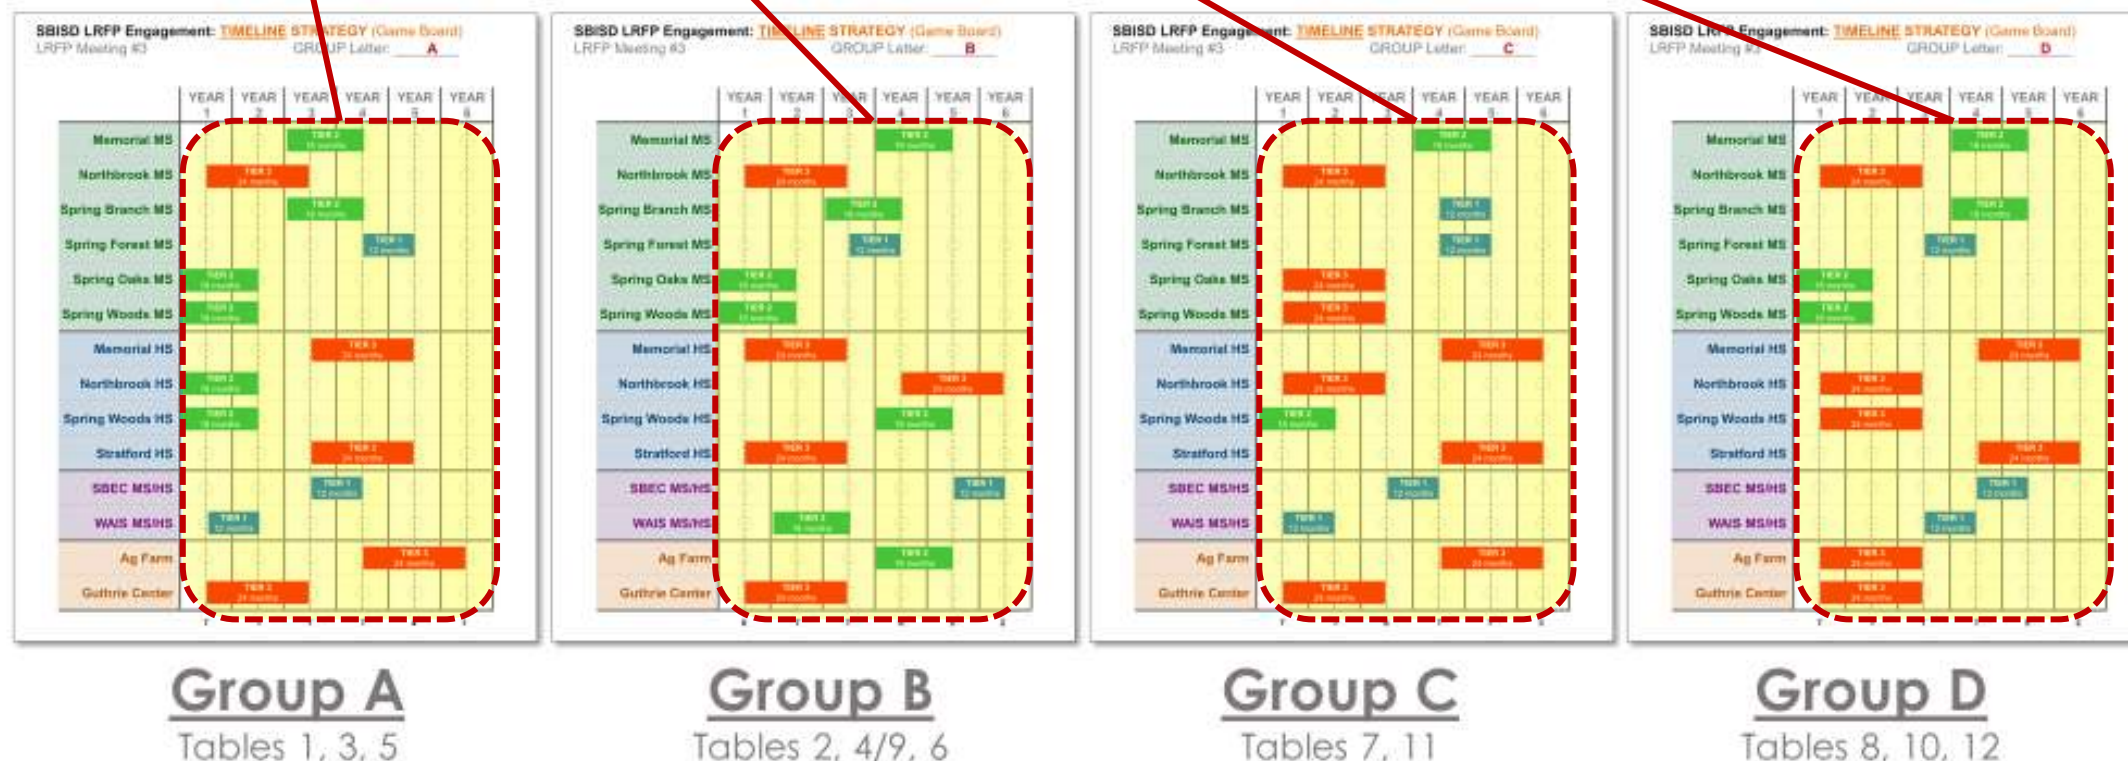

Key Planning Information:

- “**Mid-year completion**” is ideal time to for a project to allow for typical school start (August school start)
- “**Tier Strategy timeline duration**” are proposed construction time frames (12 months, 18 months, 24 months)

LRFP Planning Guidelines

- “**Prioritize**” LRFP Projects on Timeline
Higher Priority: Closer to Year 1
Lower Priority: Closer to Year 6
- **Maximum Limits / Single Year**
3 Middle Schools / Year
2 High Schools / Year
7 Total Projects / Year
- **Helpful Planning Tips**
“Tier 3” projects = Spread across timeline (longest duration)
“Tier 1” projects = Location might be driven by maximum limit / single year

Tier Strategy = Consensus Achieved!

(Group Results = Same Pattern as 12 Tables Results)

	MIDDLE SCHOOLS						HIGH SCHOOLS				SPECIALTY		CENTRAL	
	MMS	NMS	SBMS	SFMS	SOMS	SWMS	MHS	NHS	SWHS	SHS	SBEC	WAIS	AG	Guthrie
TIER 1	0	0	1	4	0	0	0	0	0	0	4	3	0	0
TIER 2	4	0	3	0	3	3	0	1	3	0	0	1	1	0
TIER 3	0	4	0	0	1	1	4	3	1	4	0	0	3	4

Middle Schools

- (T2) Memorial
- (T3) Northbrook
- (T2) Spring Branch
- (T1) Spring Forest
- (T2) Spring Oaks
- (T2) Spring Woods

High Schools

- (T3) Memorial
- (T3) Northbrook
- (T2) Spring Woods
- (T3) Stratford

Specialty MS/HS

- (T1) SBEC MS/HS
- (T1) WAIS MS/HS


Central Campus

- (T3) Ag Farm
- (T3) Guthrie


	TIER 1	TIER 2	TIER 3
Memorial MS		Memorial MS	
Northbrook MS			Northbrook MS
Spring Branch MS		Spring Branch MS	
Spring Forest MS	Spring Forest MS		
Spring Oaks MS		Spring Oaks MS	
Spring Woods MS		Spring Woods MS	
Memorial HS			Memorial HS
Northbrook HS			Northbrook HS
Spring Woods HS		Spring Woods HS	
Stratford HS			Stratford HS
SBEC MS/HS	SBEC MS/HS		
WAIS MS/HS	WAIS MS/HS		
Ag Farm			Ag Farm
Guthrie Center			Guthrie Center

Timeline Recommendation = Consensus Achieved!


Based on LRFP Mtg#3 GROUP Results

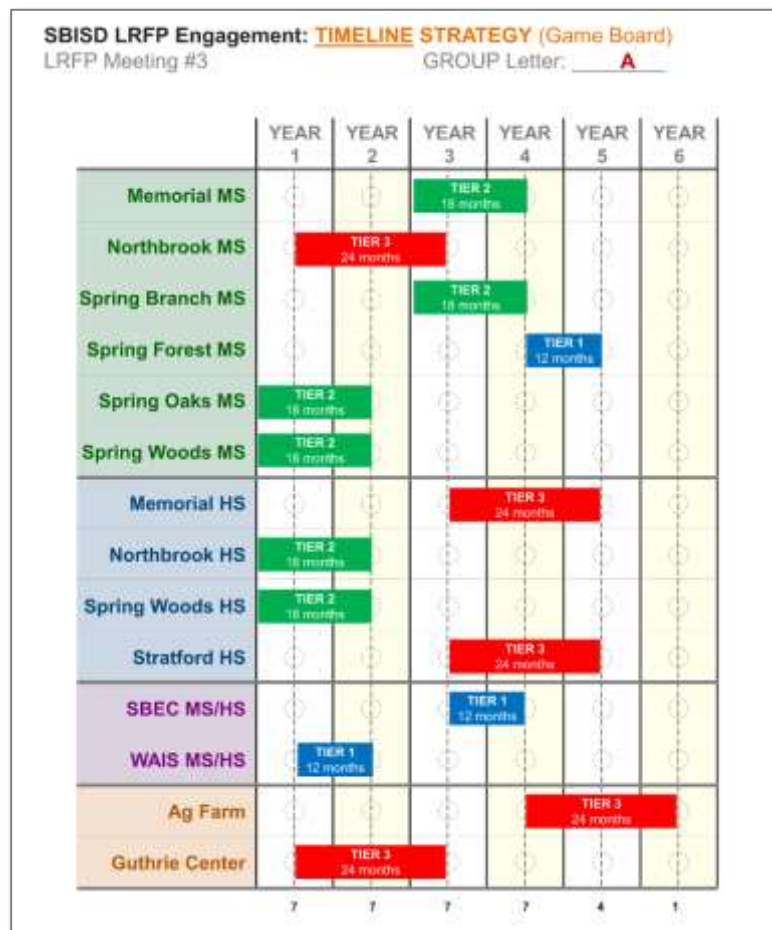


Group A
Tables 1, 3, 5

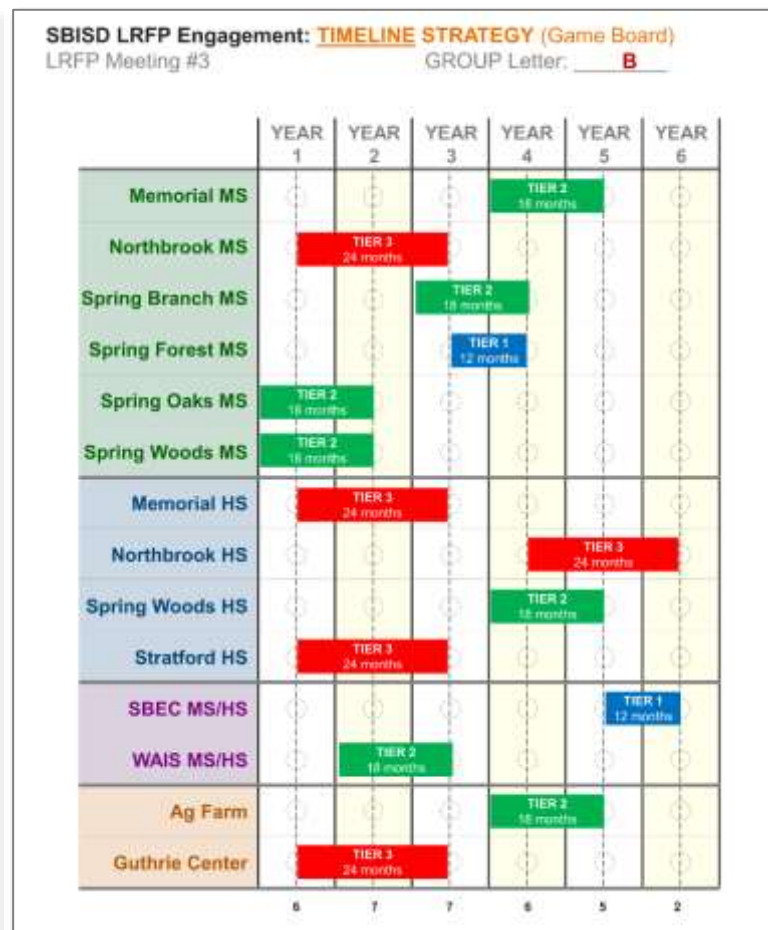


Group B
Tables 2, 4/9, 6

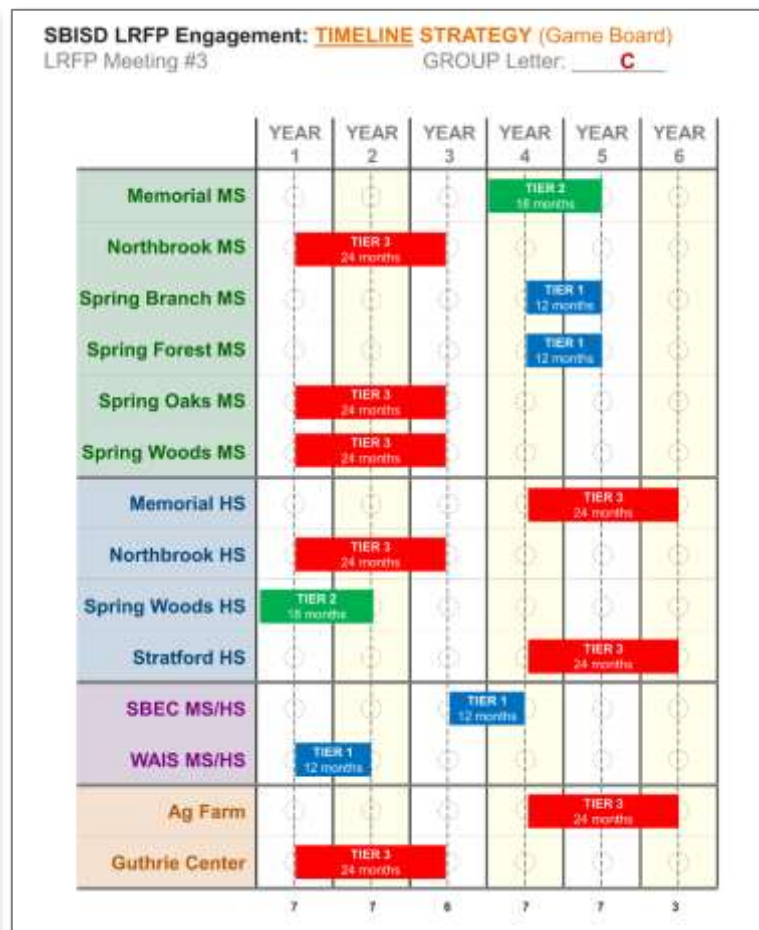

Group C
Tables 7, 11

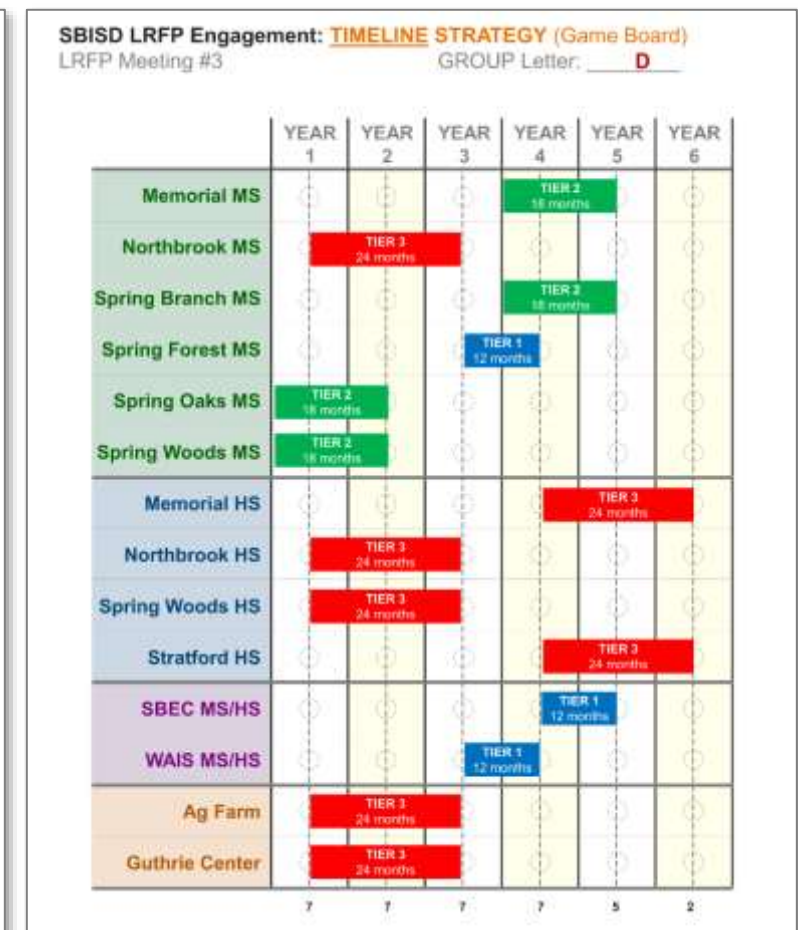

Group D
Tables 8, 10, 12

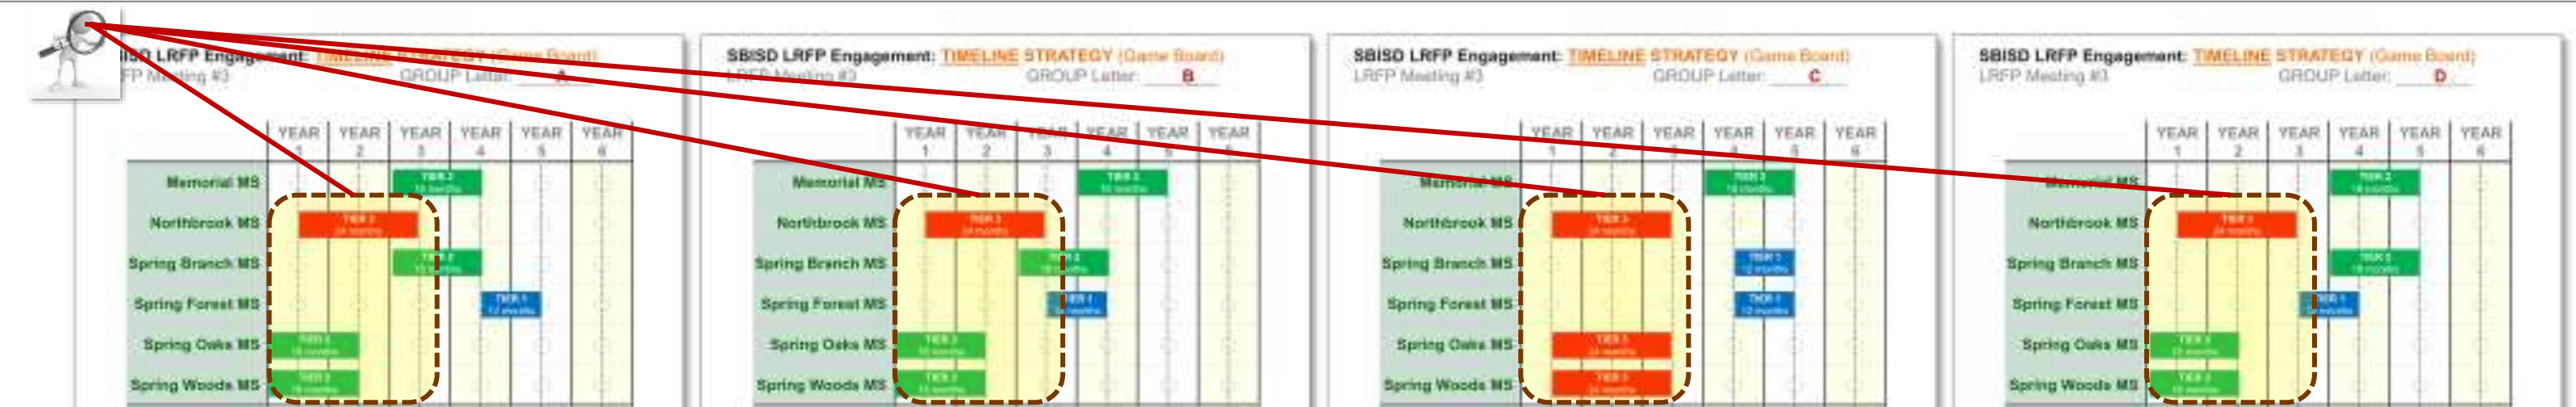


MIDDLE SCHOOLS

CTE LRFP Timeline = Consensus!

Timeline Development Notes:

- **Follow Planning Guideline**
3 MS/ Year Max Limit
- **Group1 Schools = “Locked in” Year1**
Northbrook MS
Spring Oaks MS
Spring Woods MS

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
Memorial MS	○	○	○	○	○	○
Northbrook MS	★ TIER 3 24 months	○	○	○	○	○
Spring Branch MS	○	○	○	○	○	○
Spring Forest MS	○	○	○	○	○	○
Spring Oaks MS	★ TIER 2 18 months	○	○	○	○	○
Spring Woods MS	★ TIER 2 18 months	○	○	○	○	○

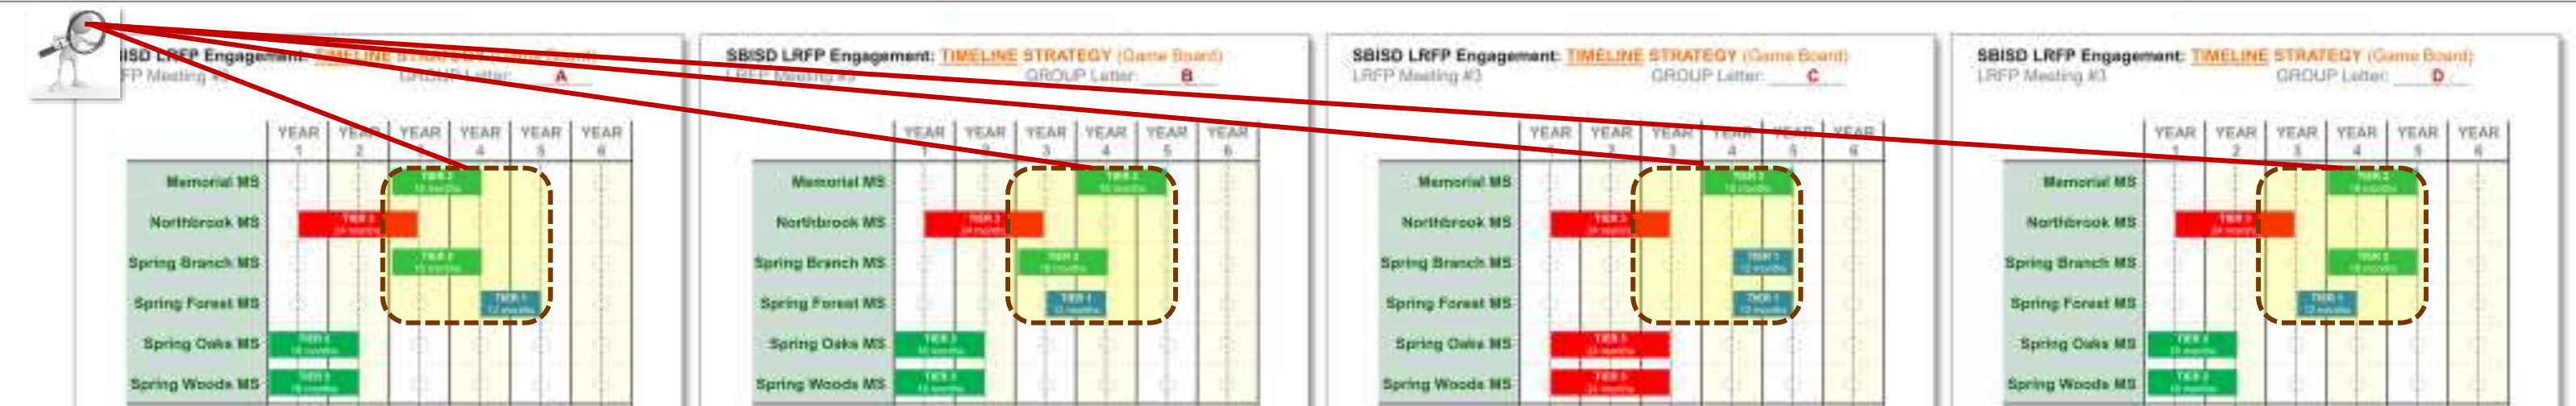

MIDDLE SCHOOLS

CTE LRFP Timeline = Consensus!

Timeline Development Notes:

- **Follow Planning Guideline**
3 MS/ Year Max Limit
- **Group1 Schools = “Locked in” Year1**
Northbrook MS
Spring Oaks MS
Spring Woods MS
- **Follow Planning Guideline**
7 Projects/Year Max Limit
- **Group2 Schools = “Maximize Yr3 Impact”**
SMS + SFMS start in Year3
MMS start in Year4

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
Memorial MS				TIER 2 18 months		
Northbrook MS	★ TIER 3 24 months			Group 2		
Spring Branch MS			TIER 2 18 months			
Spring Forest MS			TIER 1 12 months			
Spring Oaks MS	★ TIER 2 18 months					
Spring Woods MS	★ TIER 2 18 months					




HIGH SCHOOLS

CTE LRFP Timeline = Consensus!

Timeline Development Notes:

- **Follow Planning Guideline**
2 MS/ Year Max Limit
- **Pair1 Schools = “Locked in” Year1**
Northbrook HS
Spring Woods MS

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
Memorial HS						
Northbrook HS	★ TIER 3 24 months					
Spring Woods HS	★ TIER 2 18 months					
Stratford HS	Pair 1					

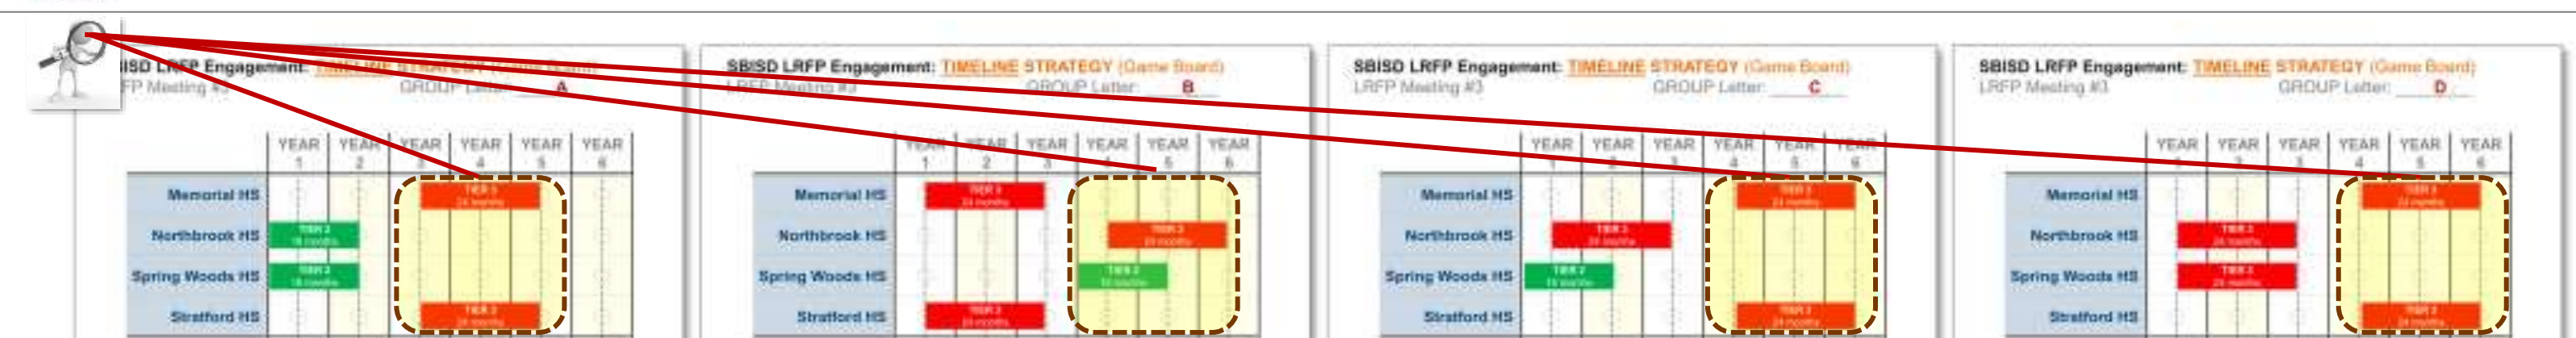



HIGH SCHOOLS

CTE LRFP Timeline = Consensus!

Timeline Development Notes:

- **Follow Planning Guideline**
2 MS/ Year Max Limit
- **Pair1 Schools = “Locked in” Year1**
Northbrook HS
Spring Woods MS
- **Follow Planning Guideline**
7 Projects/Year Max Limit
- **Pair2 Schools = Year 4 Start**
Memorial HS
Stratford HS

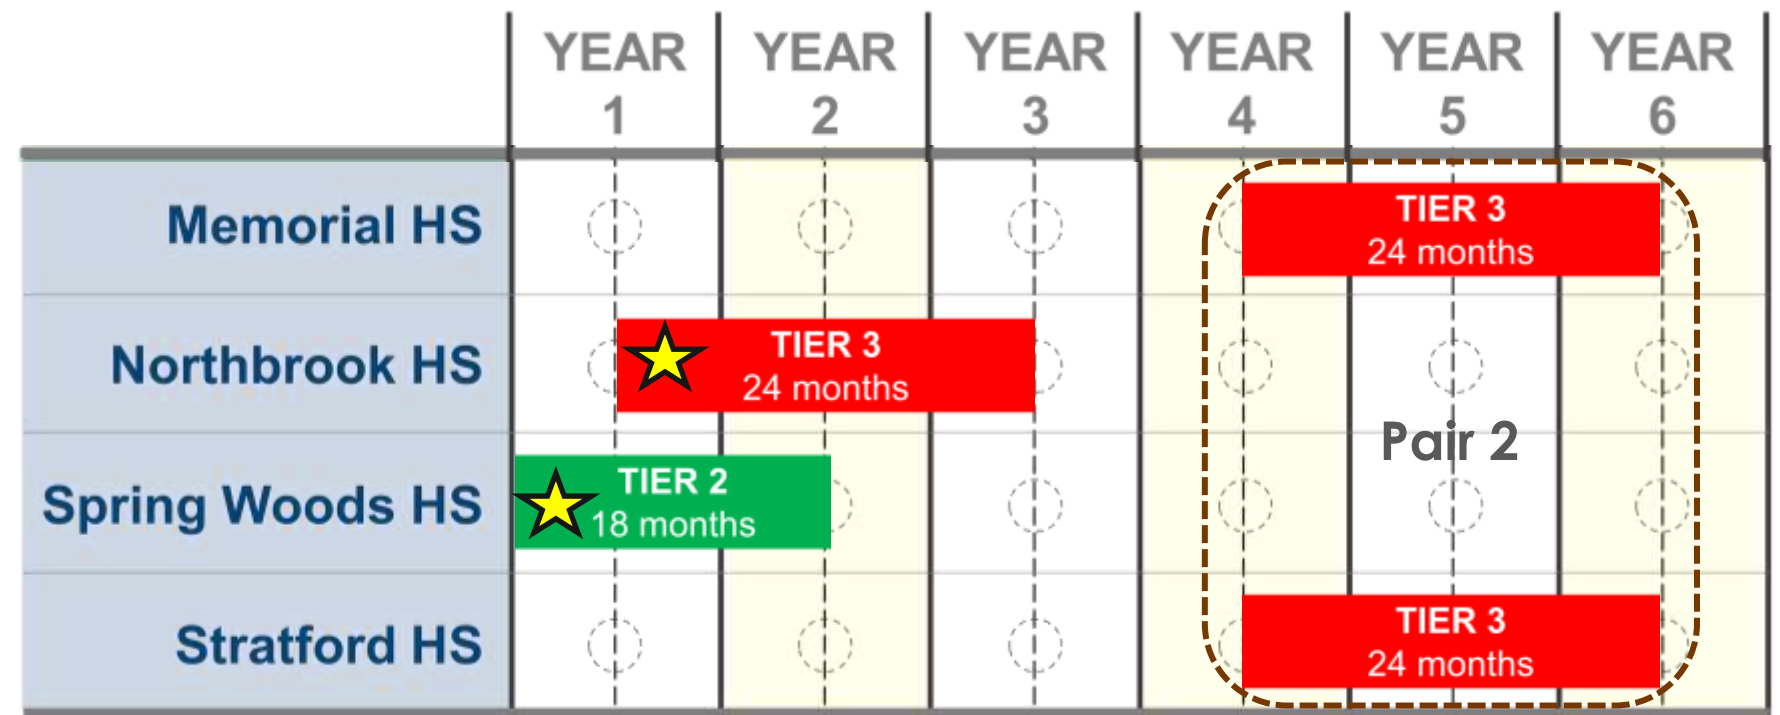

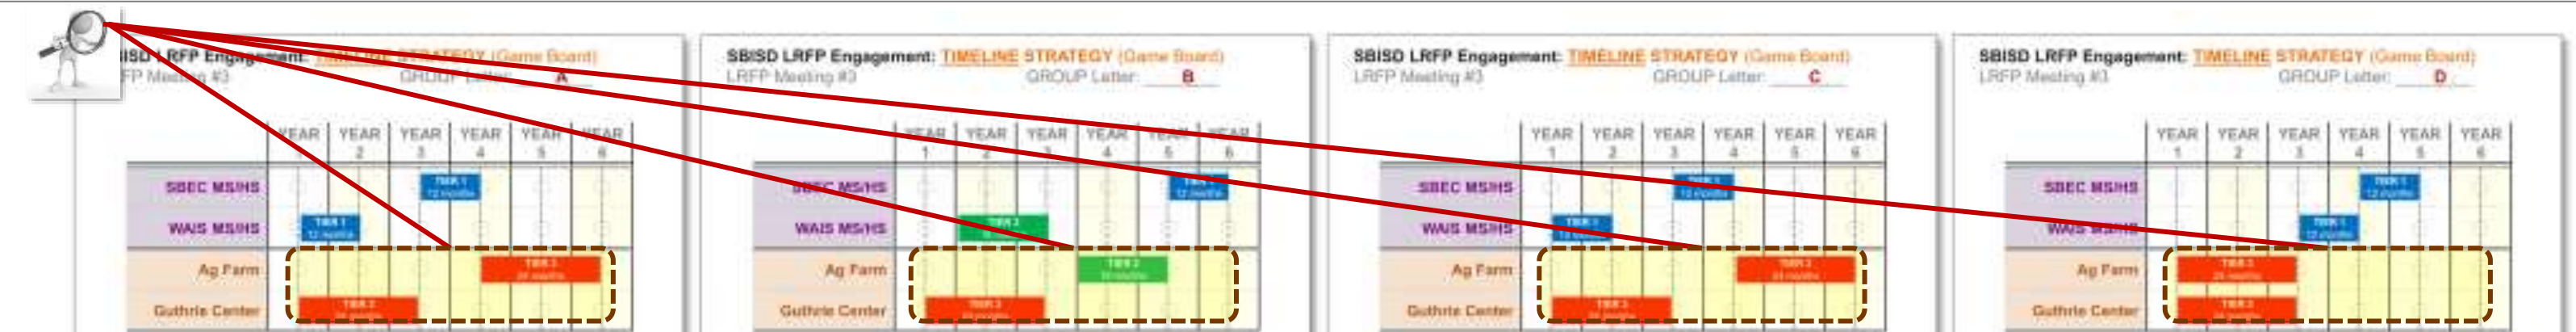

Specialty MS/HS + Central Campus

CTE LRFP Timeline = Consensus!

Timeline Development Notes:

- **Follow Planning Guideline**
7 Projects / Year Max Limit
- **Central Campus = “Locked in”**
Guthrie = Yr1 for all 4 Groups
Ag Farm = Follows based on Consensus

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
SBEC MS/HS	○	○	○	○	○	○
WAIS MS/HS	○	○	○	○	○	○
Ag Farm	○	○	○	★ TIER 3 24 months		
Guthrie Center	★ TIER 3 24 months					



Specialty MS/HS + Central Campus

CTE LRFP Timeline = Consensus!

Timeline Development Notes:

- **Follow Planning Guideline**
7 Projects / Year Max Limit
- **Central Campus = “Locked in”**
Guthrie = Yr1 for all 4 Groups
Ag Farm = Follows based on Consensus
- **Specialty MS/HS = Follow Planning Guideline**
WAIS higher priority in all 4 Groups
SBEC = Follows based on Consensus

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
SBEC MS/HS					TIER 1 12 months	
WAIS MS/HS				TIER 1 12 months		
Ag Farm				★ TIER 3 24 months		
Guthrie Center	★ TIER 3 24 months					

“Formalize” CTE LRFP Recommendation

REVIEW/DISCUSS “CTE LRFP Recommendation”
Built from LRFP Mtg#3 CONSENSUS Agreement!



1



REVIEW Recommendation – Facilitated Committee Discussion

- “Tier Strategy” for each campus
- “Proposed LRFP Timeline” for 14 projects



2



FORMALIZE Recommendation - Individual Input

- “Consensus Vote” for Final CTE Recommendation
- “Feedback” on the LRFP Process

Final Recommendation: LRFP Timeline Summary

Key Planning Information:

- **“Mid-year completion”** is ideal time to for a project to allow for typical school start (August school start)
- **“Tier Strategy timeline duration”** are proposed construction time frames (12 months, 18 months, 24 months)

LRFP Planning Guidelines

- **“Prioritize” LRFP Projects on Timeline**
Higher Priority: Closer to Year 1
Lower Priority: Closer to Year 6
- **Maximum Limits / Single Year**
3 Middle Schools / Year
2 High Schools / Year
7 Total Projects / Year
- **Helpful Planning Tips**
“Tier 3” projects = Spread across timeline (longest duration)
“Tier 1” projects = Location might be driven by maximum limit / single year

	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5	YEAR 6
Memorial MS				TIER 2 18 months		
Northbrook MS	TIER 3 24 months					
Spring Branch MS			TIER 2 18 months			
Spring Forest MS			TIER 1 12 months			
Spring Oaks MS	TIER 2 18 months					
Spring Woods MS	TIER 2 18 months					
Memorial HS				TIER 3 24 months		
Northbrook HS	TIER 3 24 months					
Spring Woods HS	TIER 2 18 months					
Stratford HS				TIER 3 24 months		
SBEC MS/HS					TIER 1 12 months	
WAIS MS/HS				TIER 1 12 months		
Ag Farm				TIER 3 24 months		
Guthrie Center	TIER 3 24 months					
	6	6	5	7	6	4

Final Recommendation: Tier Strategy + Total Project Cost Data Summary

TIER STRATEGY SUMMARY

Tier Strategy = Tier 1, Tier 2, Tier 3
Building Type = MS, HS, MS/HS, Central

	TIER 1	TIER 2	TIER 3
Memorial MS		Memorial MS	
Northbrook MS			Northbrook MS
Spring Branch MS		Spring Branch MS	
Spring Forest MS	Spring Forest MS		
Spring Oaks MS		Spring Oaks MS	
Spring Woods MS		Spring Woods MS	
Memorial HS			Memorial HS
Northbrook HS			Northbrook HS
Spring Woods HS		Spring Woods HS	
Stratford HS			Stratford HS
SBEC MS/HS	SBEC MS/HS		
WAIS MS/HS	WAIS MS/HS		
Ag Farm			Ag Farm
Guthrie Center			Guthrie Center

COST ASSUMPTIONS

Soft Cost + Hard Cost = TOTAL Project Cost
Current Cost = \$\$ Yr2021

	\$	\$\$\$	\$\$\$\$
	TIER 1	TIER 2	TIER 3
MIDDLE SCHOOLS			\$32,345,310
MEMORIAL		\$4,896,253	
NORTHBROOK			\$5,940,438
SPRING BRANCH		\$5,629,381	
SPRING FOREST	\$3,011,283		
SPRING OAKS		\$6,706,315	
SPRING WOODS		\$6,161,640	
ROLLING TOTALS	\$3,011,283	\$23,393,589	\$5,940,438
HIGH SCHOOLS			\$67,761,815
MEMORIAL			\$14,581,304
NORTHBROOK			\$17,975,257
SPRING WOODS		\$15,025,144	
STRATFORD			\$20,180,110
ROLLING TOTALS	\$0	\$15,025,144	\$52,736,671
SPECIALTY SCHOOLS			\$118,883,999
SBEC	\$1,879,834		
WAIS	\$2,493,462		
CENTRAL - AG FARM			\$25,462,662
CENTRAL - GUTHRIE			\$89,048,041
ROLLING TOTALS	\$4,373,296	\$0	\$114,510,703
TOTAL BY TIER	\$7,384,579	\$38,418,733	\$173,187,812
TECHNOLOGY SYSTEM CAPACITY			\$12,100,000
LRFPC RECOMMENDATION			\$231,091,124

“FINAL” Recommendation: Final Individual Input – **CONSENSUS VOTE**

CTE Long Range Facility Plan Process

Individual Consensus Vote

LRFP-C
CONSENSUS

Consensus:

Agreement, harmony, concurrence, accord, unity, unanimity, solidarity

General agreement – “a consensus of opinion among judges”

At this time are **you as a member of the CTE LRFP Committee** prepared to make a recommendation to the SBISD Board of Trustees that you are in **support of the Recommended CTE Long Range Facility Plan?**

CTE LRFP Committee Member Name:

Signature of CTE LRFP Committee Member

**I Support the
recommendation**

☐

...I Do NOT Support the Recommendation for the following Reason(s)


Item 3



**LRFP Committee Mtg #4
Meeting Wrap-up:**



July 19, 2021 = SBISD Board Presentation
Closing Remarks

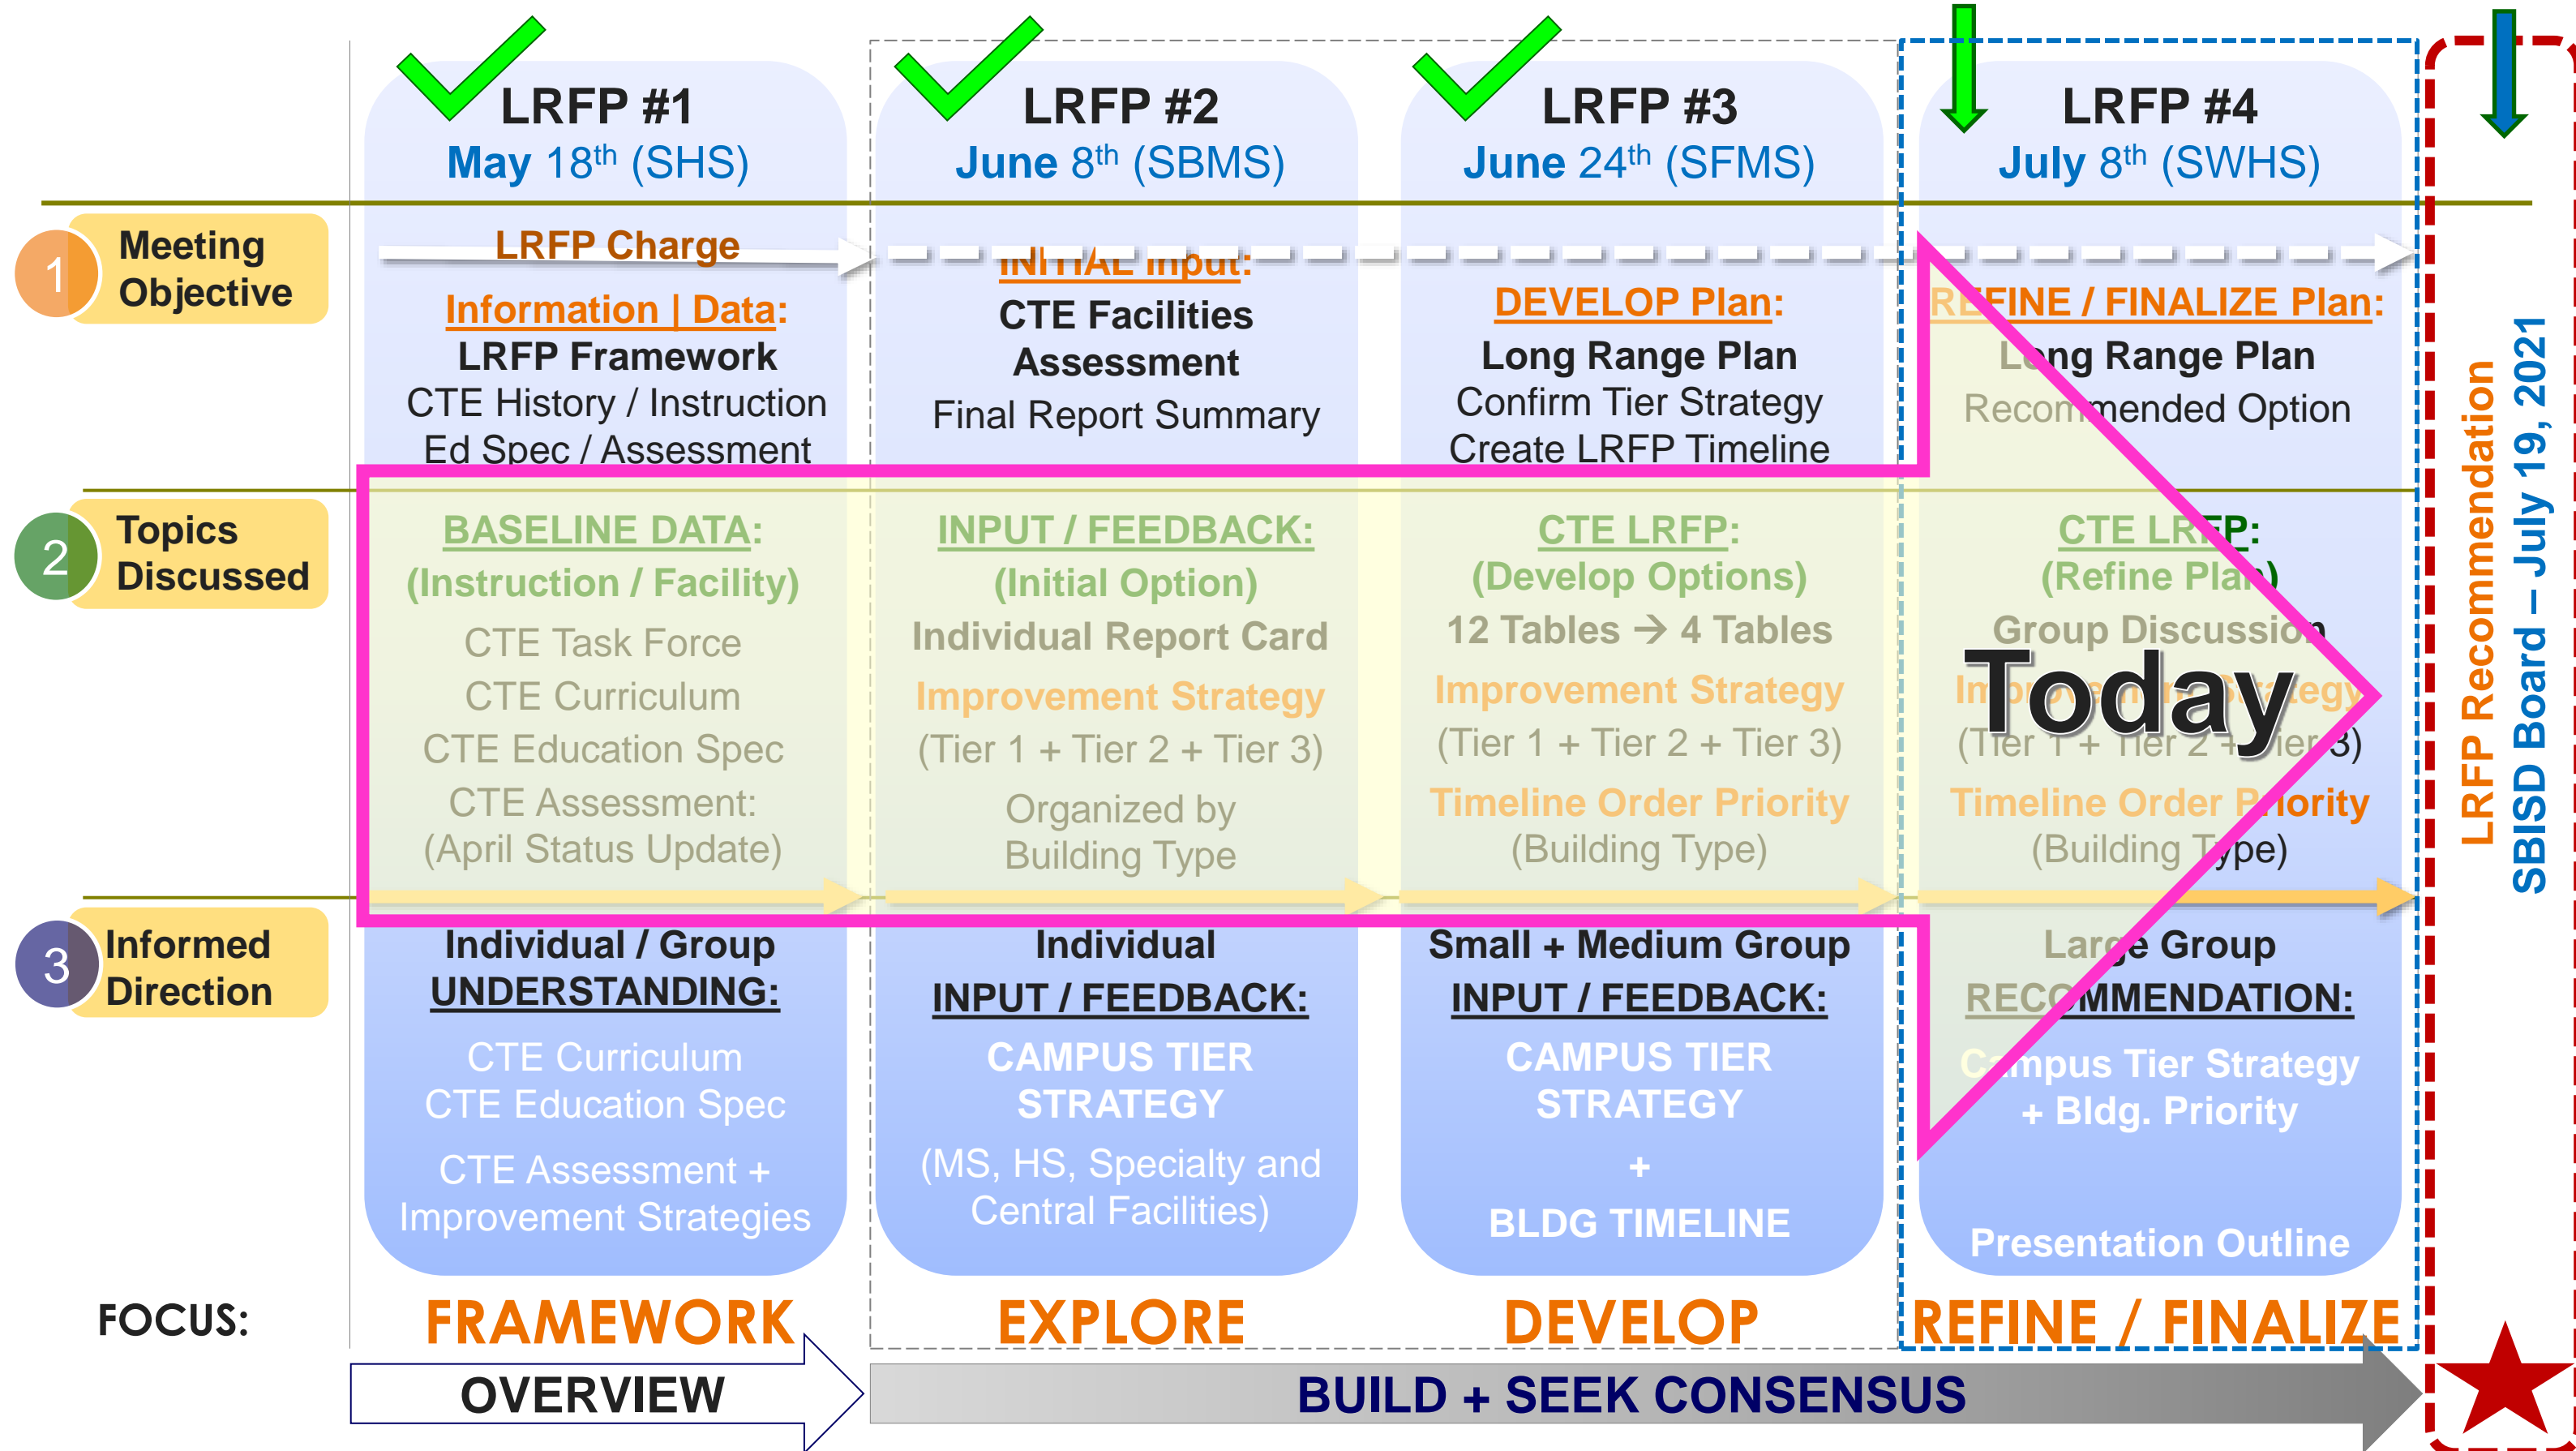

July 19th = Presentation to SBISD Board



Presentation Outline:

Presentation created from slides from LRFP Meetings #1 through #4

- **LRFP Committee Engagement Timeline:** May 8th – July 8th
- **Objective:** Participate in the Development of CTE Long Range Facility Plan
- **Engagement Exercises:** Individual → Group → Committee
- **Committee Recommendation:** Consensus = Tier Strategy + Timeline



Volunteer - LRFP Committee Member:

2 Volunteers to share brief comments on the process

- **Student:** Stakeholder - High School Perspective
- **Co-Chairs:** Stakeholder - Community Perspective

“FEEDBACK” on CTE LRFP Process: Individual Input

CTE Long Range Facility Plan Process Evaluation / Feedback

LRFP Committee INPUT

Evaluation Considerations

EXCEEDED
EXPECTATION

MET
EXPECTATION

DID NOT MEET
EXPECTATION

1. How would you rate the overall process (4 LRFP Meetings)?
2. Do you feel like your input was heard during the process?
3. Was the material presented in a way to help gain understanding?
4. Was the material presented in a clear/sequential manner?
5. Were the LRFP Engagement Activities appropriate/meaningful?

☐☐☐☐☐☐☐☐☐☐☐☐☐☐☐

Comments / Feedback: What did you like the most about the process?

Comments / Feedback: What suggestions do you have for improvement for the process?



THANK YOU !



Recommendation
July 19, 2021
SBISD Board Room
