

**LOMPOC UNIFIED SCHOOL DISTRICT
REQUEST FOR QUALIFICATIONS AND PROPOSALS
LEASE-LEASEBACK CONSTRUCTION SERVICES
RFQ/P # 18-22**

Lompoc Unified School District ("District") is seeking proposals from qualified persons, firms, partnerships, corporations, associations, or professional organizations to provide constructability review, value engineering, master scheduling, cost estimating, budgeting, and construction services for the development and construction for the New Kindergarten Classrooms Construction Project ("Project"), in accordance with the lease-leaseback structure set forth in Education Code section 17406 et seq.

The Request for Qualifications and Proposals ("RFQ/P"), which includes instructions for its completion, is enclosed for your consideration. Respondents to this RFQ/P shall submit a completed Statement of Qualifications ("SOQ") along with the Proposal (collectively "RFQ/P Packet").

The District will only receive RFQ/P Packets submitted electronically. Respondents must deliver one (1) electronic copy in PDF format of the RFQ/P Packet conforming to the requirements of this RFQ/P. RFQ/P packets will be received until **1:00 P.M. ON WEDNESDAY, APRIL 27, 2022**, only at the following email address:

Jordan Miles – jmiles@cfwinc.com
Rick Ostrander – rostrander@cfwinc.com

Any RFQ/P Packet that is submitted after this time shall be nonresponsive and returned to the bidder. **Each respondent is solely responsible for timely submission of its RFQ/P Packet; the District is not responsible for any technological issues in a respondent's ability to timely submit its RFQ/P Packet or portion thereof.**

A non-mandatory information meeting will be conducted on **MONDAY, APRIL 11, 2022**, at **11:00 A.M.** The meeting will be held at all four school sites, starting at Leonora Fillmore Elementary School, located at 1211 East Pine Avenue, Lompoc, CA 93436. Any site visits outside of this must be coordinated through the District's program manager, who may be contacted at the email addresses found above.

Questions regarding this RFQ/P may be directed to Jordan Miles at jmiles@cfwinc.com and Rick Ostrander at rostrander@cfwinc.com, and must be submitted in writing on or by **1:00 P.M. ON WEDNESDAY, APRIL 13, 2022**.

This Project is subject to labor compliance monitoring and enforcement of compliance with prevailing wage requirements by the Department of Industrial Relations pursuant to Labor Code, § 1771.4 and the skilled and trained workforce requirements provided in Public Contract Code, § 2600 et seq. Contractors of all tiers must be currently registered and qualified to perform public work pursuant to Labor Code, § 1725.5. All Respondents must be prequalified by the District in accordance with Public Contract Code, § 20111.6. First tier electrical, mechanical and plumbing subcontractors are required by Public Contract Code, §20111.6 and must be prequalified prior to the time subcontractor bids are submitted. Developer shall comply with all applicable federal, state and local laws regarding COVID-19, including Vaccination and Testing Requirements.

RFQ/P SCHEDULE SUMMARY

DATE	ACTION ITEM
March 28, 2022	Release and advertisement of RFQ/P #18-22.
March 28, 2022	RFQ/P packages available for distribution.
April 11, 2022 at 11:00 A.M.	Non-Mandatory Informational Meeting.
April 13, 2022 at 1:00 P.M.	Last day to receive written questions from Respondents.
April 15, 2022	Last day for District to issue addenda to answer questions/clarifications.
April 18, 2022 at 1:00 P.M.	Deadline for submissions of prequalification to RFQ/P #18-22.
April 21, 2022	Release of shortlist qualified Respondents and interview notifications.
April 27, 2022 at 1:00 P.M.	Deadline for submissions of response to RFQ/P #18-22.
April 29, 2022	Interviews of qualified Respondents.
Week of May 2, 2022	Notice to selected developer to commence contract negotiation.
May 10, 2022	Board Approval of selected firm(s)

The District reserves the right to change the dates on the schedule without prior notice.

[REMAINDER OF PAGE INTENTIONALLY BLANK]

**LOMPOC UNIFIED SCHOOL DISTRICT
REQUEST FOR QUALIFICATIONS AND PROPOSALS
LEASE-LEASEBACK CONSTRUCTION SERVICES**

I. INTRODUCTION

Lompoc Unified School District ("District") is a public school district serving students at nine elementary schools, three middle schools, and three high schools.

This Request for Qualifications and Proposals ("RFQ/P") defines the services sought from Respondents and generally outlines the Project requirements. Respondents to this RFQ/P shall submit a completed Statement of Qualifications ("SOQ") along with the Proposal (collectively "RFQ/P Packet").

I. PROJECT DESCRIPTION AND SCOPE OF SERVICES

A. General

The purpose of this RFQ/P is to select a qualified person, firm, partnership, corporation, association, or professional organization to provide constructability review, value engineering, master scheduling, cost estimating, budgeting, and construction services for the development and construction for the New Kindergarten Classrooms Construction Project ("Project") at Leonara Fillmore Elementary School, La Canada Elementary School, Clarence Ruth Elementary School, and Arthur Hapgood Elementary School, in accordance with the lease-leaseback structure set forth in Education Code section 17406 et seq. Selected developer shall have experience with the construction of public school facilities and complying with the requirements of the Office of Public School Construction ("OPSC"), the Division of the State Architect ("DSA"), and Title 24 of the California Code of Regulations.

To submit a proposal, Respondents must be properly licensed by the California Contractors State License Board and registered with the Department of Industrial Relations ("DIR") as required by law. Only Respondents who have been prequalified by the District in accordance with Public Contract Code section 20111.6 are eligible to respond to this RFQ/P.

The selected developer will be required to comply with the prevailing wage requirements, the skilled and trained workforce requirements, and the District's bonding and insurance requirements. This Project is funded in whole or in part with federal funds, and therefore the selected developer shall comply with the Davis-Bacon Act, applicable reporting requirements such as **APPENDICES C-4** and **C-5**, and any other applicable requirements for federal funding. The selected developer shall be required to work cooperatively with District staff, the Governing Board, all other technical consultants, the architect, the project inspector, and any program and/or construction manager, if any, retained by the District for the Project, citizens' oversight committee, other District committees, and the community at large to deliver a timely and professional completion of the Project. The selected developer and its subcontractors shall comply with all applicable federal, state and local laws regarding COVID-19, including Vaccination and Testing Requirements.

The Project is further defined in the attached **APPENDIX A**, along with the District's construction budget and schedule for the Project, including modular building construction. Respondents' Proposal shall include Respondent's proposed fees and costs to perform the Project if the Respondent is awarded the contract.

The District intends to select one Respondent that best meet the District's needs to perform the Project; however the District reserves the right to select more than one Respondent depending on the construction schedule. The criteria on which the District makes its determination will be based on the District's adopted best value methodology and criteria provided in this RFQ/P.

B. Scope of Work

Although the final scope of work will be negotiated in the executed Agreement (defined below at subparagraph F), the selected developer shall be responsible for performing the following scope of work, at a minimum:

Preconstruction Services:

1. Provide DSA pre-checked designs to architect.
2. Analyze and provide recommendations for incorporating prefabrication (component and modular) construction, within context of project functional requirements, budget, and schedule.
3. Review design and support documentation for content, constructability, completeness, scheduling, clarity, consistency, and coordination.
4. Undertake value-engineering analysis and prepare reports with recommendations to District and Architect of Record to maintain established program budget and specifications.
5. Provide detailed cost estimates.
6. Expedite design reviews, including modifications, if any, based on value analysis.
7. Provide a proposed Guaranteed Maximum Price ("GMP") for the construction of the project with identified subcontractor bids and self-performed work.

Construction Services:

1. Construction of the Project.
2. Coordination of record drawings and specifications.
3. Compilation of operations and maintenance manuals, warranties/guarantees, and certificates.
4. Obtaining occupancy permits and coordinating testing, documentation, and governmental inspections and approvals.
5. Preparation of accounting and closeout reports and occupancy plan reports.
6. Other responsibilities as necessary for the completion of the program.

C. Lease-Leaseback Structure

The Project will be funded from various sources, and any agreement reached will conform to the statutory framework for the lease-leaseback delivery method pursuant to Education Code section 17406, et seq. Financing for a portion of the construction of the Project will be included in the Agreement attached to this RFQ/P as **APPENDIX B**. During construction, the District shall pay tenant improvement payments. Once the Project is complete, the developer shall lease the completed facilities back to the District for a pre-determined monthly lease payment amount. However, the District intends that the lease will include an early termination payment option for the District.

D. District Project Management Description

District's Governing Board will be responsible for making final decisions, but the Superintendent will be responsible for day-to-day decisions and designates Caldwell Flores Winter, Inc. (CFW) as the program manager who will be the primary point of contact between the selected developer and the District.

E. Prequalification of Designated Subcontractors

If used, contractors holding C-4, C-7, C-10, C-16, C-20, C-34, C-36, C-38, C-42, C-43, and/or C-46 licenses (collectively, "MEP subcontractors") shall be prequalified by the District to perform construction work as a first tier subcontractor on the Project pursuant to Public Contract Code section 20111.6.

F. Registration of Respondent and All Tiers of Subcontractors

The selected developer(s) shall not allow any employee or subcontractor to commence work on any contract or any subcontract until the proof of registration with the Department of Industrial Relations required of the developer or subcontractor has been provided to and accepted by the District.

G. Form of Agreement

Selected developer must be able to execute the District's standard form of Site Lease and Facilities Lease ("Agreement") is attached to this RFQ/P as **APPENDIX B**. After the plans and specifications have been approved by DSA, the Facilities Lease will be amended to include the agreed upon Guaranteed Maximum Price.

H. Indemnity

Respondents to this RFQ/P must acknowledge that they have reviewed the District's indemnity provision set forth in the Facilities Lease (**APPENDIX B**) and must agree to the indemnity provision and confirm in writing that, if given the opportunity to contract with the District, the Respondent has no substantive objections to the use of the District's standard indemnity provision.

[REMAINDER OF PAGE IS INTENTIONALLY LEFT BLANK]

I. Insurance

The District requires at least the following insurance coverage from the selected developer:

Commercial General Liability	Product Liability and Completed Operations, Fire Damage Liability – Split Limit	Developer: \$5,000,000 per occurrence; \$10,000,000 annual aggregate Subcontractors (less than 10% of GMP): \$2,000,000 per occurrence; \$4,000,000 annual aggregate
Excess Liability		Developer: \$10,000,000 per occurrence; \$10,000,000 annual aggregate Subcontractors (less than 10% of GMP): \$4,000,000 per occurrence; \$4,000,000 annual aggregate
Automobile Liability – Any Auto	Combined Single Limit	\$3,000,000 (limits may be met with Excess Liability Policy required herein)
Workers’ Compensation		Statutory limits pursuant to State law
Employer’s Liability		\$1,000,000
Builder’s Risk		Replacement Cost
Pollution Liability		\$2,000,000 per occurrence; \$2,000,000 annual aggregate

The limits of insurance for those subcontractors whose scope of work does not exceed One million dollars (\$1,000,000) shall not be less than the following amounts:

Commercial General Liability	Product Liability and Completed Operations	\$2,000,000 per occurrence; \$4,000,000 annual aggregate
Excess Liability		\$5,000,000 per occurrence; \$5,000,000 annual aggregate
Automobile Liability - Any Auto	Combined Single Limit	\$2,000,000
Workers Compensation		Statutory limits pursuant to State law
Employers’ Liability		\$1,000,000

Selected developer shall provide to the District certificate(s) of insurance and endorsements satisfactory to the District. Insurance policy(ies) shall not be amended or modified and coverage amounts shall not be reduced without thirty (30) days' written notice to District prior to modification and/or cancellation. For Commercial General Liability and Automobile Liability, District shall be named as an additional insured on all policies. Selected developer's policy(ies) shall be primary; any insurance carried by the District shall only be secondary and supplemental. Selected developer shall not allow any employee or subcontractor to commence work on any contract or any subcontract until the proof of insurance required of the developer or subcontractor has been provided to and accepted by the District.

II. FULL OPPORTUNITY

The District hereby affirmatively ensures that all Respondents, including without limitation Disadvantaged Business Enterprises ("DBE"), Small Local Business Enterprise ("SLBE"), Small Emerging Local Business Enterprise ("SELBE") and Disabled Veterans Business Enterprise ("DVBE") firms, shall be afforded full opportunity to submit qualifications in response to this RFQ/P and will not be discriminated against on the basis of race, religious creed, color, national origin, ancestry, physical disability, mental disability, medical condition, genetic information, marital status, sex, gender, gender identity, gender expression, age, sexual orientation, or veteran or military status in any consideration leading to the award of contract.

III. LIMITATIONS

This RFQ/P is neither a formal request for bids, nor an offer by the District to contract with any party responding to this RFQ/P. The District reserves the right to add additional prequalified Respondents for consideration after distribution of this RFQ/P if it is found to be in the best interest of the District. All decisions concerning selection of the developer will be made in the best interests of the District. The awarding of the contract pursuant to this RFQ/P, if at all, is at the sole discretion of the District.

The District makes no representation that participation in the RFQ/P process will lead to an award of contract or any consideration whatsoever. The District shall in no event be responsible for the cost of preparing any RFQ/P Packet in response to this RFQ/P.

RFQ/P Packets and any other supporting materials submitted to the District in response to this RFQ/P will not be returned and will become the property of the District unless portions of the materials are designated as proprietary at the time of submittal, and are specifically requested to be returned. Vague designations and/or blanket statements regarding entire pages or documents are insufficient and will not bind the District to protect the designated matter from disclosure. Pursuant to *Michaelis, Montanari, & Johnson v. Superior Court* (2006) 38 Cal.4th 1065, RFQ/P Packets shall be held confidential by the District and shall not be subject to disclosure under the California Public Records Act until after either: (1) the District and the successful Respondent have completed negotiations and entered into an Agreement, or (2) the District has rejected all Proposals. Furthermore, the District will have no liability to the Respondent or other party as a result of any public disclosure of any RFQ/P Packet.

IV. RESTRICTIONS ON LOBBYING AND CONTACTS

From the period beginning on the date of the issuance of this RFQ/P and ending on the date of the award of the contract, no person, or entity submitting in response to this RFQ/P, nor any officer, employee, representative, agent, or consultant representing such a person or entity shall contact through any means or engage in any discussion regarding this RFQ/P, the evaluation or selection process/or the award of the contract with any member of the District,

Governing Board, selection members, or any member of the Citizens' Oversight Committee. Any such contact shall be grounds for the disqualification of the Respondent submitting a RFQ/P Packet.

V. NON-MANDATORY INFORMATIONAL MEETING AND SITE WALK

Respondents are requested attend a non- mandatory informational meeting and site walk, to be conducted on **MONDAY, APRIL 11, 2022, at 11:00 A.M.** The site walk will include all four school sites, starting at Leonora Fillmore Elementary School, located at 1211 East Pine Avenue, Lompoc, CA 93436. At this non-mandatory meeting, District representatives will distribute information and materials to further describe the Project, the scope of work, and walk the proposed Project site. Respondents shall consider and address the materials and information distributed at the meeting in their RFQ/P Packets. Any site visits outside of this must be coordinated through CFW Inc., who may be contacted at the email addresses found above.

VI. SUBMITTAL FORMAT

A. Format

Material must be in 8½ x 11 inch format with font no less than 11 point font size. The RFQ/P Packets shall include divider tabs labeled with boldface headers below (e.g. the first tab would be entitled "Executive Summary," the second tab would be entitled "Table of Contents," etc.) One (1) electronic copy of the RFQ/P Packet shall be submitted. Each submittal shall not contain more than thirty (30) single-sided pages, and excluding front and back covers, tabs, certificates of insurance, detailed schedule charts, and comments to the Form of Agreement (Tab 11). Any double-sided page is counted as two single-sided pages. Submittals containing more than the authorized number of pages will not be considered.

B. General Overview

Each RFQ/P Packet shall include a description of the type, technical experience, backgrounds, qualifications and expertise of the Respondent. The description shall show that the firm possesses the demonstrated skills and professional experience to perform the general functions of the Project and fulfill the goals and vision of the District as its developer for the Project. Submittals shall describe in detail the Respondent's methods and plan for carrying out the Project. Included in this information must be a description of construction scheduling, staging, and logistics based on timelines and information provided by the District in this RFQ/P and the non-mandatory informational meeting. Describe the Respondent's approach to the Project, including any creative methodology and/or technology that the Respondent uses or unique resources that the Respondent can offer to the District and Project. Include a description of the Respondent's identified modular building system and vendor. Provide background information on the proposed modular building system and vendor including the appropriateness of the system to the proposed project.

C. Contents

Respondents shall comply with the following requirements for its RFQ/P Packet:

1. TAB 1 – Executive Summary (max. 1 page)

This should be an overview of the entire RFQ/P Packet with a description of the general approach and/or methodology the Respondent will use to meet the goals and fulfill the general functions as set forth in this RFQ/P.

2. TAB 2 – Table of Contents

This should be a complete and clear listing of the headings and pages to allow easy reference to key information.

3. TAB 3 – Cover Letter Identifying Respondent (max. 1 page)

This should be a letter of introduction signed by an authorized officer of the Respondent. If the Respondent is a joint venture, duplicate the signature block and have a principal or officer sign on behalf of each party to the joint venture. The letter shall also include:

- a. Respondent's name.
- b. Address, include any branch office address and point of contact.
- c. Telephone number.
- d. Facsimile number.
- e. E-Mail address.
- f. Identify team.
- g. Clearly identify the individual(s) who are authorized to speak for the Respondent during the evaluation process.
- h. And, the following statement:

“[RESPONDENT’S NAME] received a copy of the District’s Site Lease and Facilities Lease (“Agreement”) attached as Appendix B to the RFQ/P. [RESPONDENT’S NAME] has reviewed the indemnity provisions and insurance requirements contained in the Agreement. If given the opportunity to contract with the District, [RESPONDENT’S NAME] has no objections to the use of the Agreement.”

- i. Respondent shall certify that no official or employee of the District, nor any business entity in which an official of the District has an interest, has been employed or retained to solicit or assist in the procuring of the resulting contract(s), nor that any such person will be employed in the performance of any/all contract(s) without immediate divulgence of this fact to the District.

4. TAB 4 - Respondent Information

- a.** A brief history of the Respondent. Please include any former names of the Respondent and the number of years the Respondent has participated in construction as a general contractor under each name. List any reasons for change or name or corporate structure.
- b.** Organizational chart for Respondent. This shall include the names of all key personnel, joint venture partners, and sub-consultants with their titles and specific task assignments for the Project. Resumes of personnel to be involved with the Project should be included, including their school construction experience. The District's evaluation will consider the entire team. Therefore, no changes in the Respondent's composition will be allowed without prior written approval by the District.

Identify up to three (3) persons who will be primarily responsible for working with the District and their respective roles and responsibilities, including Superintendent and Foreman. If Respondent is selected for an interview, the identified individuals must attend the interview and any required in-person presentations.

- c.** Description of Respondent's technical competence, including a description of in-house resources (e.g. computer capabilities, software applications, modeling programs, etc.), and Respondent's ability to draw upon multi-disciplinary staff to address the services required under the RFQ/P.
- d.** Provide the volume of construction in dollars for each of the past three (3) years.
- e.** Provide a statement regarding the Respondent's availability and resources.
- f.** Provide a statement on financial resources, bonding capacity and insurance coverage.
- g.** Provide a claims statement for all resolved or ongoing claims for Respondent *and* its personnel, as well as Associated Firms. Statement must include any and all suits or claims in which the Respondent or its personnel instigated a claim and/or litigation regarding construction projects within the past five (5) years, and indicating any and all claims in which claims and/or litigation have been pursued against the Respondent or its personnel. For each listed claim and/or litigation: state the issues in the claim and/or litigation, the status of the claim/litigation, the names of the parties involved, and the outcome, if any.

"Associated Firms" are businesses, corporations, companies, partnerships, or other entities associated with Respondent

and/or its personnel (e.g., firm name changes, association as prior owner, general partner, limited partner, or other officer).

- h.** Contractor license number and whether license has been revoked or suspended in the last five (5) years. Respondent must hold a General Building Contractor License (B License), which is current, valid and in good standing with the Contractor's State License Board. Provide the following for each license:
 - i. Exact name of license holder on file.
 - ii. License Classification.
 - iii. License Number.
 - iv. Date Issued.
 - v. Expiration Date.
 - vi. Whether license has been suspended or revoked in the past five (5) years. If so, explain.
- i.** Provide signatory status.
- j.** Location of nearest local office and main office, if different.
- k.** Certificate(s) of Insurance identifying the firm's current insurance coverages.
- l.** Provide Non-Collusion Declaration. (**APPENDIX C-1.**)
- m.** Provide Iran Contracting Act Certification. (**APPENDIX C-2.**)

5. TAB 5 – Methods and Strategic Plan

Detailed description of Respondent's methods and plan for carrying out the Project, including:

- a.** The technical and managerial approach to the Respondent's partnership with the District. Take into account the District's goals for the Project and the general functions required. Respondent may identify additional necessary tasks and discuss these in its proposed method to accomplish the work.
- b.** How Respondent plans to incorporate skilled and trained workforce into the Project.
- c.** How Respondent plans to incorporate local subcontracting teams into the Project.
- d.** How Respondent plans to incorporate construction means and methods into the Project.

- e. Proposed cost for completing preconstruction services for the Project for which the Proposal is being submitted and the cost of modular building(s), including cost of modular manufacturer providing architectural and engineering services as a subconsultant to the Architect.
- f. Detailed discussion of costs related to fees, general conditions, insurance, supervision, and management of the construction portion of the scope of work.

Emphasis will be given to the methods and strategic plan as they relate to preconstruction services and how the preconstruction services will transition into the construction services.

6. TAB 6 – Prior Relevant Experience

Description of the Respondent’s experience with respect to the areas of public schools or similar construction over the past five (5) years. Specifically, please provide a list of completed or ongoing projects the Respondent has been involved with for the past five (5) years where the total project contracts exceeded five million dollars (\$5,000,000) per project. Within that list:

- a. Identify the method (e.g. lease-leaseback, bid-build, etc.) by which each project was constructed. For lease-leaseback projects, include the total cost of each project and a breakdown of the total cost by preconstruction services and construction services.
- b. Include a discussion of Respondent’s experience with working with the DSA on public school projects.
- c. Identify and include discussion of Respondent’s experience with projects performed in an occupied building and/or immediately adjacent to an occupied building and/or campus.
- d. Identify and include a discussion on Respondent’s experience with modular construction. Identify and include discussion of Respondent’s intended prefabrication/modular vendor/brand, model(s), and piggyback contract price list(s), if available.
- e. Identify and include a discussion on the modular subcontractor that Respondent plans to use, and the modular subcontractor’s experience with prefabrication/modular projects installed (in whole or in part) at California K-12 public school districts. Modular subcontractor license number and whether license has been revoked or suspended in the last five (5) years. Modular subcontractor must hold a General Building Contractor License (B License) or General Manufactured Housing Contractor License (C-47 License), which is current, valid and in good standing with the Contractor’s State License Board.
 - i. Exact name of license holder on file.
 - ii. License Classification.

- iii. License Number.
 - iv. Date Issued.
 - v. Expiration Date.
 - vi. Whether license has been suspended or revoked in past five (5) years. If so, explain.
- f.** Identify whether the project is completed or ongoing.
 - g.** Identify if any of the projects had phased completion.

For the projects listed, above, be sure to also include the following information:

- a.** Project's name and description;
- b.** Firm's role;
- c.** Award and completion dates;
- d.** Project's initial contract price and final contract price;
- e.** Amount of fees received;
- f.** Staffing, including Respondent's team members, subcontractors and consultants;
- g.** Relationship with owner/client;
- h.** References: Provide a contact name, telephone number and email address for the owners and indicate which key personnel of Respondent worked on each project; and
- i.** Discussion of claims, demands, and/or litigation arising from the project and involving the Respondent, and resolution of the same.
- j.** Include examples of other similar project assignments on the part of the Respondent.
- k.** Prefabrication and/or modular components as a percent of the project's hard costs, and as a percent of total project square footage; specific prefabrication/modular vendor and model(s).

List projects Respondent has successfully completed that had some or all of the following obstacles, including the creative solutions from the Respondent on how these obstacles were overcome:

- a.** A very aggressive schedule.
- b.** Significant budgetary restrictions.

- c. Be prepared to expand upon what you did to accommodate:
 - i. The complexity of the project;
 - ii. The needs of the clients;
 - iii. Minimizing inconvenience; and
 - iv. Maximizing safety.

7. TAB 7 – Contracting History

If any of the following have occurred, please describe in detail the circumstances of each occurrence:

- a. Failure to enter into a contract or professional services agreement once selected.
- b. Withdrawal of a proposal or bid as a result of an error.
- c. Termination or failure to complete a contract.
- d. Debarment by any municipal, county, state, federal, or local agency.
- e. Involvement in litigation, arbitration, or mediation, whether concluded or ongoing.
- f. Conviction of the Respondent or its principals for violating any state or federal antitrust laws by bid or proposal rigging, collusion, or restrictive competition between bidders or proposers, or conviction of any other federal or state law related to bidding or performance of services.
- g. Knowing concealment of any deficiency in the performance of a prior contract.
- h. Falsification of information or submission of deceptive or fraudulent statement in connection with a contract.
- i. Willful disregard for applicable rules, laws, or regulations.
- j. Failure to disclose information regarding any of the above may be deemed to indicate an unsatisfactory record of performance. Information regarding any of the above may be considered in determining the suitability of Respondent to perform the needed services. Accordingly, Respondent may describe mitigating factors as part of description of any of the above.

8. TAB 8 – Pricing and Contingency

The pricing will be evaluated based on the: (1) preconstruction services cost or method of calculation; (2) Respondent's fee, which includes profit and overhead; (3) general conditions

cost; (4) bonds and insurance percentage; (5) construction contingency to be applied to errors and omissions; (6) allowances, if any; and (7) proposed modular vendor cost based on make and model with current DSA PC number which would be applicable for the specific building configuration anticipated as part of the Project, indicated as a cost per square foot of modular building area as well as the cost of modular design services to architect and in-plant observation.

After the Agreement is awarded and DSA approves the plans and specifications, the selected developer will be required to provide a Guaranteed Maximum Price ("GMP") for the Project. As part of the District review of the GMP, the District will expect to have access to all subcontractor bids, contingency breakdown and tracking documents, general conditions breakdown and tracking documents, and Respondent's fees. The GMP shall include all of Respondent's cost for labor, materials, equipment, overhead and profit, general conditions, contractor contingency, and allowances, if any, but shall specifically exclude the amount of the District contingency. In the event the selected developer realizes a savings on any aspect of the Project, such savings shall be added to the District contingency and expended consistent with the District contingency. In addition, any portion of the contractor contingency and/or allowance remaining after completion of the Project shall be added to the District contingency. The Facilities Lease will be amended to include the agreed upon GMP, if the District proceeds with the construction phase of the Project.

9. TAB 9 – Insurance

Each Respondent must demonstrate that it can maintain adequate insurance as required herein. Therefore, each RFQ/P Packet must include a letter from the Respondent's insurance company indicating its ability to provide insurance coverage on behalf of Respondent in accordance with the insurance requirements in **APPENDIX B**.

10. TAB 10 – Assurances

The Respondent must acknowledge each of the following items and confirm that it will be willing and able to perform these items:

Preconstruction Services: Respondent shall provide services that relate to the organization and development of the Project prior to the start of construction including the following:

- **Site Evaluation:** Consult with District staff in relation to the existing site. Selected developer should make site visits, as needed to review the current site conditions. During this evaluation, selected developer may make recommendations relating to soils investigations and utility locations and capacities, in order to minimize unforeseen conditions.
- **Modular Design and/or Technical Assistance:** The District anticipates its design professional in general responsible charge of the Project(s) will delegate authority regarding PC modular design and in-plant observation, pursuant to DSA Bulletin 16-01 and DSA 1-MR.
- **Plan Review:** Provide plan review and constructability services. Refer to the Facilities Lease for the required scope. Place an emphasis on ensuring that the Project can be completed within the established schedule and within the available budget. During the review, selected developer shall review the documents for clarity, consistency, constructability and coordination. The

results of the review shall be provided in writing and as notations on the documents to the District and Bond Management team. The selected developer shall also make recommendations to the District and Bond Management team with respect to constructability, construction cost, sequence of construction, and construction duration.

- **Pre-construction Meetings:** Attend meetings at the Project site with the architect of record and the Bond Management team every two (2) weeks, until the Notice to Proceed with Construction is issued on or about August 27, 2020 (meeting duration is approximately 2 hours).
- **Value Engineering:** Provide a detailed analysis of all major Project systems with an emphasis on possible value engineering possibilities.
- **Detailed Construction Critical Path Schedule:** Produce detailed construction critical path schedules to be incorporated into the Project documents including identification of the Project critical path and agency approvals.
- **Preliminary and Detailed Estimates:** Provide preliminary construction estimates using like-kind construction costs. Upon receipt of the Project plans and specifications, provide detailed construction estimates showing the values of all major components of the Project.
- **Construction Planning:** Plan the phases and staging of construction, staging areas, temporary fencing, office trailer placement, access, etc. as required.
- **Other services:** Any other services that are reasonable and necessary to control the budget and schedule.

Construction Services:

- **Project Accounting and Management Systems:** In coordination with District staff, develop the Project accounting and budget management systems. A process of up-to-date costs management will be necessary. During construction, monthly reporting will be required.
- **General Conditions:** List what is included in the Respondent's general conditions (including full-time and part-time personnel) and a monthly value of the general conditions. Indicate what would be included as a cost of work versus a line item in the general conditions. See **APPENDIX C-3** for an example.
- **Management of Project:** Administer and coordinate on a daily basis the work of all trade contractors the successful Respondent hires to work on the Project. Enforce strict performance, scheduling, and notice requirements. Document the progress and costs of the Project. Report proactively on potential schedule impacts. Recommend potential solutions to schedule problems.
- **Trade Contractors:** Pursuant to Public Contract Code section 20111.6, each prospective MEP Contractor holding C-4, C-7, C-10, C-16, C-20, C-34, C-36, C-38, C-42, C-43, and/or C-46 licenses shall be prequalified by the District to perform construction work as a first tier subcontractor on the Project.

11. TAB 11 – Comments to Form of Agreement

Respondents must thoroughly review the Agreement attached to this RFQ/P as **Appendix B** and confirm in writing that, if given the opportunity to contract with the District, Respondent has no substantive objections to the use of the District’s standard agreement. Respondent must also identify any term or condition of the Agreement that Respondent requests modifying, deleting, or adding. Respondents must set forth a clear explanation of what modification would be sought and specific alternate language. ***If selected, Respondent will be precluded from negotiating changes that have not been identified in its RFQ/P Packet.*** The District will review, but is not obligated to accept, any proposed changes.

VII. SELECTION CRITERIA

A. Best Value Evaluation

The RFQ/P Packets will be evaluated based on the District’s adopted criteria and rating system to determine the qualified Respondent(s) providing the best value to the District for all candidates that meet the pass / fail criteria listed below (i.e., receive a PASS).

CRITERIA ITEM	DESCRIPTION	MAXIMUM POINTS
Conflict of Interest	Is there a conflict of interest?	PASS / FAIL
Safety	Safety record	PASS / FAIL
Form of Agreement	Proposed changes to District Form of Agreement	PASS / FAIL
Interview (If used, score; if not used, all respondents receive 0 points.)	Proposed team, experience, performance, approach to work	51 points
Technical Expertise	Relevant experience with like-Projects, prior lease-leaseback experience, value-engineering experience, constructability experience, experience with modular building systems, references	15 points
Price Points	Fees, general conditions, contingency, interest proposed on lease payments	15 points
Staffing	Management and Staffing Approach, including skilled and trained workforce	9 points
Schedule/Liquidated Damages	History of meeting Project Schedule and Delivery Date	5 points
Claims/Litigation	Acceptable history of claims and litigation	5 points
TOTAL: MAXIMUM 100 POINTS		

Based on these criteria, District staff assign points to each proposer and then calculate the total points awarded to the proposer. The more points, the higher the proposer is ranked. The highest ranked proposer reflects the best combination of price and qualifications for the Project.

B. District Investigations

The District may perform investigations of proposing parties that extend beyond contacting the references identified in the proposals.

C. Selection Process

RFQ/P Packets shall be evaluated and the Project awarded in the following manner:

1. All proposals received shall be reviewed to determine those that meet the format requirements and the standards specified in RFQ/P.
2. District shall evaluate the qualifications of the Respondents based solely upon the adopted criteria and evaluation methodology, and shall assign a best value score to each proposal. Once the evaluation is complete, all responsive proposals shall be ranked from the highest best value to the lowest best value to the District.
3. The District's Governing Board shall award the Project to the responsive proposer whose proposal is determined, in writing by the Governing Board, to be the best value to the District.
4. If the selected developer refuses or fails to execute the tendered proposed contract, the Governing Board may award the contract to the proposer with the second highest best value score if it deems it to be for the best interest of the District. If the second selected developer refuses or fails to execute the tendered instrument, the Governing Board may award the instrument to the proposer with the third highest best value score if it deems it to be for the best interest of the District.
5. Notwithstanding any other law, upon issuance of a contract award, the District shall publicly announce its award, identifying the entity to which the award is made, along with a statement regarding the basis of the award. The statement regarding the District's contract award and the contract file shall provide sufficient information to satisfy an external audit.

D. Interviews

The District will invite some of the finalists to meet with a District selection committee. Key proposed Project staff, including the modular subcontractor, will be expected to attend the interview. The interview will be an opportunity for the District selection committee to review the proposal, the firm's history, and other matters the committee deems relevant to firm evaluation with the firm. The interview will start with the firm presenting its proposal and its Project team. The finalists may be required to submit in advance of the interview a more detailed fee proposal. If requested, this fee proposal shall include all charges and costs proposed to be charged to the District, including rates for extra work.

Any comments or objections to the form of Agreement attached hereto as **APPENDIX B** to this RFQ/P shall be provided in writing in the RFQ/P Packet and may be the subject of inquiry at the interview. Comments on the form of Agreement will be excluded from the page count. District reserves the right to accept, reject or negotiate requested revisions. Any comments or objections to the form of Agreement not provided in writing before the interview will not be entertained by the District.

E. Final Determination and Award

It is expected that the selection committee will make recommendations to District staff regarding the candidates and awarding the contract. The awarding of contract(s) is at the sole discretion of the District.

The District reserves the right to contract with any entity responding to this RFQ/P for all or any portion of the work described herein and/or in an agreement offered to the entity, to reject any proposal as non-responsive, and/or not to contract with any firm for the services described herein. The District makes no representation that participation in the RFQ/P process will lead to an award of contract or any consideration whatsoever. The District reserves the right to seek proposals from or to contract with any firm not participating in this process. The District shall in no event be responsible for the cost of preparing any RFQ/P Packet in response to this RFQ/P.

The RFQ/P packet, and any other supporting materials submitted to the District in response to this RFQ/P will not be returned and will become the property of the District unless portions of the materials are designated as proprietary at the time of submittal, and are specifically requested to be returned. This RFQ/P does not commit the District to negotiate an agreement with any proposing firm or individual.

VIII. SUBMISSION GUIDELINES

The District will only receive RFQ/P Packets submitted electronically. RFQ/P Packets will be received until 1:00 P.M., ON WEDNESDAY, APRIL 27, 2022, only at the following email addresses:

Jordan Miles – jmiles@cfwinc.com
Rick Ostrander – rostrander@cfwinc.com

Any RFQ/P Packet that is submitted after this time shall be nonresponsive and returned to the bidder. **Each respondent is solely responsible for timely submission of its RFQ/P Packet; the District is not responsible for any technological issues in a respondent's ability to timely submit its RFQ/P Packet or portion thereof.**

Each submittal must conform and be responsive to the requirements set forth in this RFQ/P. The District reserves the right to waive any informalities or irregularities in the RFQ/P Packets. The District also reserves the right to reject any and all RFQ/P Packets and to negotiate contract terms with one or more respondents. The District retains the sole discretion to determine issues of compliance and to determine whether a respondent is responsive, responsible, and qualified.

The District hereby notifies all respondents that it will affirmatively insure that, in any contract entered into pursuant to this advertisement, no respondent will be discriminated against on the grounds of race, religious creed, color, national origin, ancestry, physical disability, mental disability, medical condition, genetic information, marital status, sex, gender, gender identity, gender expression, age, sexual orientation, or veteran or military status in consideration for the award.

WE THANK YOU FOR YOUR INTEREST IN THE DISTRICT'S PROJECT.

APPENDIX A Project Description

SCOPE OF WORK:

The District desires to select a firm capable of providing LLB pre-construction and construction services for the project. The selected firm for the project should expect to perform pre-construction services as established by the District pursuant to a Pre-Construction Services Agreement. If the District proceeds with the construction of the project, the selected firm may be retained as an LLB contractor pursuant to a Construction Services Agreement, Lease and Sub-lease and may contract with separate specialty trade contractors to perform the required scope of work.

Pre-Construction Services are anticipated to include the following:

1. Review design and support documentation for content, constructability, completeness, scheduling, clarity, consistency and coordination
2. Undertake value-engineering analysis and prepare reports with recommendations to District and Architect of Record to maintain established program budget and specifications
3. Provide detailed cost estimates at schematic, design development, and construction document design phases
4. Expedite design reviews, including modifications, if any, based on value analysis
5. Provide a proposed guaranteed maximum price for the construction of the project
6. Provide DSA PC drawings for incorporation into sitewide plans and specifications

Construction Services are anticipated to include, but not be limited to the following:


1. Provision of a proposed Guaranteed Maximum Price (GMP) for the construction of the project with identified subcontractor bids, including the modular construction of buildings, and self-performed work
2. Construction of the Project
3. Coordination of record drawings and specifications
4. Compilation of operations and maintenance manuals, warranties/guarantees, and certificates
5. Obtaining occupancy permits and coordinating testing, documentation, and governmental inspections and approvals
6. Preparation of accounting and closeout reports and occupancy plan reports
7. Other responsibilities as necessary for the completion of the program

PROJECT DESCRIPTION:

The Project is located at four (4) elementary school sites across the District: Leonora Fillmore Elementary School, La Canada Elementary School, Clarence Ruth Elementary School, and Arthur Hapgood Elementary School. Although located at different sites, these projects are to be funded from the same local sources on hand and considered to be one project. This project is to be designed and constructed concurrently at all sites. Firms are allowed to submit responses with separate fee proposals and cost estimates for all four school sites, and it is up to the discretion of the District if one firm will be selected for all four school sites or if the project will be assigned to different firms.

The project includes the construction of modular classrooms that meet Title 5 requirements for Transitional Kindergarten (TK) and Kindergarten (K) instruction. Figure 1 below depicts a popular TK/K design formulated by CFW that was previously funded by the state. The design meets Title 5 TK/K standards of not less 1,350 square feet, including restrooms, storage, teacher preparation spaces, and wet and dry areas. The restrooms are self-contained within the classroom and designed to allow supervision of the play yards and the classroom. They are equipped with 21st Century classroom improvements, mobile, flexible furnishings for maximum flexibility in the classroom, multiple display monitors mounted to the walls with floor to ceiling white boards, and wireless connectivity throughout the room.

Figure 1 – Sample Kindergarten Floor Plan

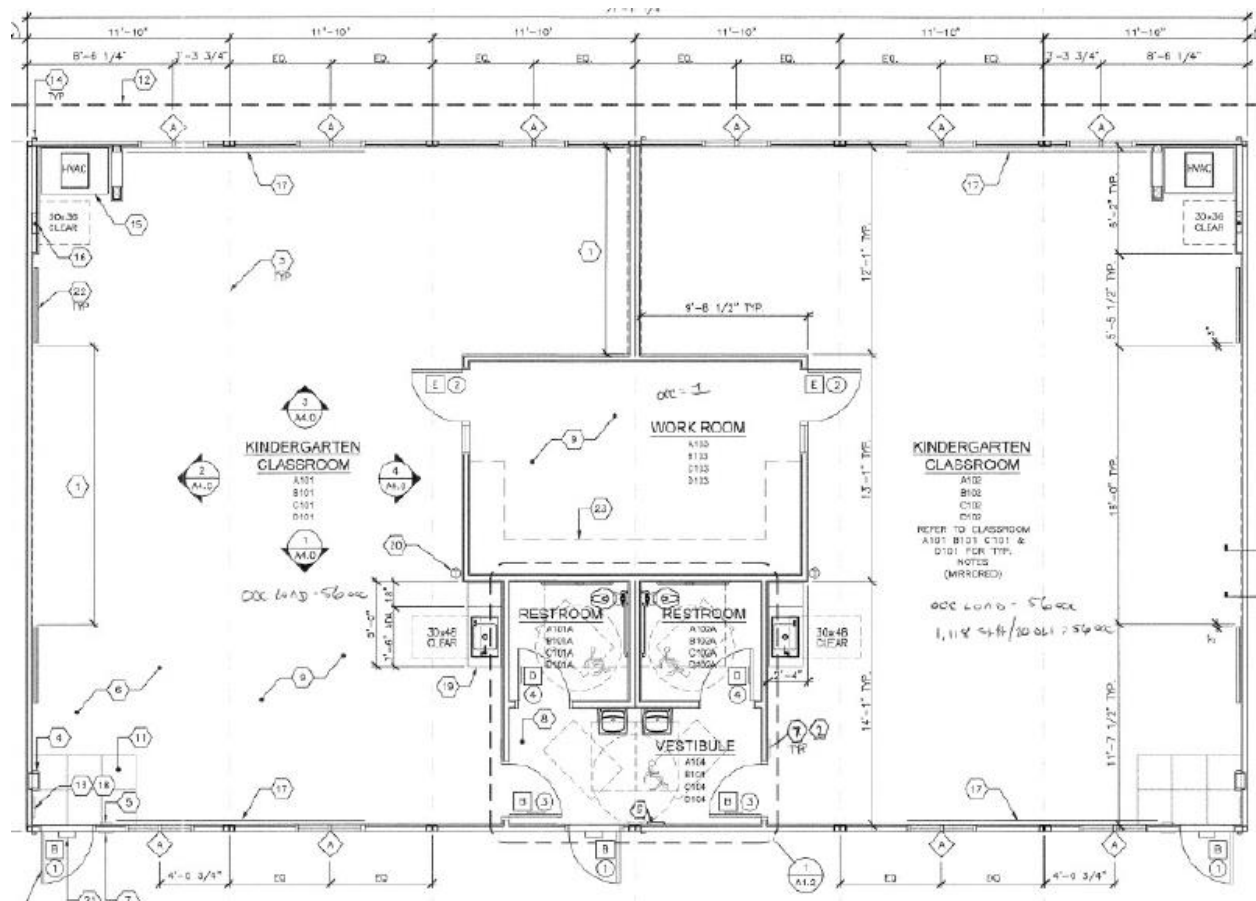

A. LEONARA FILLMORE ELEMENTARY SCHOOL

Leonora Fillmore Elementary School (Fillmore) is located at 1211 East Pine Avenue. The school occupies 12 acres and is bounded by residential development on all sides. The Grace Baptist Church of Lompoc borders a portion of the school to the west, and Pioneer Park borders a portion of it to the south. The school was originally built in 1959 and modernized in 2004. Fillmore has a total of 25 permanent classrooms and 12 portable classrooms.

It is contemplated that the proposed classrooms be located at the southeast corner of the school buildings near East Pine Street, parallel to the existing kindergarten classrooms. The existing kindergarten playground to the east would be accessible for kindergarten students in the new classrooms. Potential site improvements could be made for pick-up and drop-off along Sixth Street to accommodate lesser traffic and a more welcoming access point. Overall, the goal would be to add to the creation of a TK/K village within the school that promotes propinquity, teacher interaction, parent access and shared support spaces for the benefit of TK/K students.

Figure 2 – Fillmore Elementary School Proposed TK/K Facilities




B. LA CAÑADA ELEMENTARY SCHOOL

La Cañada Elementary School (La Cañada) is located at 621 West North Avenue. The school occupies 15 acres and is bounded by residential development on all sides. The school was originally built in 1962 and modernized in 2005. La Cañada has a total of 24 permanent classrooms and 15 portable classrooms.

It is anticipated that the proposed classrooms be located as a western expansion of the existing campus into an "L" shaped courtyard with the existing kindergarten classrooms. With this configuration, a quad is formed that would be ideal to accommodate a common playground for all kindergarten children. Drop off and pick up would be located in the parking area to the south of the existing kindergarten classrooms. As with Fillmore, the goal would be to expand the creation of a TK/K village within the school that promotes propinquity, teacher interaction, parent access and shared support spaces for the benefit of TK/K students.

Figure 3 – La Cañada Elementary School Proposed TK/K Facilities

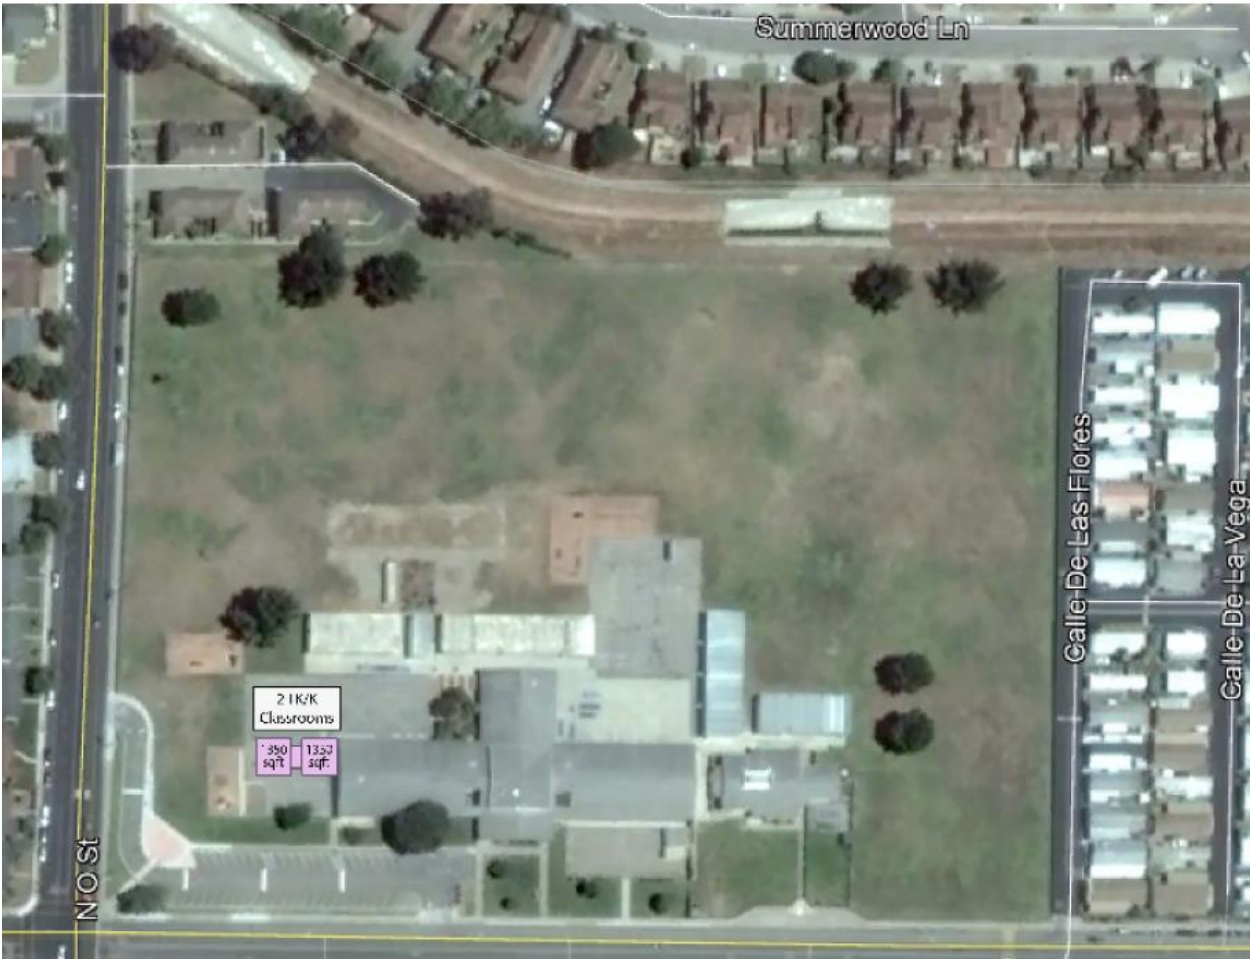

C. CLARENCE RUTH ELEMENTARY SCHOOL

Clarence Ruth Elementary School (Clarence Ruth) is located at 501 North West Street. The school occupies 11 acres and is bounded by residential development on the northern, western, and southern sides. The school was originally built in 1960 and modernized in 2004. Clarence Ruth has a total of 19 permanent classrooms and 19 portable classrooms.

It is anticipated that the proposed classrooms be located in the front of campus and to the west of and approximately in line with the existing kindergarten classrooms on the campus. A new drop off and pick up will need to be configured off North W Street to the south of the proposed placement of the new TK classrooms. This drop off and pick up will be shared by TK

and K students. The current playground will be used and shared with the kindergarten students. The goal will be to create and expand a TK/K village within the school that promotes propinquity, teacher interaction, parent access and shared support spaces for the benefit of TK/K students. The addition of the two permanent TK classrooms to the site will also assist in meeting the District’s adopted educational specification for elementary schools at the site as well as provide the necessary space to accommodate the anticipated increase in TK enrollment.

Figure 4 – Clarence Ruth Elementary School Proposed TK/K Facilities



D. ARTHUR HAPGOOD ELEMENTARY SCHOOL

Arthur Hapgood Elementary School (Hapgood) is located at 324 South A Street. The school occupies approximately 13.4 acres and is bounded by residential development on all sides. The school was originally built in 1952 and modernized in 2005. Hapgood Elementary has a total of 32 permanent classrooms and four portable classrooms.

Likewise, it is proposed that two TK classrooms be added to Arthur Hapgood Elementary. As with Clarence Ruth Elementary, this will assist the site in meeting the District’s adopted educational specification for permanent classrooms at the site as well as support the current enrollment and the need for Title 5-compliant TK classrooms. The proposed TK classrooms

for Arthur Hapgood Elementary School may be placed in the southwest portion of the school, parallel to the existing kindergarten classrooms. This location will locate all early childhood students in a common area with a shared playground creating an early childhood education center for the school. A new drop off and pick up area will need to be constructed near South A Street to accommodate both TK and K students and parents.

The addition of the TK classrooms at this site may also have the added benefit of strengthening the Dual Language Immersion program and better prepare students to be fully bilingual in English and Spanish if the program is expanded to include the TK students.

Figure 5 – Arthur Hapgood Elementary School Proposed TK/K Facilities



Summary Timeline & Schedule

At this time, the District is proceeding with the design of the two kindergarten classroom and the necessary site development work surrounding these new facilities. A Request for Proposals for a project architect was issued in January 2022, responses reviewed in early February 2020, and the Board of Trustees approved of a proposal at the March 8, 2022, meeting. The selected architect, 19six Architects, has begun schematic design of the project.

The construction schedule and academic schedule may require that both new and old portions of the campus be in operation simultaneously. Confirming that existing site utilities have adequate capacity for this simultaneous use will be a critical component of achieving a successful project. Teams are encouraged to engage with the architect of record and Civil Engineering consultants early in the process in this regard. The schedule depicted below is

based on the District’s fiscal year calendar, in which Q1 of FY2022 effectively begins July 1, 2021, and Q4 of FY2022 effectively ends June 30, 2022.

New Kindergarten Classrooms Construction Project

- **Board meeting to approve Architect contract:** March 8, 2022
- **Board meeting to approve LLB Contractor:** May 10, 2022
- **Submittal to DSA:** July 2022
- **DSA Approval:** November 2023
- **Start Construction:** January 2023
- **End Construction:** July 2023

Approved Project Budget

The total “all-in” (construction and soft costs combined) budget for the projects is \$8,601,234 estimated in current dollars (including contingencies, and both hard and soft costs), including demolition and site work. The budget in Figure 6 is inclusive of all hard costs, including general conditions and requirements, contractor fees, and overhead. Soft costs are also included, which include design fees, furniture and equipment, consulting services, testing and inspection services, agency approval fees, etc. Additional improvements may be added based on available funding sources.

A Program Reserve has been established for the combined projects to deal with unplanned and required improvements and escalations in construction costs.

Figure 6 – Adopted All-in Project Budget

Project Budget	
Filmore ES	
New Modular TK/Kindergarten Classrooms	\$ 2,202,494
La Canada ES	
New Modular TK/Kindergarten Classrooms	\$ 2,116,565
Clarence Ruth ES	
New Modular TK/Kindergarten Classrooms	\$ 2,141,840
Arthur Hapgood ES	
New Modular TK/Kindergarten Classrooms	\$ 2,140,335
Total - Project Costs	\$ 8,601,234

APPENDIX B
Form of Agreement

See Attached:

Site Lease
Facilities Lease

APPENDIX C-1

NON-COLLUSION DECLARATION
(Public Contract Code Section 7106)

The undersigned declares:

I am the _____ of _____, the party making the foregoing
[Title] [Name of Firm]
bid/proposal.

The bid/proposal is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation. The bid/proposal is genuine and not collusive or sham. The bidder/proposer has not directly or indirectly induced or solicited any other bidder/proposer to put in a false or sham bid. The bidder/proposer has not directly or indirectly colluded, conspired, connived, or agreed with any bidder/proposer or anyone else to put in a sham bid/proposal, or to refrain from bidding/proposing. The bidder/proposer has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid/proposal price of the bidder/proposer or any other bidder/proposer, or to fix any overhead, profit, or cost element of the bid/proposal price, or of that of any other bidder/proposer. All statements contained in the bid/proposal are true. The bidder/proposer has not, directly or indirectly, submitted his or her bid/proposal price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, to any corporation, partnership, company, association, organization, bid depository, or to any member or agent thereof, to effectuate a collusive or sham bid/proposal, and has not paid, and will not pay, any person or entity for such purpose.

Any person executing this declaration on behalf of a bidder/proposer that is a corporation, partnership, joint venture, limited liability company, limited liability partnership, or any other entity, hereby represents that he or she has full power to execute, and does execute, this declaration on behalf of the bidder/proposer.

I declare under penalty of perjury under the laws of the State of California that the foregoing is true and correct and that this declaration is executed on _____,
[Date]

at _____, _____.
[City] [State]

Signature: _____

Print Name: _____

Title: _____

END OF DOCUMENT

APPENDIX C-2

**IRAN CONTRACTING ACT CERTIFICATION
(Public Contract Code Sections 2202-2208)**

Prior to bidding on or submitting a proposal for a contract for goods or services of \$1,000,000 or more, the bidder/proposer must submit this certification pursuant to Public Contract Code section 2204.

The bidder/proposer must complete **ONLY ONE** of the following two options. To complete OPTION 1, check the corresponding box **and** complete the certification below. To complete OPTION 2, check the corresponding box, complete the certification below, and attach documentation demonstrating the exemption approval.

OPTION 1. Bidder/Proposer is not on the current list of persons engaged in investment activities in Iran created by the California Department of General Services ("DGS") pursuant to Public Contract Code section 2203(b), and we are not a financial institution extending twenty million dollars (\$20,000,000) or more in credit to another person, for 45 days or more, if that other person will use the credit to provide goods or services in the energy sector in Iran and is identified on the current list of persons engaged in investment activities in Iran created by DGS.

OPTION 2. Bidder/Proposer has received a written exemption from the certification requirement pursuant to Public Contract Code sections 2203(c) and (d). *A copy of the written documentation demonstrating the exemption approval is included with our bid/proposal.*

CERTIFICATION:

I, the official named below, CERTIFY UNDER PENALTY OF PERJURY, that I am duly authorized to legally bind the bidder/proposer to the OPTION selected above. This certification is made under the laws of the State of California.

<i>Vendor Name/Financial Institution (Printed)</i>	<i>Federal ID Number (or n/a)</i>
<i>By (Authorized Signature)</i>	
<i>Printed Name and Title of Person Signing</i>	<i>Date Executed</i>

END OF DOCUMENT

APPENDIX C-3

**Allowable General Condition Costs
Construction Phase Scope Detail**

Project (On Site Jobsite Staff)		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Operations Manager		X		
2	Project Manager		X		
3	Project Superintendent		X		
4	Project Engineer		X		
5	Home Office Engineer		X		
6	Scheduling Engineer		X		
7	Field Engineer		X		
8	Draftsman/Detailer		X		
9	Record Drawings		X		
10	Field Accountant		X		
11	Time Keeper/Checker		X		
12	Secretarial/Clerk Typist		X		
13	Independent Surveyor	X			
14	Safety &. E.E.O. officer		X		
15	Runner/Water Boy		X		
16	Vacation Time/Job Site Staff		X		
17	Sick Leave/Job Site Staff		X		
18	Bonuses/Job Site Staff			X	
19	Quality Control Program		X		
20	Qualified SWPPP Practitioner (QSP)	X			
21	SWPPP Creation, Approval, Notifications	X			

Temporary Utilities		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Telephone Installation		X		
2	Telephone Monthly Charges		X		
3	Elect Power Installation	X			
4	Elect Power Distribution - Wiring/Spider boxes/ Lighting for construction	X			
5	Elect Power Monthly Charges				X
6	Water Service for construction	X			
7	Heating & Cooling Costs for construction	X			
8	Light Bulbs & Misc. Supplies for construction	X			
9	Clean-Up-Periodical	X			
10	Clean-Up-Final	X			
11	Dump Permits and Fees	X			
12	Recycling/Trash Dumpster Removal/Hauling	X			
13	Flagger/Traffic Control	X			
14	Dust Control	X			
15	Temporary Road and Maintenance if	X			
16	Trash Chute & Hopper (if applicable)	X			

Direct Job Costs		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Wages of Construction Labor	X			
2	Labor/Fringe Benefits & Burden	X			
3	Subcontract Costs	X			
4	Material & Equipment/Included		X		
	a. Contractor Owned Equip, trucks		X		
	b. Small Tools - Purchase		X		
	c. Small Tools - Rental		X		
5	Warranty Work & Coordination			X	

Temporary Facilities		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Office Trailer including shared office for IOR & CM (office must include lockable door, 2 desks, 2 chairs, 1 file cabinet, and Wi-Fi connection)		X		
2	Storage Trailer & Tool Shed Rental		X		
3	Office Furniture/Equip/computers		X		
4	Xerox Copies/Misc Printing		X		
5	Postage/UPS/FedEx		X		
6	Project Photographs		X		
7	Temporary Toilets		X		
8	Project Sign		X		
9	Temporary Fencing/Enclosures		X		
10	Covered Walkways if required	X			
11	Barricades	X			
12	Temporary Stairs	X			
13	Opening Protection	X			
14	Safety Railing & Nets	X			
15	Drinking Water/Cooler/Cup		X		
16	Safety/First Aid Supplies		X		
17	Fire Fighting Equipment		X		
18	Security Guards		X		
19	Watchman Service		X		
20	Phone/fax lines, cell phones, WiFi		X		
21	Temporary "Swing space" portables to house teachers and students as required for phasing				X
22	Utility connections and civil work needed for temporary "swing space" portables as required for phasing	X			

Miscellaneous Project Costs		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Performance and Payment Bonds				
2	Developer-provided insurance				
3	Printing - Drwgs & Specs (Max of 15 sets)				X
4	Initial Soils Investigation				X
5	Testing and Inspection				X
6	Maintenance After Occupancy				X
7	Facility Operator/Training	X			
8	Fees				X

Hoisting		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Hoist & Tower Rental	X			
2	Hoist Landing & Fronts	X			
3	Hoist Operator	X			
4	Hoist Safety Inspections	X			
5	Hoist Material Skips/Hoppers	X			
6	Erect & Dismantle Hoists	X			
7	Crane Rental	X			
8	Crane Operators	X			
9	Crane Safety Inspections	X			
10	Erect & Dismantle Crane	X			
11	Fuel, Repairs, Maintenance	X			
12	Crane Raising/Jumping Costs	X			
13	Safety Inspections	X			
14	Forklift Rental	X			
15	Forklift Operator	X			
16	Forklift Safety Inspections	X			
17	Fuel, Repairs, Maintenance	X			

Contractor's Main Office Staff		Direct Cost of the Work	General Conditions	Overhead and Profit	Paid by District
1	Corporate Executives			X	
2	Principal in Charge			X	
3	Estimating Cost Engineering			X	
4	Value Engineering			X	
5	Scheduling			X	
6	Drafting and Detailing			X	
7	Purchasing & Contracts			X	
8	Accounting & Bookkeeping			X	
9	Safety & E.E.O Officer			X	
10	Secretarial			X	
11	Clerk/Typist			X	
12	Computer/Data Processing			X	
13	Legal (General Services/Pertaining to			X	
14	Travel & Subsistence			X	
15	Fringe Benefits & Burden			X	
16	Vacation Time/Main Office			X	
17	Bonuses/Main Office			X	
General Conditions Total Cost transfer to Fee Proposal			\$		

APPENDIX C-4

FEDERAL DEBARMENT CERTIFICATION

1. Bidder certifies to the best of its knowledge and belief, that it and its principals:
 - a. Are not presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded by any Federal department or Board;
 - b. Have not within a three-year period preceding this bid been convicted of or had a civil judgment rendered against them for commission of fraud or a criminal offense in connection with obtaining, attempting to obtain, or performing a public (Federal, State or local) transaction or contract under a public transaction; violation of Federal or State antitrust statutes or commission of embezzlement, theft, forgery, bribery, falsification or destruction of records, making false statements, or receiving stolen property;
 - c. Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of the offenses enumerated in paragraph (1)(b) of this certification; and
 - d. Have not within a three-year period preceding this application/proposal had one or more public transactions (Federal, State or local) terminated for cause or default.

2. Where Bidder is unable to certify to any of the statements in this certification, Bidder shall attach an explanation to this certification.

3. Bidder agrees to include the following certification in all subcontracts, for all lower tiers:

"Debarment and Suspension Certification – By submission of its proposal, the contractor (or vendor, or consultant, depending on the transaction) certifies to the best of its knowledge and belief that it and its principals are not presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from covered transactions by any Federal department or agency in accordance with 2 CFR 200.213 and 2 CFR 180."

Date: _____

Name of Developer: _____

Signature: _____

Print Name: _____

Title: _____

APPENDIX C-5

BYRD ANTI-LOBBYING CERTIFICATION

**Applicable to Grants, Subgrants, Cooperative Agreements, and Contracts
Exceeding \$100,000 in Federal Funds**

Submission of this certification is a prerequisite for making or entering into this transaction and is imposed by section 1352, Title 31, U.S. Code. This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Any person who fails to file the required certification shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.

The undersigned certifies, to the best of their knowledge and belief, that:

- (1) No Federal appropriated funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with the awarding of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment or modification of any Federal contract, grant, loan, or cooperative agreement.
- (2) If any funds other than Federal appropriated funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form-LLL, "Disclosure of Lobbying Activities," in accordance with its instructions.
- (3) The undersigned shall require that the language of this certification be included in the award documents of all sub-awards at all tiers (including subcontracts, sub-grants, and contracts under grants, loans, and cooperative agreements) and that all sub- recipients shall certify and disclose accordingly.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by section 1352, title 31, United States Code. Any person who fails to file the required certification shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.

Contractor

Address

Certified by: (type or print)

Title

Signature

Date

Disclosure of Lobbying Activities

Approved by OMB
0348-004

Complete this form to disclose lobbying activities pursuant to 31 U.S.C. 1352
(See following page for public burden disclosure)

1. Type of Federal Action: <input type="checkbox"/> contract <input type="checkbox"/> grant <input type="checkbox"/> cooperative agreement loan <input type="checkbox"/> loan guarantee <input type="checkbox"/> loan insurance	2. Status of Federal Action: <input type="checkbox"/> proposal/offer/application <input type="checkbox"/> initial award <input type="checkbox"/> post-award	3. Report Type: <input type="checkbox"/> initial filing <input type="checkbox"/> material change For material change only: Year _____ quarter ____ Date of last report _____
4. Name and Address of Reporting Entity: _____ Prime _____ Subawardee Tier _____, if known: Congressional District, if known:	5. If Reporting Entity in No. 4 is Subawardee, Enter Name and Address of Prime: Congressional District, if known:	
6. Federal Department/Agency:	7. Federal Program Name/Description: CFDA Number, if applicable: _____	
8. Federal Action Number, if known:	9. Award Amount, if known: \$	
10a. Name and Address of Lobbying Registrant (if individual, last name, first name, MI):	10b. Individuals Performing Services (including address if different from No. 10a) (last name, first name, MI):	
11. Information requested through this form is authorized by title 31 U.S.C. section 1352. This disclosure of lobbying activities is a material representation of fact upon which reliance was placed by the tier above when this transaction was made or entered into. This disclosure is required pursuant to 31 U.S.C. 1352. This information will be reported to the Congress semi-annually and will be available for public inspection. Any person who fails to file the required disclosure shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.	Signature: _____ Print Name: _____ Title: _____ Telephone No.: _____ Date: ____	
Federal Use Only	Authorized for Local Reproduction Standard Form - LLL (Rev. 7-97)	

INSTRUCTIONS FOR COMPLETION OF SF-LLL, DISCLOSURE OF LOBBYING ACTIVITIES

This disclosure form shall be completed by the reporting entity, whether subawardee or prime Federal recipient, at the initiation or receipt of a covered Federal action, or a material change to a previous filing, pursuant to Title 31, U.S.C. section 1352. The filing of a form is required for each payment or agreement to make payment to any lobbying entity for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with a covered Federal action. Complete all items that apply for both the initial filing and material change report. Refer to the implementing guidance published by the Office of Management and Budget for additional information.

1. Identify the type of covered Federal action for which lobbying activity is and/or has been secured to influence the outcome of a covered Federal action.
2. Identify the status of the covered Federal action.
3. Identify the appropriate classification of this report. If this is a follow up report caused by a material change to the information previously reported, enter the year and quarter in which the change occurred. Enter the date of the last previously submitted report by this reporting entity for this covered Federal action.
4. Enter the full name, address, city, State and zip code of the reporting entity. Include Congressional District, if known. Check the appropriate classification of the reporting entity that designates if it is, or expects to be, a prime or subawardee recipient. Identify the tier of the subawardee, e.g., the first subawardee of the prime is the 1st tier. Subawards include but are not limited to subcontracts, subgrants and contract awards under grants.
5. If the organization filing the report in item 4 checks "Subawardee," then enter the full name, address, city, State and zip code of the prime Federal recipient. Include Congressional District, if known.
6. Enter the name of the federal agency making the award or loan commitment. Include at least one organizational level below agency name, if known. For example, Department of Transportation, United States Coast Guard.
7. Enter the Federal program name or description for the covered Federal action (item 1). If known, enter the full Catalog of Federal Domestic Assistance (CFDA) number for grants, cooperative agreements, loans, and loan commitments.
8. Enter the most appropriate Federal identifying number available for the Federal action identified in item 1 (e.g., Request for Proposal (RFP) number; Invitations for Bid (IFB) number; grant announcement number; the contract, grant, or loan award number; the application/proposal control number assigned by the Federal agency). Included prefixes, e.g., "RFP-DE-90-001."
9. For a covered Federal action where there has been an award or loan commitment by the Federal agency, enter the Federal amount of the award/loan commitment for the prime entity identified in item 4 or 5.
10. (a) Enter the full name, address, city, State and zip code of the lobbying registrant under the Lobbying Disclosure Act of 1995 engaged by the reporting entity identified in item 4 to influence the covered Federal action.

(b) Enter the full names of the individual(s) performing services, and include full address if different from 10(a). Enter Last Name, First Name, and Middle Initial (MI).
11. The certifying official shall sign and date the form, print his/her name, title, and telephone number.

According to the Paperwork Reduction Act, as amended, no persons are required to respond to a collection of information unless it displays a valid OMB control Number. The valid OMB control number for this information collection is OMB No. 0348-0046. Public reporting burden for this collection of information is estimated to average 10 minutes per response, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding the burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to the Office of Management and Budget, Paperwork Reduction Project (0348-0046), Washington, DC 20503.

END OF DOCUMENT
